

# District 5 ITS Project Update

**Michael W. Smith**  
**ITS Systems Manager**

# DASH I (414715-1-52-01)

## □ I-4/I-95 from SR 472 to SR 40

### ■ CONTRACTOR:

□ MASTEC

### ■ STATUS:

□ System Final Acceptance March 12, 2007

### ■ # OF DEVICES:

□ 24 CCTV, 44 DMS (6 Interstate & 38 Trailblazer), and 18 VDS



# DASH II (414723-1 & 414758-1)

## □ I-95 from SR 40 to US 1

### ■ CONTRACTOR:

□ FIE

### ■ STATUS:

□ System Final Acceptance Feb 5, 2007

### ■ # of DEVICES:

□ 11 CCTV, 11 DMS (1 Interstate & 10 Trailblazer), and 5 VDS (2 Loops, 3 Radar Detectors).



# DASH III (414719-1 & 414759-1)

## □ I-95 from SR 514 to SR 400

- **CONTRACTOR:**
  - TCD
- **STATUS:**
  - Under Construction;  
Approx 60% Complete;  
Conduit on I-95 Completed
- **# OF DEVICES:**
  - 125 CCTV, 96 DMS, 81 Radar Detectors, 23 Loop Detectors
- **EST. DATE OF CONSTRUCTION COMPLETION:**
  - January 2008



# RTMC Video Wall and Consoles Project (416393-1)

- VIDEO WALL INCLUDES: Modular DLP Projection and Displays 80 Individual Video Streams
  - STATUS: Final Accepted December 2006



# Flagler County (416391-1)

- I-95 from US 1 to US 1
  - **STATUS:**
    - Design Build Project
    - Short listed Feb 12
    - Award Anticipated Apr 30
    - NTP Anticipated June 26
  - **EST. # OF DEVICES:**
    - 14 CCTV (2 mi spacing), 2 DMS, 14 detector sites
  - **EST. DATE OF COMPLETE CONSTRUCTION:**
    - August 2008




# 420653-1

□ I-4 From US 27 to Osceola County Line

□ Design Build

- **STATUS:**
  - RFP Under Development
  - SEMP Ready For FHWA Review
- **EST. DATE FOR BID:**
  - January 2008
- **EST. DATE FOR NTP:**
  - May 2008

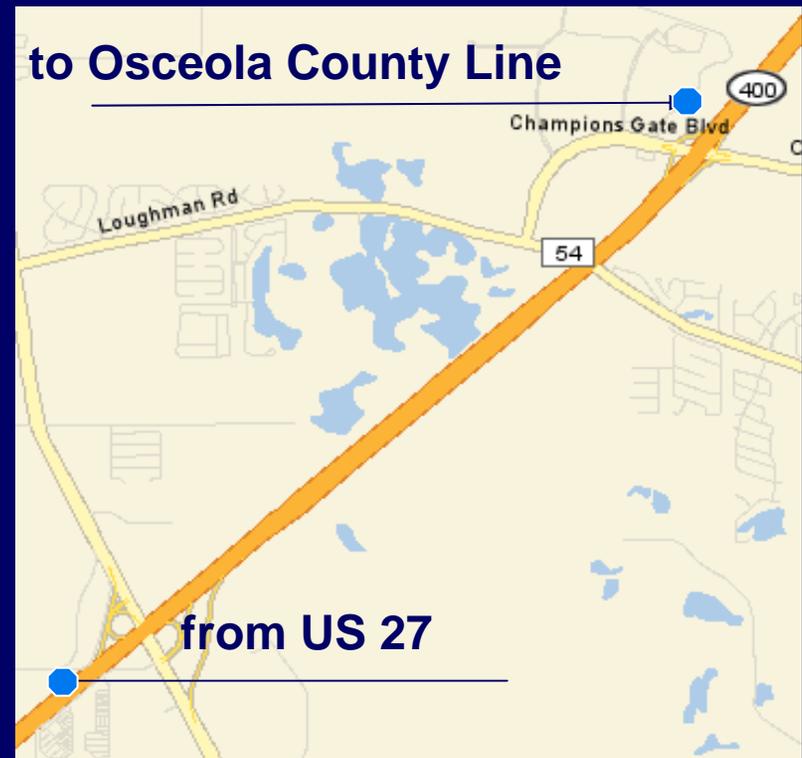

# SunGuide Orlando RTMC

- ❑ SunGuide For Volusia County
- ❑ DASH I & DASH II
  - **INCLUDES:**
    - ❑ Integration of SunGuide and DASH Field Equipment
  - **STATUS:**
    - ❑ Operational



# Questions?

**Michael W. Smith**

**FDOT District 5**

**(386) 943-5360**

**[MichaelW.Smith@dot.state.fl.us](mailto:MichaelW.Smith@dot.state.fl.us)**

