

CR 490A Halls River Road | Bridge Replacement

CONSTRUCTION UPDATE

Milestone	Actual	Forecast
Start Construction – Begin Phase I	1/9/2017	
Begin Phase II – Construct North Side	1/26/2017	
Begin Northern Substructure (Piles)	2/15/2017	
Begin Northern Pile Caps	3/10/2017	
Pour Phase II Deck		5/31/2017
Begin Phase III – Construct South Side		6/21/2017
Project Completion		12/8/2017




% Time:	31%
% Money	32%
Original Contract \$	\$6,015,645.00
Original Contract Time	310 Days

CR 490A Halls River Road| Bridge Replacement




Halls River Road (CR 490A) Bridge Replacement
FPN: 430021-1


Construction
Phasing




Existing Condition -
Begin Construction
January 2017




Build New Westbound Bridge,
Temporary Signal, One Lane of Traffic
6 Months approx.



Eastbound Construction, Two Lanes of Traffic,
Move Traffic to new Westbound lanes, Build
Eastbound Lanes
5 Months approx.



Eastbound Construction, Two Lanes of Traffic,
Move Traffic to new Eastbound lanes, Build
Pedestrian Barriers on Westbound Bridge
2 Months



Final (Construction Complete)



Florida Department of Transportation

T7386 | 430021-1-52-01

CR 490A Halls River Road| Bridge Replacement



CR 490A Halls River Road | Bridge Replacement



Bridge Demolition Prep Work

CR 490A Halls River Road | Bridge Replacement



**Bridge
Demolition -
Cutting Existing
Pile Caps**

CR 490A Halls River Road | Bridge Replacement

**SWFWMD
Permit only
allowed 41
NTUs above
background in
Mixing Zone**



CR 490A Halls River Road | Bridge Replacement

**Driving
18" CFRP
Concrete
Pile**



CR 490A Halls River Road | Bridge Replacement

**UNDERGROUND
FISSURE OPENED
FROM PILE
DRIVING**



CR 490A Halls River Road | Bridge Replacement



CR 490A Halls River Road | Bridge Replacement




CR 490A Halls River Road | Bridge Replacement



Maine:
The Un-
Shine
State!!!

CR 490A Halls River Road | Bridge Replacement

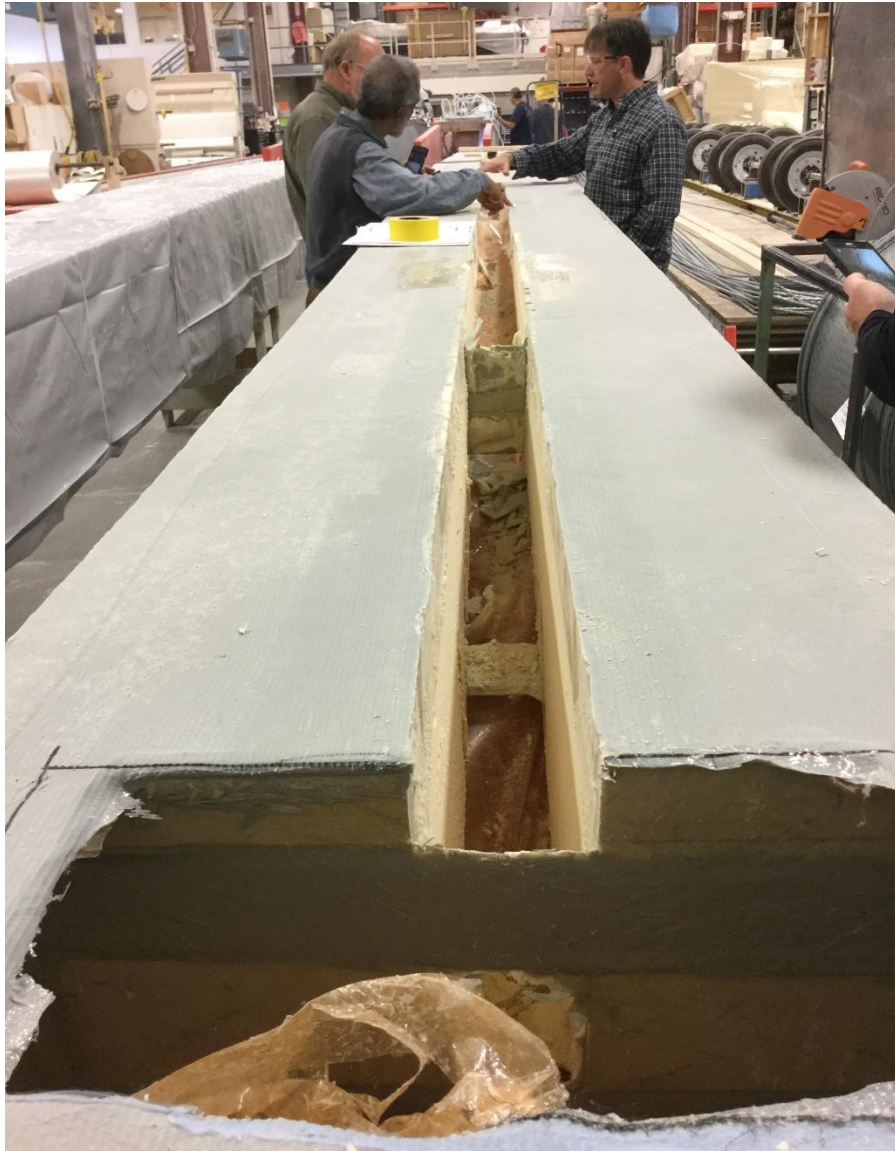

CR 490A Halls River Road | Bridge Replacement

