

Consultant Acquisition Plan

**Florida Department of Transportation
District 5**

This meeting and project are being conducted without regard to race, color, national origin, age, sex, religion, disability or family status. Persons wishing to express their concerns relative to FDOT compliance with Title VI may do so by contacting:

Jennifer Smith
FDOT District Five Title VI Coordinator
719 South Woodland Boulevard
Deland, Florida 32720
386-943-5367
Jennifer.smith2@dot.state.fl.us

Jacqueline Paramore
State Title VI Coordinator
605 Suwannee Street, Mail Station 65
Tallahassee, FL 32399-0450
850-414-4753
Jacqueline.paramore@dot.state.fl.us

All inquiries or complaints will be handled according to FDOT procedure and in a prompt and courteous manner.

Agenda

- Opening Remarks
- Construction, Engineering and Inspection
- Materials and Research
- District Maintenance
- Traffic Operations
- Disadvantaged Business Enterprise/Small Business
- 30 minute “Networking Break”
- Rejoin Remarks
- Design including Design Build
- Planning and Environmental Management
- Right-of-Way
- Closing Remarks



Construction

CEI Contracts

John Tyler, DCE

Amy Scales, Assistant DCE

Alida Schmitt, District CEI Manager

Denise Nazario, CEI Contract Administrator

CEI Work Program

CEI Group		Advertising Date	Design Build	2016												2017						
				Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug
151	Williams																					
	407143-4	2/1/2016		Sand Lake Road from West of International Drive to Universal Boulevard.																		
	407143-5			Sand Lake Road from Universal Boulevard to West of John Young Parkway																		
	407143-6			John Young Pkwy at Sand Lake Road Overpass																		
152	Bauknecht																					
	238275-7 (6)	6/20/2016	X	SR429/46 (Wekiva Pkwy)(section 6)																		
AW 10	Nazario																					
	237984-2-62-14	6/20/2016		Continuing Services, provide CEI Support district wide																		
154	Coleman																					
	237984-2-62-15	7/11/2016		Continuing Services CEI to provide Inspection Staff for Orlando Construction																		
155	Jaggers																					
	238319-2	10/10/2016	X	SR 19 over Little Lake Harris Br. 110026																		
156	Navarro																					
	437100-1	11/7/2016		Regional Traffic Management Center (RTMC)																		
157	Jaggers																					
	238275-2 (3B)	1/16/2017		SR 46 Wekiva Section 3B																		
	238275-3 (3A)			SR 46 Wekiva Section 3A																		
158	Glenn Raney																					
	435056-1	2/13/2017		I-4 (SR 400) at SR 472 (Lighting																		
	435053-1			I-4 AT US 17/92 (Lighting)																		
	435059-1			I-95 Volusia & Flagler (Lighting)																		
	436325-1			Event Management Daytona Beach (ITS)																		
	436323-1			ST Johns River Br. Securit																		
159	Martens																					
	426905-3	2/6/2017		I-95 INT @ Ellis Rd. (Interchange)																		
	435054-1			I-95 (SR 9) at Wickham(Lighting)																		

All selections will be by Expanded Letters.

Projects Highlights

GROUP 151, Orange County


407143-4 Sand Lake Road from West of International Drive to Universal Boulevard.

407143-5 Sand Lake Road from Universal Boulevard to West of John Young Parkway.

407143-6 John Young Pkwy at Sand Lake Road Overpass.

Construction Cost: **\$71.45 Million**

CEI Advertise: **February 01, 2016**

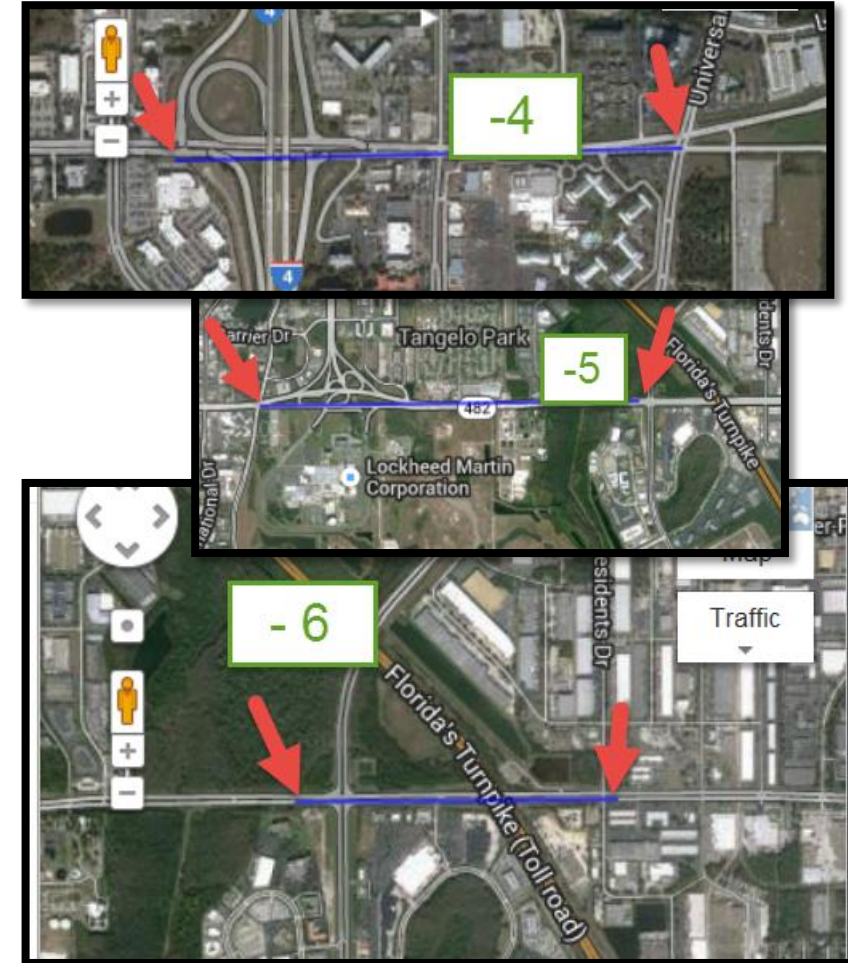

Projects Highlights

Areawide 10 : 237984-2-62-14

Continuing Services to provide Area wide CEI Support.

CEI Advertise: **June 20, 2016**

CEI Group 154 (Hybrid): 237984-2-62-15

Continuing Services CEI to provide Inspection Staff to Orlando Construction Office.

CEI Advertise: **July 11, 2016**

Length 5 years. Amount \$5 Million.

Projects Highlights

GROUP 152, Seminole/Lake Counties (Wekiva Section 6)

238275-7-62-01 (Design Build)

From West of Old McDonald Road to East of Wekiva River Road

Construction Cost: \$215.7 Million

CEI Advertise: June 20, 2016



Florida Department of Transportation

CAP

FDOT-D5

January 26, 2016

Projects Highlights

GROUP 155, Lake County

238319-2-62-01 (Design Build)

SR 19 Over Little Lake Harris Bridge # 110026. Replace Bridge

Estimated Construction Cost: **\$44.7 Million**

CEI Advertise: **October 10, 2016**



Projects Highlights

GROUP 156, Seminole County **REGIONAL TRAFFIC** **MANAGEMENT CENTER**

437100-1-62-01

Construction Cost: **\$13.7 Million**

CEI Advertise: **Nov. 07, 2016**



Projects Highlights

GROUP 157, Lake County (Wekiva 3A/3B)

238275-2

SR 46 from W of US 441 to E of Vista View Lane (**Section 3B**)

238275-3

SR 46 from E of Vista View Lane
to E of Round Lake Road
(**Section 3A**)

Construction Cost: **\$33.2 Million**

CEI Advertise: **January 16, 2017**



Projects Highlights

GROUP 158, 5 Projects Volusia and Flagler Counties

ITS and Lighting Projects

435056-1: I-4 at 472 (Lighting)

Construction Cost: **\$1.2 Million**

435053-1: I-4 at 17/92 (Lighting)

Construction Cost: **\$1.1 Million**

435059-1: I-95, Volusia and Flagler (Lighting)

Construction Cost: **\$5.6 Million**

436325-1: Daytona Beach Event Management (ITS)

Construction Cost: **\$2.2 Million**

436323-1: St John's River Br. Security System (ITS)

Construction Cost: **\$0.7 Million**

CEI Advertise: **February 13, 2017**

Projects Highlights

GROUP 159, 2 Projects: Brevard County



426905-3: I-95 INT @ Ellis Rd /St. Johns Heritage Pkwy. (New Interchange)

Construction Cost: \$41.9 Million

435054-1: I-95 at Wickham, SR 520 and SR 524 (Lighting)

Construction Cost: \$2.3 Million

CEI Advertise: February 06, 2017

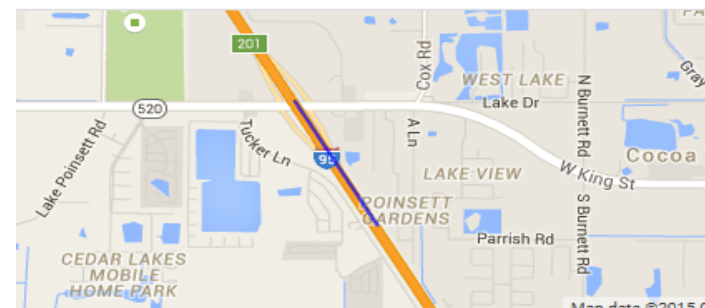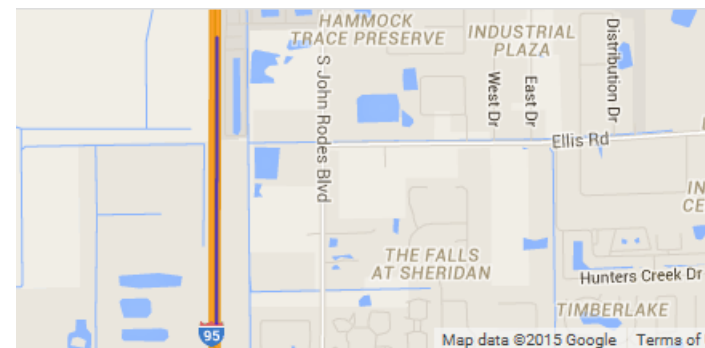


Materials & Research

Geotechnical & Material Testing & Inspection Contracts

Jack Davis, Materials Manager - Contracts

Materials Contact Info

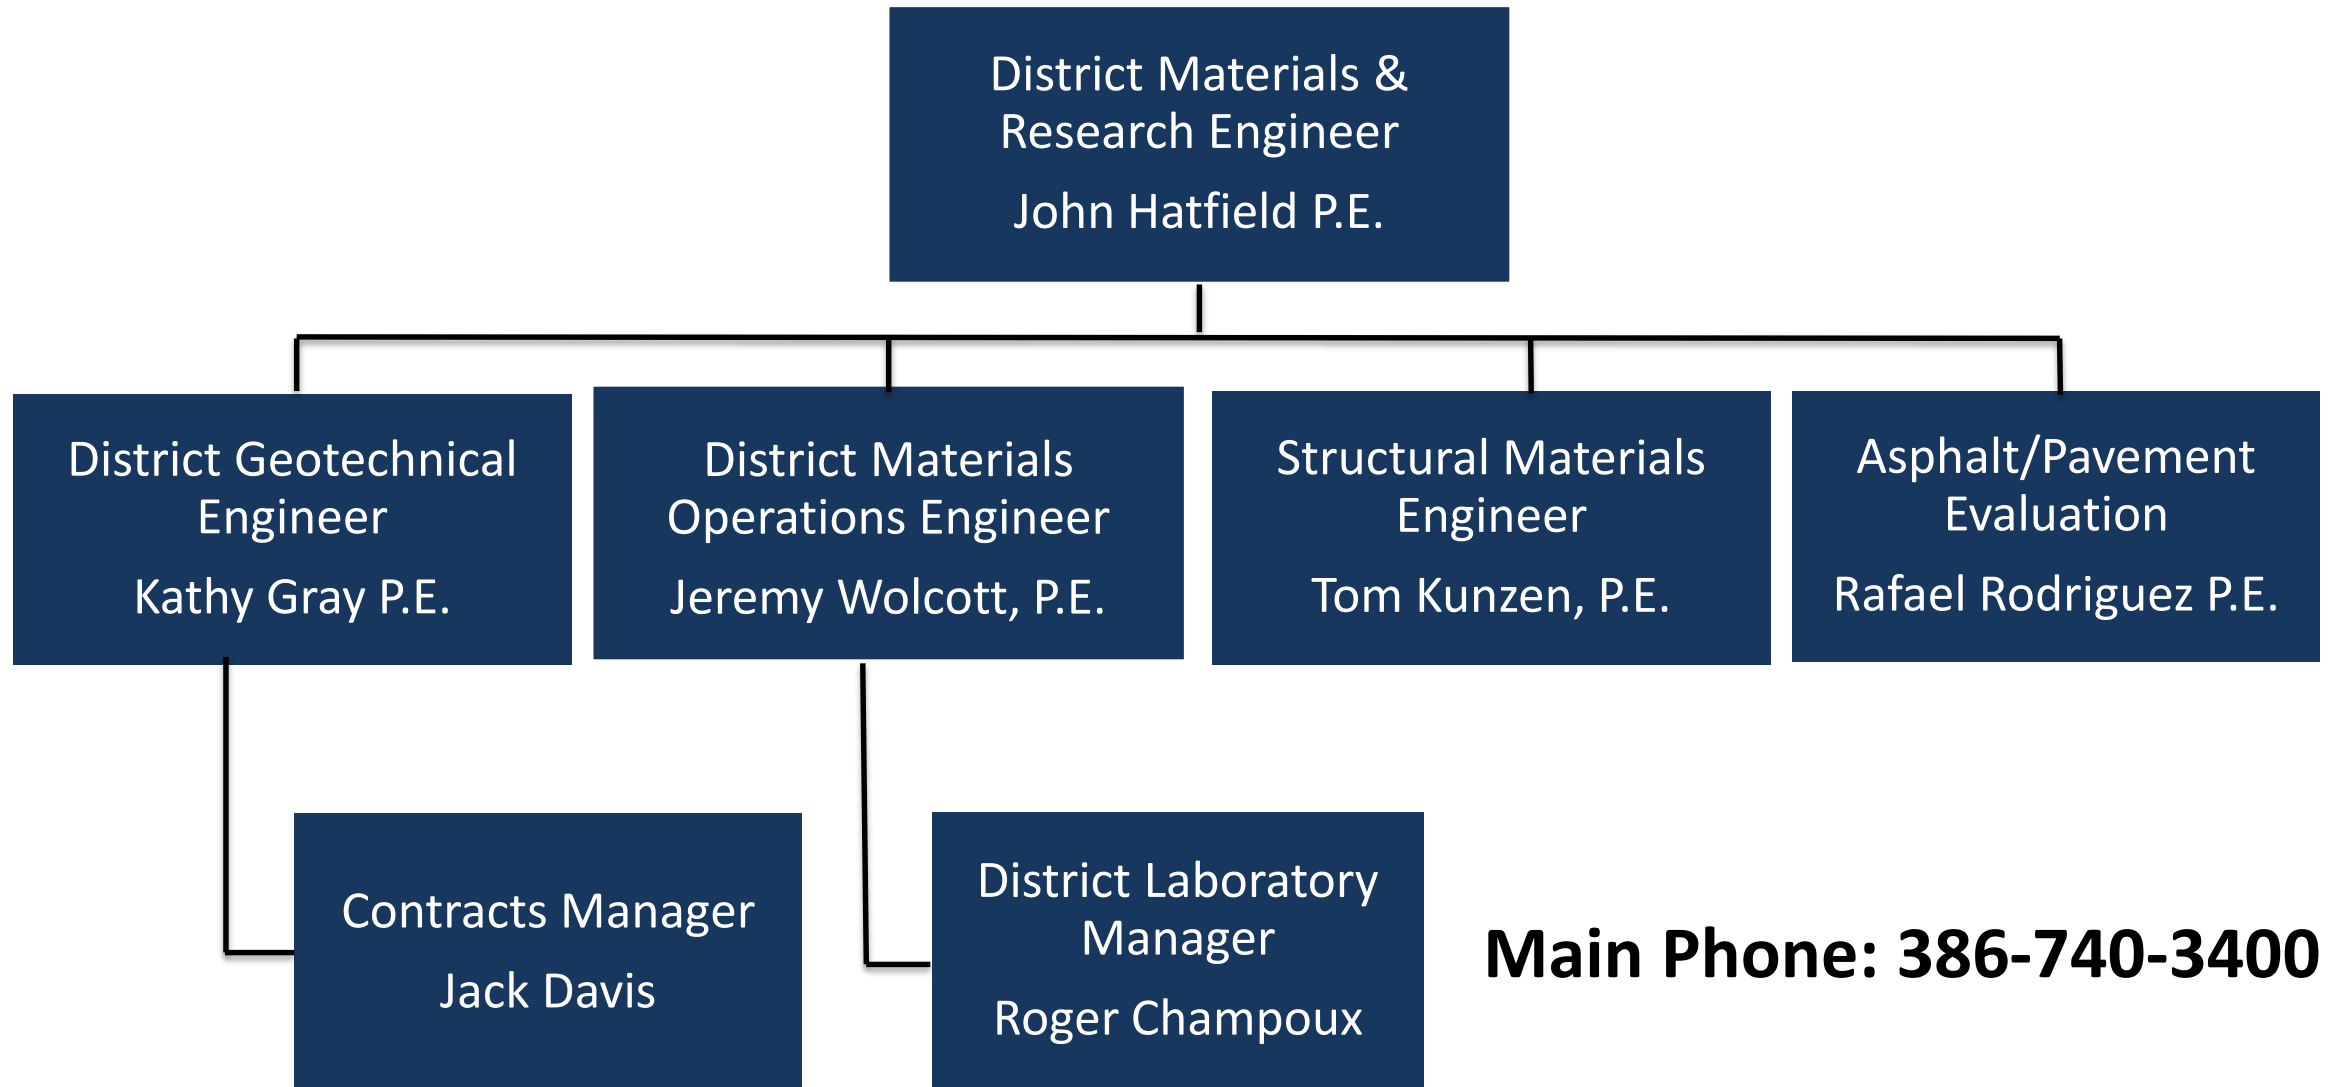

Main Phone: 386-740-3400

Materials Contracts

- **Materials & Research maintains at least two contracts at all times:**
 - **5 year/5 million Continuing Service Contracts**
 - **Qualification Groups 9.1, 9.2, 9.3, 9.4.1, 9.4.2, 10.1, 10.3**
 - **Prime consultant and multiple Sub-consultants**
 - **Existing contracts are held by:**
 - **C9570 - Elipsis Engineering & Consulting, Inc. (Expiration 4/8/2017)**
 - **C9C40 - Ardaman & Associates, Inc. (Expiration 9/22/18)**
 - **C9G78 - Page One Consultants, Inc. (Expiration 3/10/2020)**

Materials Contracts

The following services are provided:

- **Phase 32/Design Support:**
 - Geotechnical Design Support
 - Pavement Coring & Evaluation
- **Phase 62/Construction Support:**
 - Asphalt Plant Verification Technicians
 - Pre-Stress/Pre-Cast Plant Inspection
 - Dynamic Pile Testing
 - Drilled Shaft Support Program
 - Material Laboratory Testing
 - Database Entry (LIMS/MAC)
 - GIS Soil Boring Database

Materials Contracts

Upcoming Opportunities:

- Continuing Service Contract for Geotechnical & Materials Testing & Inspection
- 5 year/5 million
- Advertising March 2016
- Will cover all services and Qualification Groups (9.1, 9.2, 9.3, 9.4.1, 9.4.2, 10.1, 10.3)
- TRC Members – John Hatfield, Jeremy Wolcott, Kathy Gray

Jack Davis - Materials & Research Consultant Project Manager,
386-740-3507, Jack.Davis@dot.state.fl.us



DISTRICT MAINTENANCE

DISTRICT WIDE MISCELLANEOUS DESIGN/ DRAINAGE CONSULTANT

- **PROJECT NO. 237975-1-32-09**
- **5 YEAR CONTRACT - INITIAL BUDGET: \$500,000**
- ***RESERVED FOR SMALL BUSINESS PARTICIPATION***
- **MAJOR WORK GROUP: 3.1**
- **MINOR WORK GROUPS: 4.1, 8.1, 8.2, 8.3, 8.4, 9.1, 9.2, 9.4 & 9.5**
- **PROJECT MANAGER: Victor A. LoPiccolo**
- **ADVERTISE: March 1, 2016**
- **TRC COMMITTEE MEMBERS:**
Emily Schanker; Chris Barone; Patrick McConaghy

DISTRICT MAINTENANCE

DISTRICT WIDE MISCELLANEOUS DESIGN/ DRAINAGE CONSULTANT



Traffic Operations

Continuing Services Contracts

Traffic Operations Continuing Services Contracts

TRC Members

Rick Morrow – District Traffic Operations Engineer

Chris Cairns – Assistant District Traffic Operations Engineer

Mike Sanders – District Studies Engineer

Traffic Operations Continuing Services Contracts

Financial Projects 237987-1 & 237988-1

Two Continuing Services Contracts

Work Mix – Preliminary Engineering

- Traffic Studies
- Signal Retimings
- Minor Design
- ITS

Major Work Group – 6.1

\$525,000 Initial - \$5M Cap, 5 years

Advertise – March 2016

Execute – September 2016

Project Manager – Jackie Michalos



District Five

Construction Contract Compliance

Dennis Kirk
District Contract Compliance Manager

District 5 Contract Compliance

- Provides oversight and tracking of compliance activities
- Conducts annual contractor compliance training
- Federally Funded Project Activities
 - Review all payrolls for the prime contractor and subcontractors
 - Review DBE Commitments and Payments in EOC
 - Help Contractors locate DBEs to utilize on projects
 - Review the contractor's DBE solicitation efforts

DBE Program Objectives

- Ensure equal opportunity in contract award and administration
- Level the playing field to promote competitiveness
- Ensure FDOT's DBE program complies with applicable laws
- Ensure the integrity of certifying DBE firms
- Remove barriers to DBE participation on DOT contracts
- Enable firms to successfully compete in the marketplace



FDOT DBE Program Details

- State wide DBE goal is 9.91%
 - DBE availability is 10% on consultant projects
 - Federal project DBE commitments for Professional Services is 5.48%
 - State project DBE commitments for Professional Services is 9.55%
- Project specific DBE availability
- 49 CFR Part 26
- FHWA 1273 (Section II.10)
- FDOT Standard Specification 7-24 (Construction Contracts)

Under-Utilization Goal for DBEs & Small Businesses

- The goal of the Department's Under-utilization strategy is to encourage and promote use of Disadvantaged Business Enterprises (DBE) and Small Businesses in areas of work where they have been under-used.
- Consultants are strongly encouraged to propose a DBE or Small Business to perform services for each under-utilized work group identified in the advertisement.
- Use of under-utilized DBEs or Small Businesses for Consultant teaming is a shortlist consideration factor for projects referencing this Standard Note.

DBE/SBE Aspirational Goals for Consultants

- FDOT has established an aspiration goal of 10% DBE usage and an additional 3% non-DBE Small Business usage for the subject Project.
- Although not a contract requirement, FDOT believes that the aforementioned aspiration goal can realistically be achieved based on current availability of DBEs and small businesses.
- FDOT further believes that the 13% overall goal can be achieved through race neutral means, using standard competitive procurement processes.

FDOT Standard Specification 7-24

- Disadvantaged Business Enterprise (DBE) Affirmative Action Program Plan
- Verify access to the Equal Opportunity Compliance (EOC) System
- Bid Opportunity Reporting
- DBE Records and Reports
 - Commitments entered into EOC
 - Monthly payments entered into EOC
 - Adjust commitments as new DBE firms are added



DBE Participation Best Practices for Consultants


- Review your DBE/AA plan and **“implement your plan”**
- Consider DBE firms during your bid or proposal processes
- Document results from solicitations and requests for proposal
- Attend contract compliance workshops
- Pass along DBE availability in your sub-contractual agreements
- Contact the Department or CEI Supportive Services for assistance
- Refer DBE or potential DBE firms to the Department for assistance



BREAK

OFFICE OF DISTRICT DESIGN

Annette Brennan, District Design Engineer
Suzanne Phillips, Consultant Project Management
Jeff Cicerello, District Roadway Design Engineer
Neil Kenis – District Structure Design Engineer
Ty Garner – District Utilities Administrator
Gary Roche, Surveying & Mapping

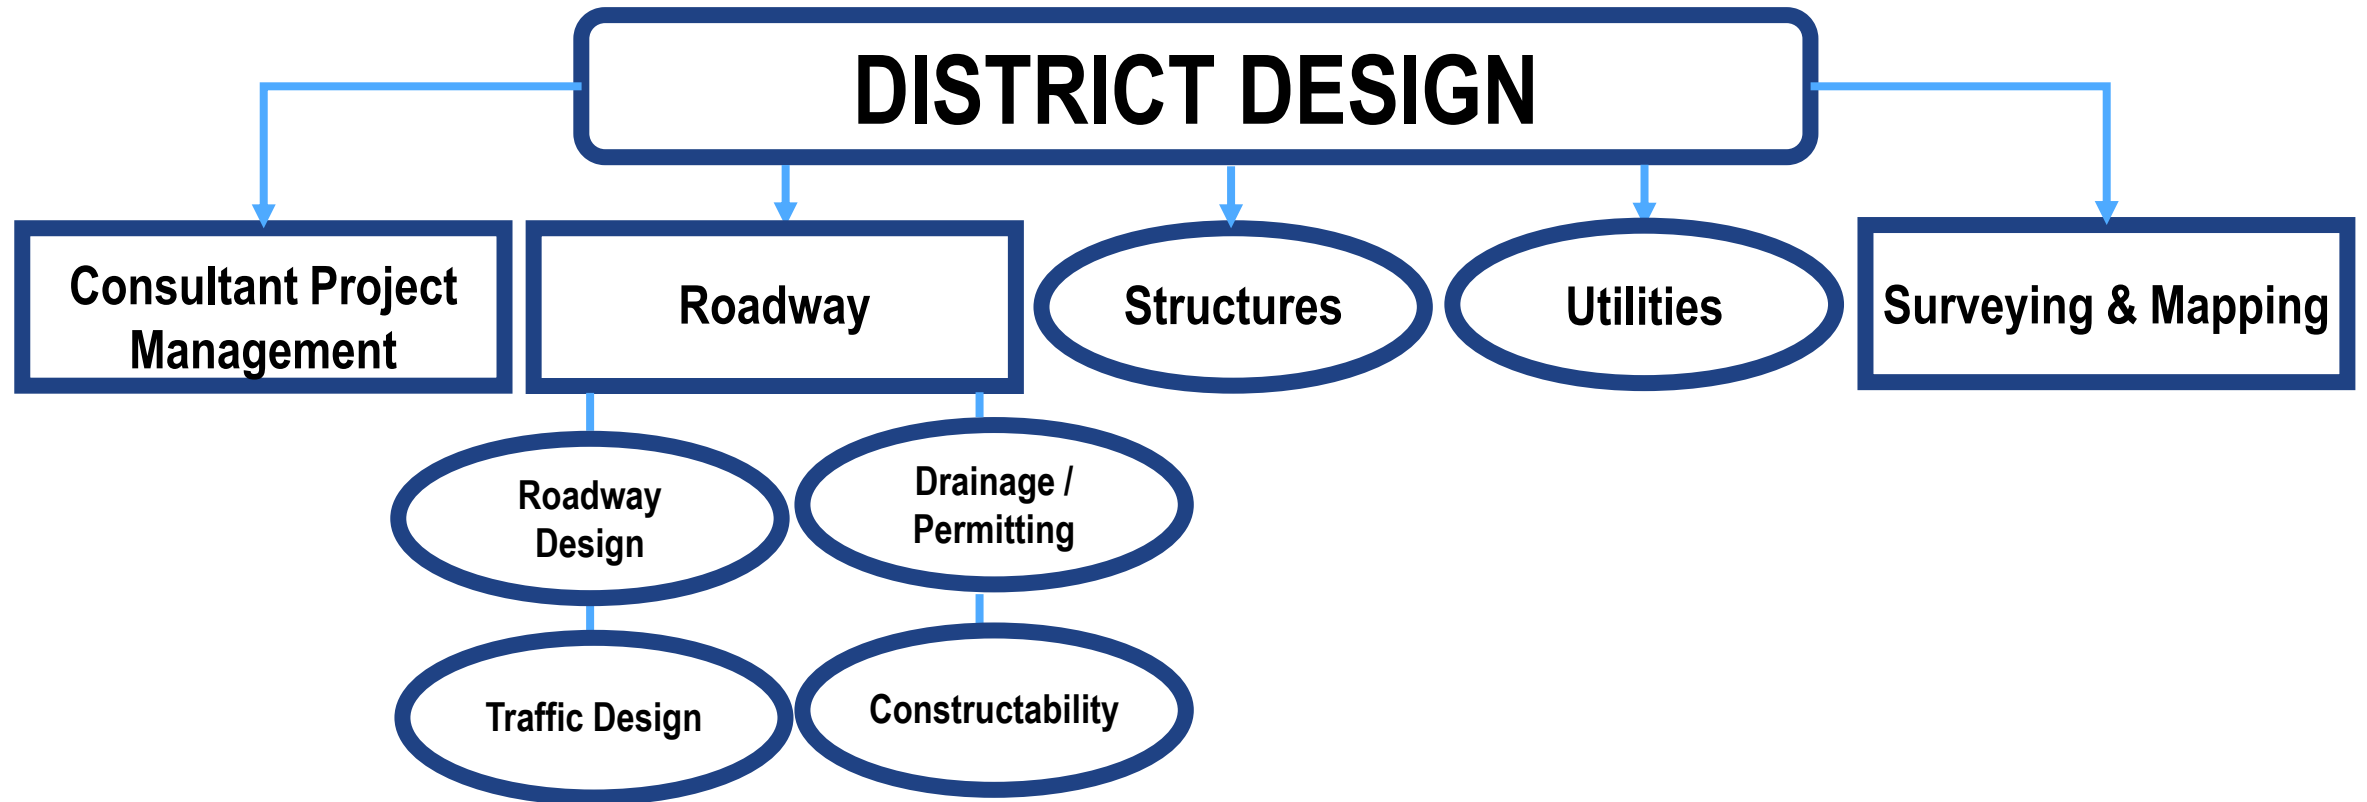

TRC

CONSULTANT PROJECT MANAGEMENT

Suzanne Phillips, PE - District Consultant Project Mgmt. Eng.

David Cooke - Project Management Supervisor

Beata Stys-Palasz, PE - Project Management Supervisor

Todd Long, PE - Project Management Supervisor

Vacant - Project Management Supervisor

TRC

CONSULTANT PROJECT MGMT TEAM

Hatem Aguib, PE
Christine Bacomo, PE
Todd Alexander, EI
Catalina Chacon, PE

Leonel Cortes, PE
Kathy Enot, EI
Matt Hassan, PE
Heather Johnstone, PE

Storm Kazmierczak, PE
Kevin Moss, PE
Taleb Shams, PE
Sarah Van Gundy

TRC

ROADWAY DESIGN TEAM

Jeff Cicerello, PE – District Roadway Design Engineer

George Borchik, PE – Roadway Engineer Supervisor

Naziru Isaac, PE – Roadway Engineer Supervisor

Hadil Jardaneh, PE

Ed Cashman, PE

TRC

TRAFFIC DESIGN TEAM

Vacant – District Traffic Design Engineer

Angela Cardona, PE

TRC

DRAINAGE / PERMITTING TEAM

Ferrell Hickson, PE – District Drainage Design Engineer

Karen Snyder, PE – Assistant District Drainage Engineer

Carol Hatfield, PE

Patrick McConaghy, PE

Casey Lyon

Efren Rivera, PE

TRC

CONSTRUCTABILITY TEAM

Ashraf Elmaghraby, PE – Roadway Engineer Supervisor
Lori Epperson – Pavement Designer

TRC

STRUCTURES TEAM

Neil Kenis, PE – District Structure Design Engineer

Chris Dabson, PE

Jonathan Jastremsky, PE

Marianne Saunders, PE

Gary Skofronick, PE

Haosu Sun, PE

Mark Trebitz, PE

TRC UTILITIES

Ty Garner – District Utilities Administrator

TRC

SURVEYING & MAPPING TEAM

Gary Roche, PSM – District Surveyor & Mapper
Scott Miller, PLS – Surveying & Mapping Supervisor
John Cheney, PLS – Surveying & Mapping Supervisor
Thomas LaCorte, PLS – Surveying & Mapping Supervisor

DESIGN PROJECT SUMMARY – FY 17

CONTRACT TYPE	NUMBER OF CONTRACTS	PROJECTS	DESIGN COST \$	DESIGN BUILD COST \$
Major	1		\$1,662,135	
Minor	7		\$6,111,000	
Minor Bundled	2	2 Contracts with 2 Projects	\$2,617,000	
SBE	4		\$2,275,000	
SBE Bundled	1	1 Contract with 2 Projects	\$895,000	
Design Build	2			\$260,396,032
DW Contracts	2		\$200,000	
TOTAL	19	22 Projects	\$13,760,135	\$260,396,032



DESIGN

MAJOR PROJECTS



Florida Department of Transportation

CAP
FDOT-D5
January 26, 2016

Design/Major **Financial Project 240200-3**

- **SR 46 (WEKIVA PKWY) FROM WEST OF CENTER RD TO INTERSTATE 4**
- Seminole County
- Work Mix – ADD LANES & RECONSTRUCT
- Work Types – 3.2
- Design Costs - \$1,662,135
- Advertisement Date – March 21, 2016
- Project Manager – Matt Hassan
- TRC Members – Suzanne Phillips,
Karen Snyder, Annette Brennan



DESIGN

MINOR PROJECTS




Florida Department of Transportation

CAP
FDOT-D5
January 26, 2016

Design/Minor


Financial Project 437338-1

- **SR 500 (US 441) FROM WEST OF SR 451 TO SR 429 CONNECTOR ROAD**
- Orange County
- Work Mix – RESURFACING
- Work Types – 3.1
- Design Costs - \$810,000
- Advertisement Date – April 4, 2016
- Project Manager – Jerald Marks
- TRC Members – Matt Hassan,
Hadil Jardaneh, George Borchik

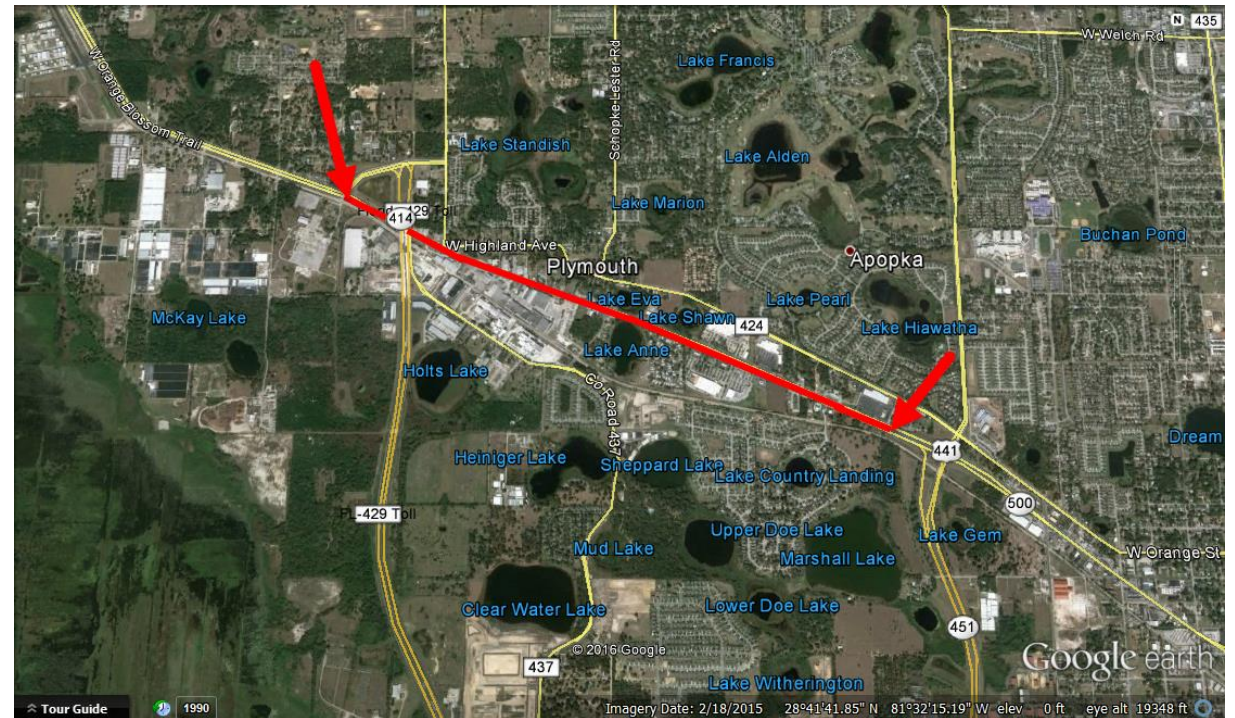

Design/Minor **Financial Project 431935-1**


- **SR 40 CORRIDOR FROM US 441 TO NE 8TH AVENUE**
- Marion County
- Work Mix – SIDEWALK
- Work Types – 3.1
- Design Costs - \$1,000,000
- Advertisement Date – Sept. 12, 2016
- Project Manager – Matt Hassan
- TRC Members – Kevin Moss,
Brenda Young, Hadil Jardaneh

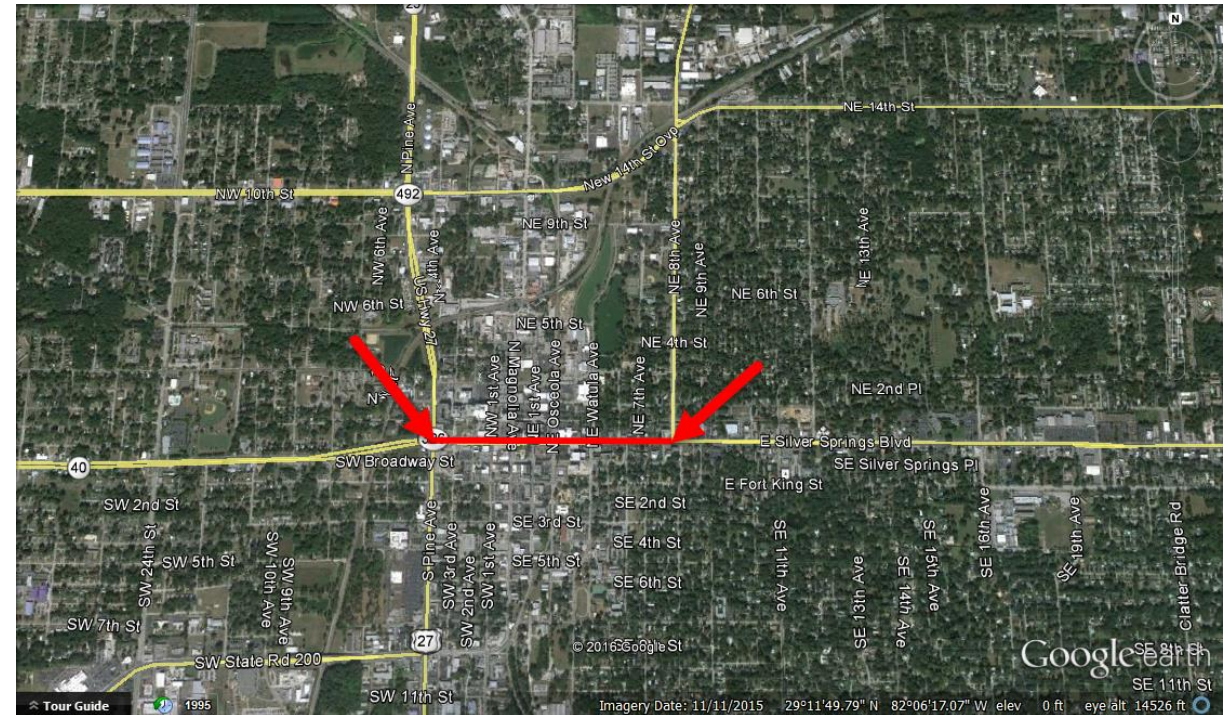

Design/Minor **Financial Project 437331-1**

- **US 441/SR 500/ORANGE BLOSSOM TRAIL - NORTH OF JONES AVE TO SOUTH OF WADSWORTH ROAD**


- Orange County
- Work Mix – RESURFACING
- Work Types – 3.1
- Design Costs - \$662,000
- Advertisement Date – May 2, 2016
- Project Manager – Gene Varano
- TRC Members – Todd Long,
Naziru Isaac, Jonathan Jastremsky

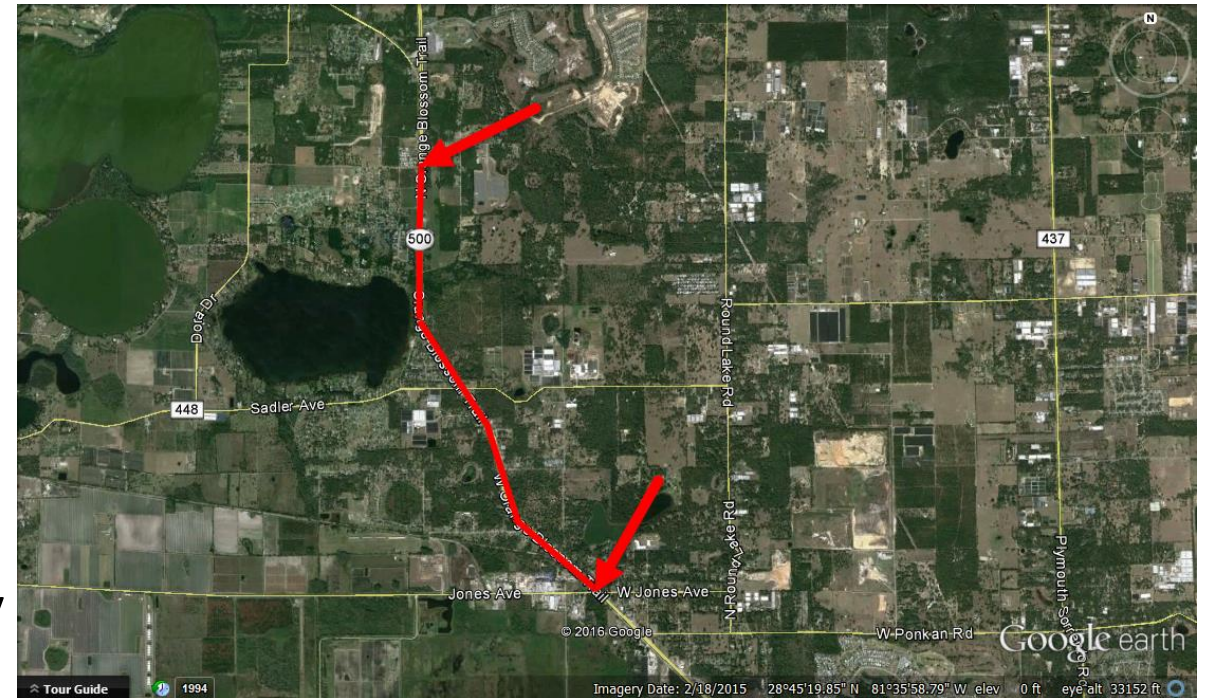

Design/Minor **Financial Project 437341-1**

- **SR 435/KIRKMAN ROAD FROM NORTH OF SR 482 TO SOUTH OF SR 408**


- Orange County
- Work Mix – RESURFACING
- Work Types – 3.1
- Design Costs - \$1,390,000
- Advertisement Date – June 27, 2016
- Project Manager – Heidi Trivett
- TRC Members – Storm Kazmierczak, Efren Rivera, Sarah Van Gundy

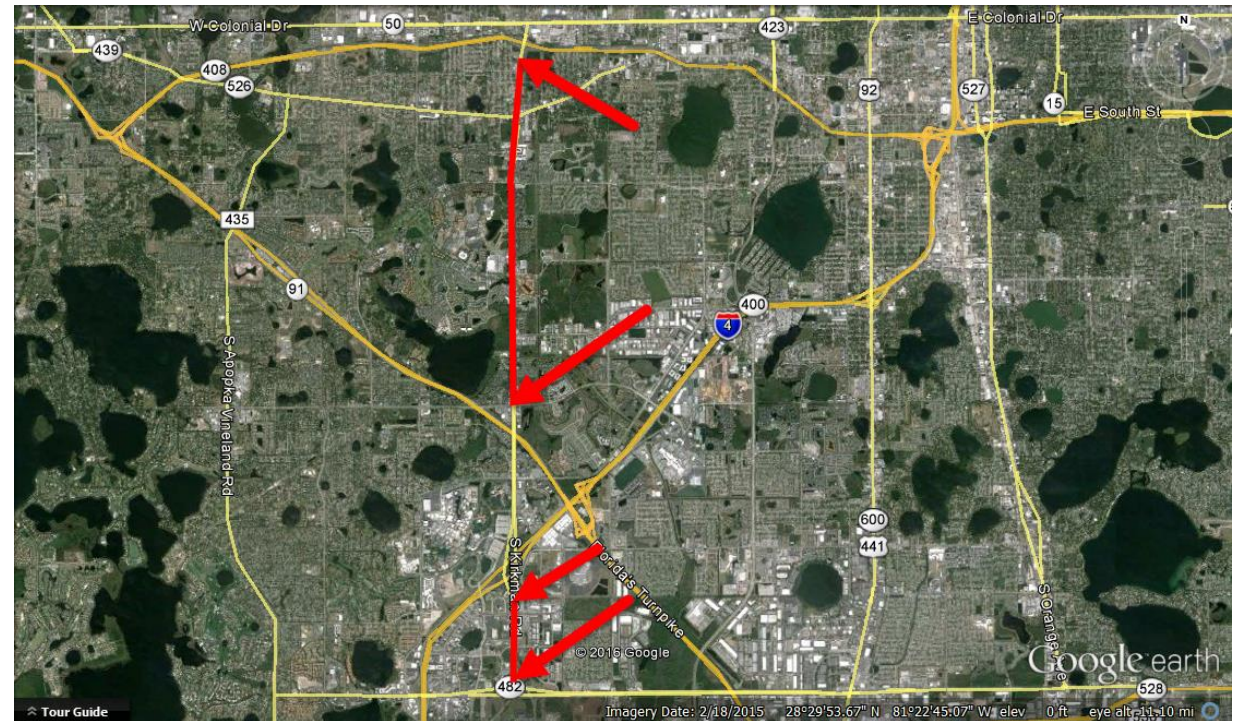

Design/Minor **Financial Project 437116-1**


■ **SR 5/US 1 DRAINAGE OUTFALL FROM NORTH OF CROSS ROAD TO INDIAN RIVER DRIVE**

- Brevard County
- Work Mix – DRAINAGE IMPROVEMENTS
- Work Types – 3.1
- Design Costs - \$358,000
- Advertisement Date – July 11, 2016
- Project Manager – Catalina Chacon
- TRC Members – Hatem Aguib,
Ferrell Hickson, Carol Hatfield

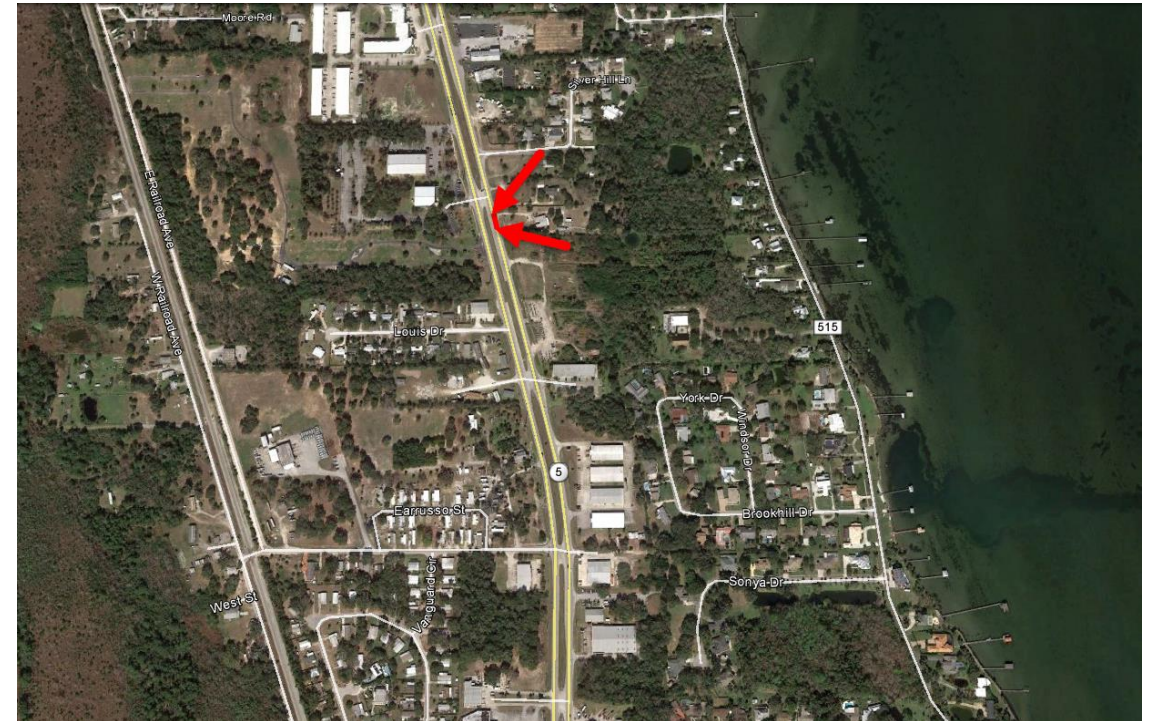

Design/Minor **Financial Project 437345-1**


- **SR 50/CHENEY HIGHWAY FROM ORANGE COUNTY LINE TO INTERSTATE 95 SB ON RAMP**
- Brevard County
- Work Mix – RESURFACING
- Work Types – 3.1
- Design Costs - \$846,000
- Advertisement Date – August 1, 2016
- Project Manager – Kevin Moss
- TRC Members – Todd Alexander,
Ed Cashman, Marianne Saunders

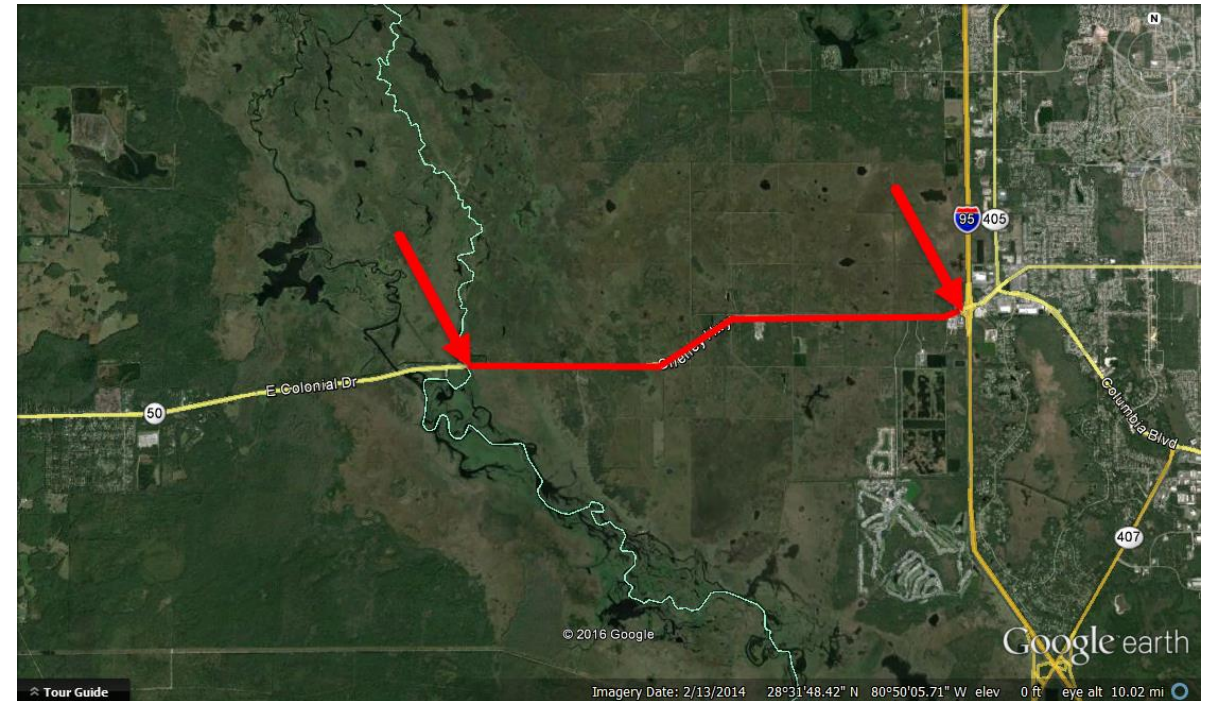

Design/Minor **Financial Project 436122-1**

■ **SR 405 SPACEPORT CONNECTOR SIS INTERSECTION IMPROVEMENTS**

- Brevard County
- Work Mix – ADD LEFT TURN LANE(S)
- Work Types – 3.1
- Design Costs - \$1,045,000
- Advertisement Date – November 21, 2016
- Project Manager – Jerald Marks
- TRC Members – Kevin Moss,
Ashraf Elmaghraby, Ed Cashman

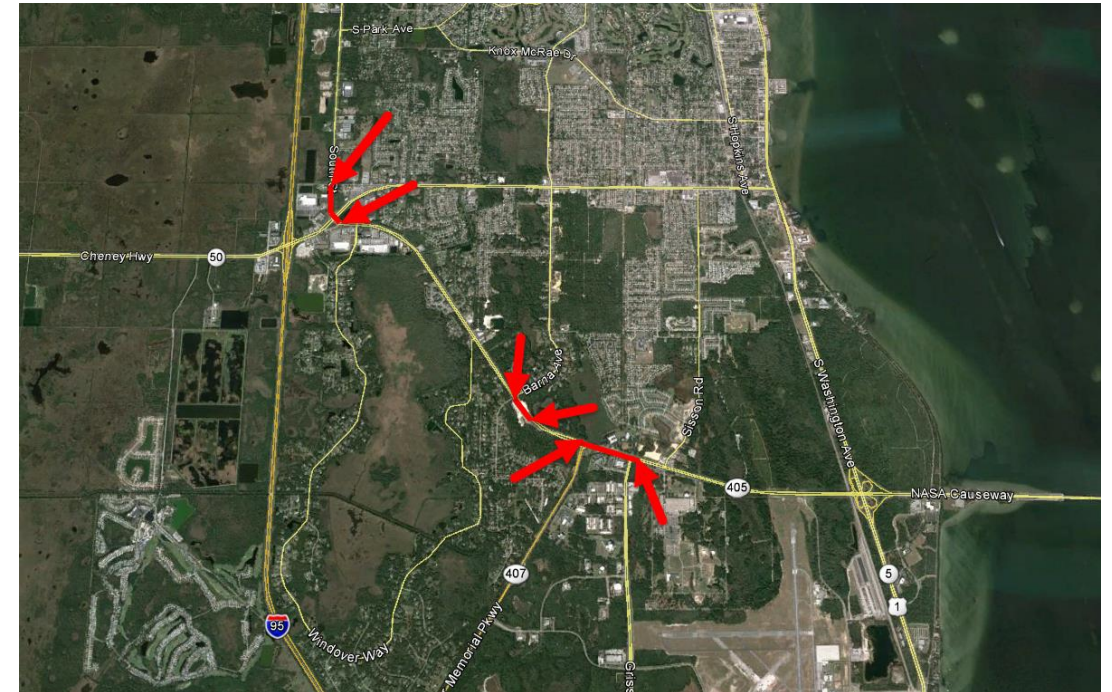

DESIGN

MINOR BUNDLED PROJECTS



Florida Department of Transportation

CAP
FDOT-D5
January 26, 2016

Design/Major Bundled Projects

Financial Project 437330-1

Financial Project 437634-1

Total Design Cost - \$1,317,000




Florida Department of Transportation

CAP
FDOT-D5
January 26, 2016

Design/Major Bundled Projects – 437330-1 & 437634-1

Financial Project 437330-1

- **SR 527/SR 426/ORANGE AVENUE - ORANGE AVENUE SB BIFURCATION TO NORTH GRANT ST**
- Orange County
- Work Mix – RESURFACING
- Work Types – 3.1
- Design Costs - \$817,000
- Advertisement Date – July 18, 2016
- Project Manager – Taleb Shams
- TRC Members – TBD,
TBD, Ty Garner

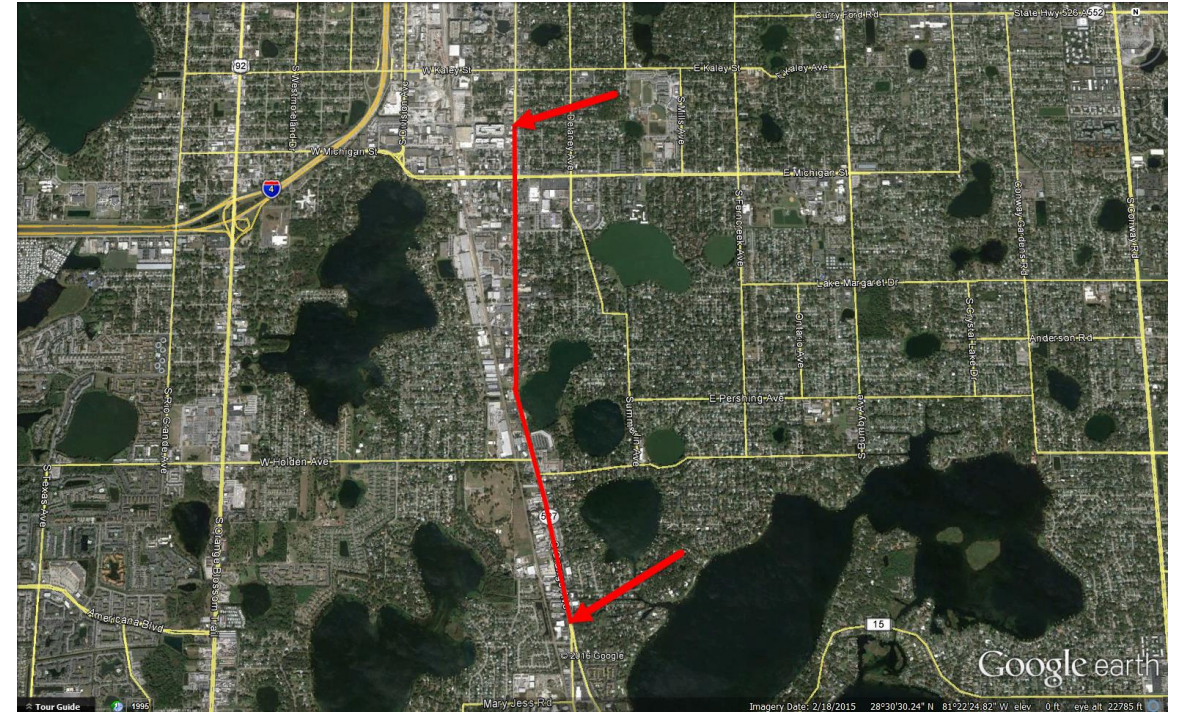


Design/Major Bundled Projects – 437330-1 & 437634-1

Financial Project 437634-1

■ SR 551 FROM NORTH OF RAMP 75008037 TO NORTH OF CAROLYN AVENUE

- Orange County
- Work Mix – SAFETY PROJECT
- Work Types – 3.1
- Design Costs - \$500,000
- Advertisement Date – July 18, 2016
- Project Manager – Taleb Shams
- TRC Members – TBD,
TBD, Ty Garner

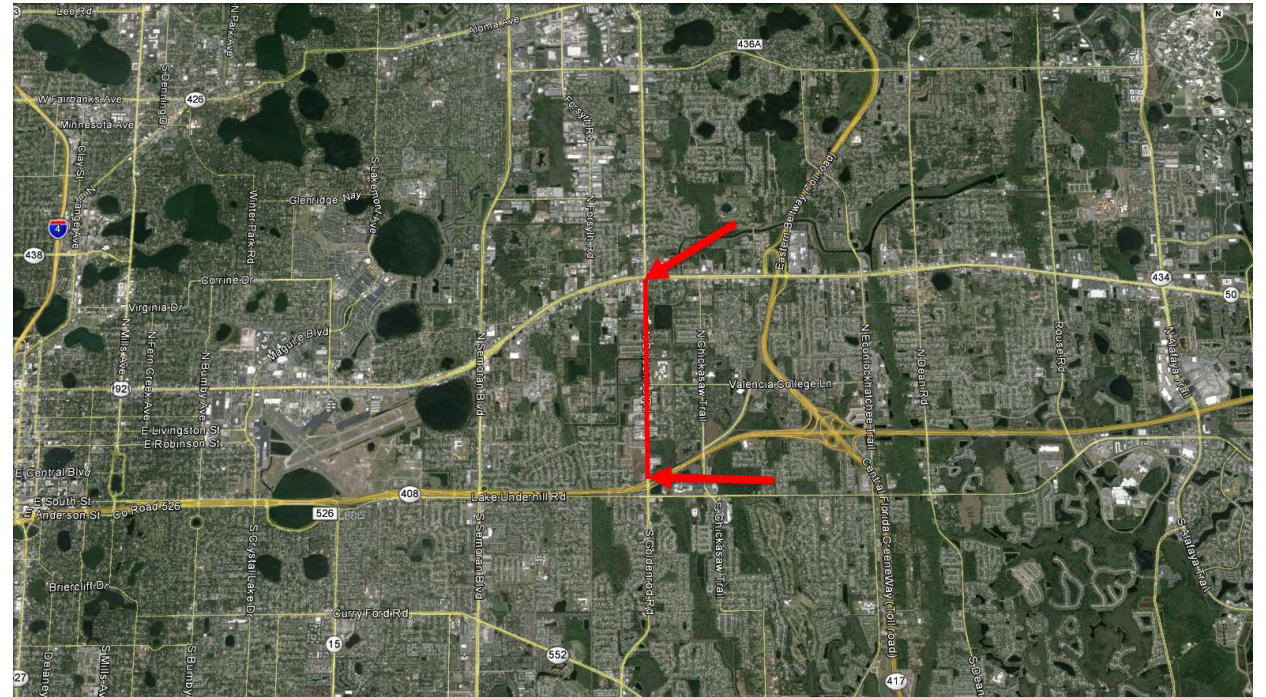

Design/Major Bundled Projects

Financial Project 438003-1
Financial Project 438003-2

Total Design Cost - \$1,300,000




Florida Department of Transportation

CAP
FDOT-D5
January 26, 2016

Design/Major Bundled Projects – 438003-1 & 438003-2

Financial Project 438003-1

- **INTERSTATE 95 FROM VOLUSIA COUNTY LINE TO NORTH OF PALM COAST PARKWAY**
- Flagler County
- Work Mix – RESURFACING
- Work Types – 3.1
- Design Costs - \$650,000
- Advertisement Date – August 15, 2016
- Project Manager – Heidi Trivett
- TRC Members – Gary Skofronick,
Leo Cortes, Ashraf Elmaghraby

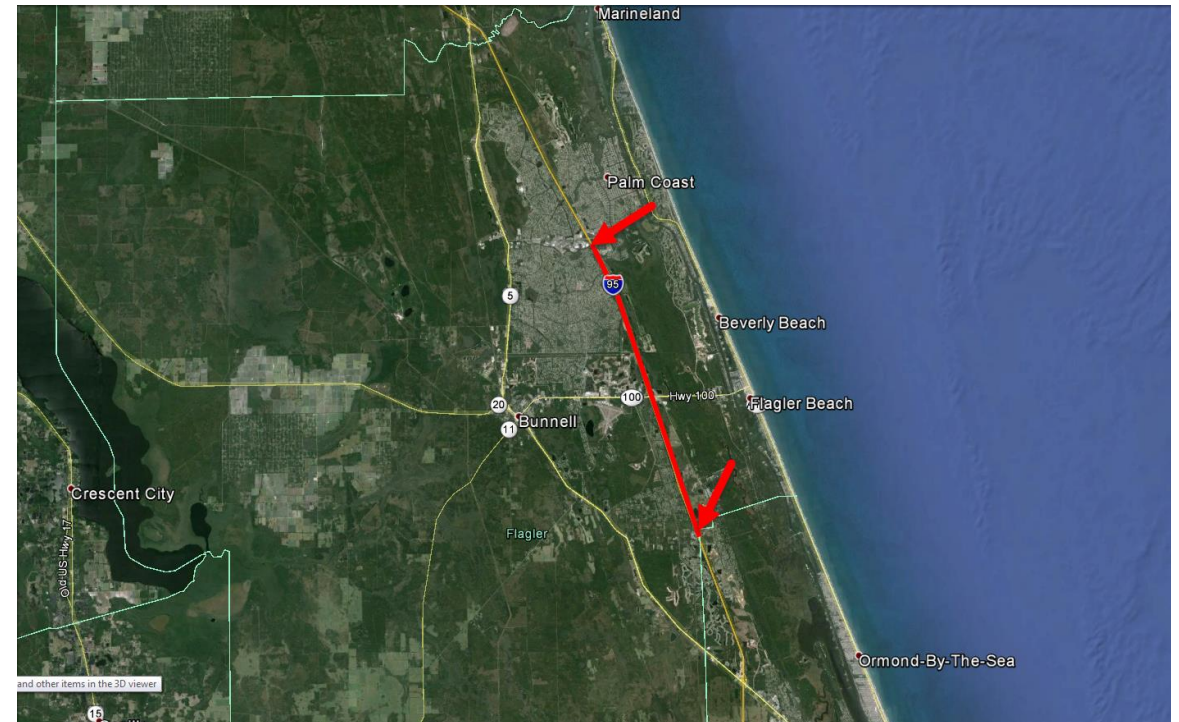


Design/Major Bundled Projects – 438003-1 & 438003-2

Financial Project 438003-2

■ INTERSTATE 95 FROM NORTH OF PALM COAST PARKWAY TO PELLICER CREEK

- Flagler County
- Work Mix – RESURFACING
- Work Types – 3.1
- Design Costs - \$650,000
- Advertisement Date – August 15, 2016
- Project Manager – Heidi Trivett
- TRC Members – Gary Skofronick,
Leo Cortes, Ashraf Elmaghraby

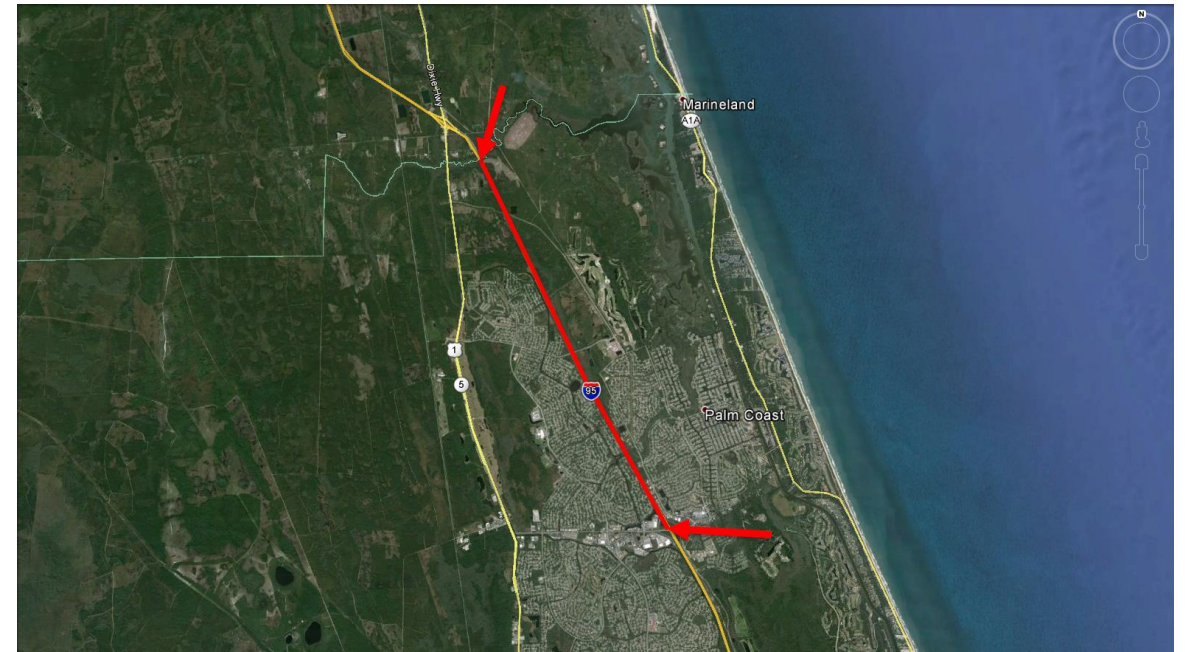

DESIGN

SMALL BUSINESS ENTERPRISE (SBE)



Florida Department of Transportation

CAP
FDOT-D5
January 26, 2016


Financial Project 437451-1

- **US 192 AT HOAGLAND BLVD**
- Osceola County
- Work Mix – ADD LEFT TURN LANE(S)
- Work Types – 3.1
- Design Costs - \$300,000
- Advertisement Date – May 30, 2016
- Project Manager – Kathy Enot
- TRC Members – Taleb Shams,
Mark Trebitz, Lori Epperson




Financial Project 437592-1

- **SR 600/SR 500/US 441/US 17-92 FROM SOUTH OF SR 482 (SAND LAKE ROAD) TO NORTH OF SR 482**
- Orange County
- Work Mix – INTERSECTION IMPROVEMENT
- Work Types – 3.1
- Design Costs - \$335,000
- Advertisement Date – April 18, 2016
- Project Manager – Hatem Aguib
- TRC Members – Heather Johnstone,
Chris Dabson, Kathy Enot

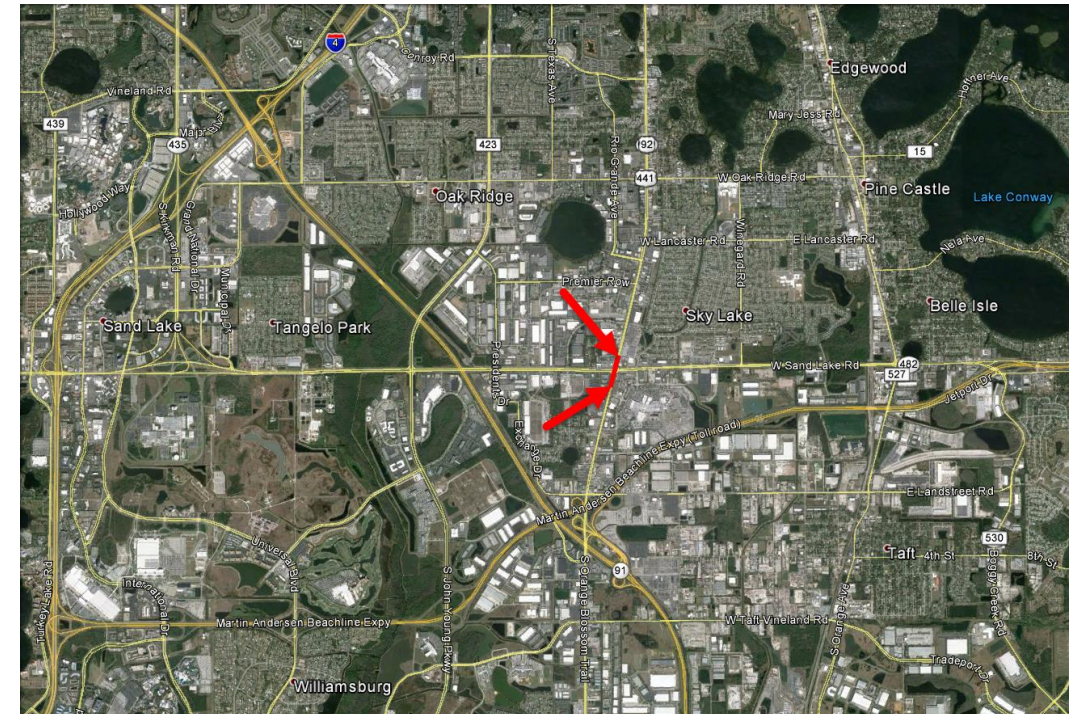


Financial Project 437339-1

- **SR 500 / US 27 FROM LEVY COUNTY LINE TO CR 326**
- Marion County
- Work Mix – RESURFACING
- Work Types – 3.1
- Design Costs - \$340,000
- Advertisement Date – August 8, 2016
- Project Manager – Gene Varano
- TRC Members – Catalina Chacon,
Angela Cardona, Naziru Isaac

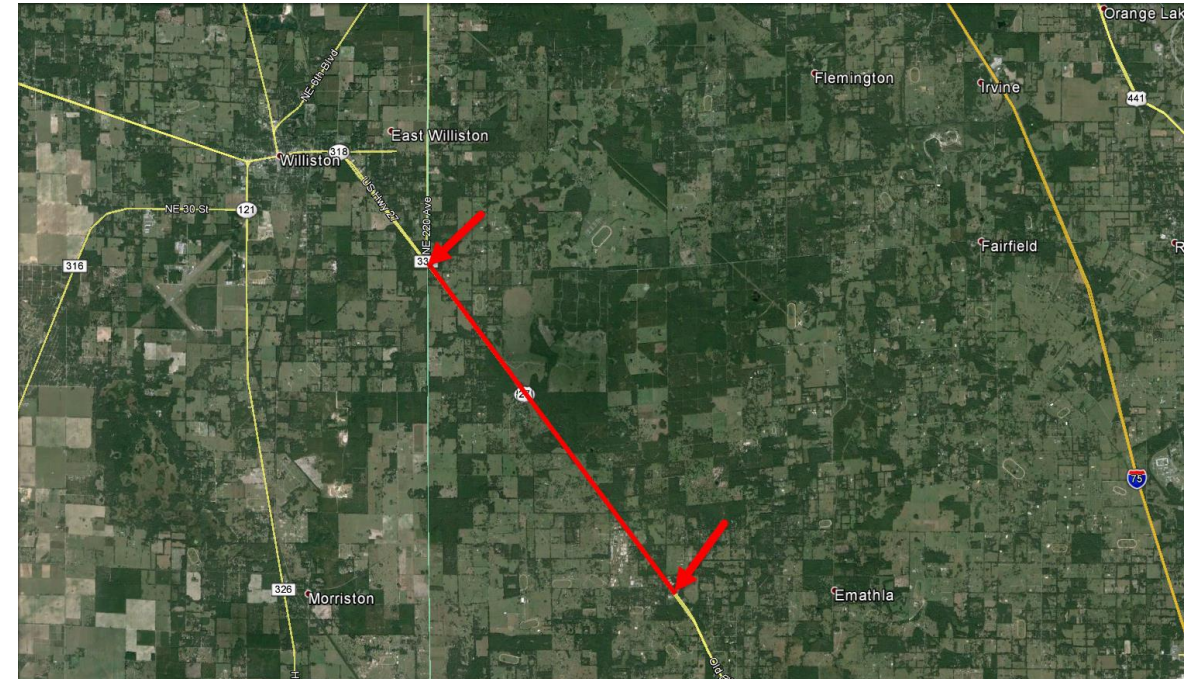

Financial Project 437348-1

- **SR 44 FROM 1900' WEST OF CR 437 TO VOLUSIA COUNTY LINE**
- Lake County
- Work Mix – RESURFACING
- Work Types – 3.1
- Design Costs - \$1,300,000
- Advertisement Date – September 5, 2016
- Project Manager – Sarah Van Gundy
- TRC Members – Christine Bacomo,
Heather Johnstone, Neil Kenis

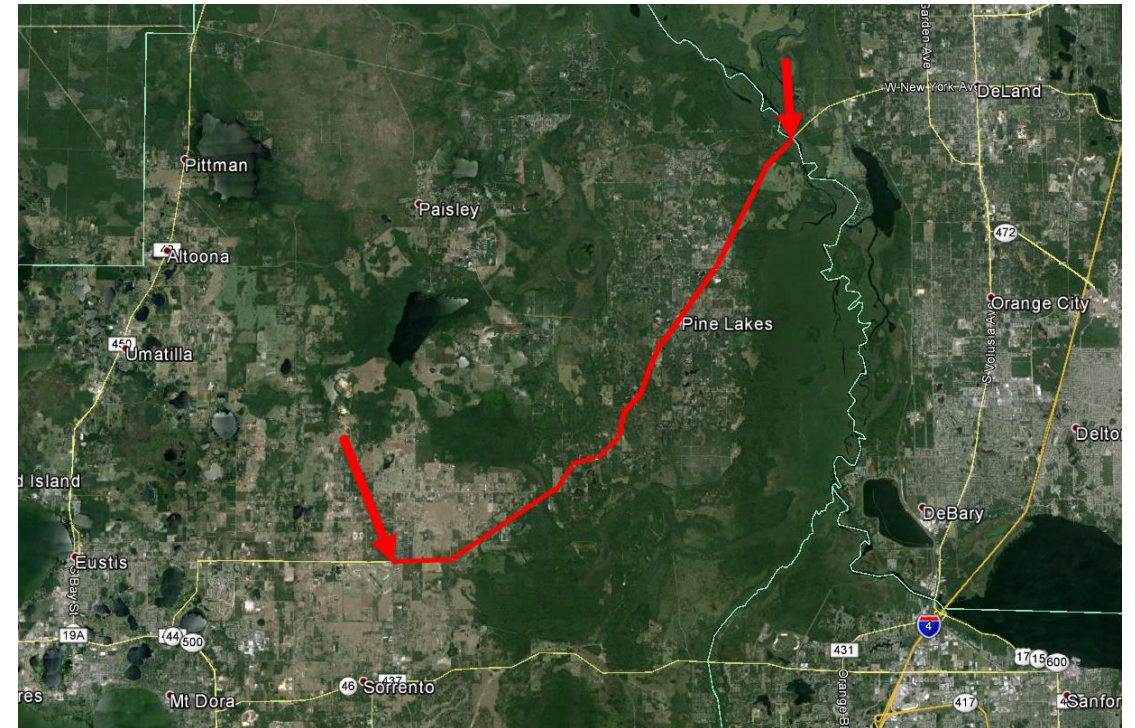

DESIGN

SMALL BUSINESS ENTERPRISE (SBE) BUNDLED PROJECTS



Florida Department of Transportation

CAP
FDOT-D5
January 26, 2016


Financial Project 435647-1
Financial Project 435651-1

Total Design Cost - \$895,000

Design/SBE Bundled Projects – 435647-1 & 435651-1

Financial Project 435647-1


- **SR A1A/ASTRONAUT BLVD FROM MCKINLEY/ TO ATLANTIC AVENUE**
- Brevard County
- Work Mix – TRAFFIC SIGNALS
- Work Types – 3.1
- Design Costs - \$575,000
- Advertisement Date – March 28, 2016
- Project Manager – Christine Bacomo
- TRC Members – Beata Stys- Palasz,
Angela Cardona, Ty Garner

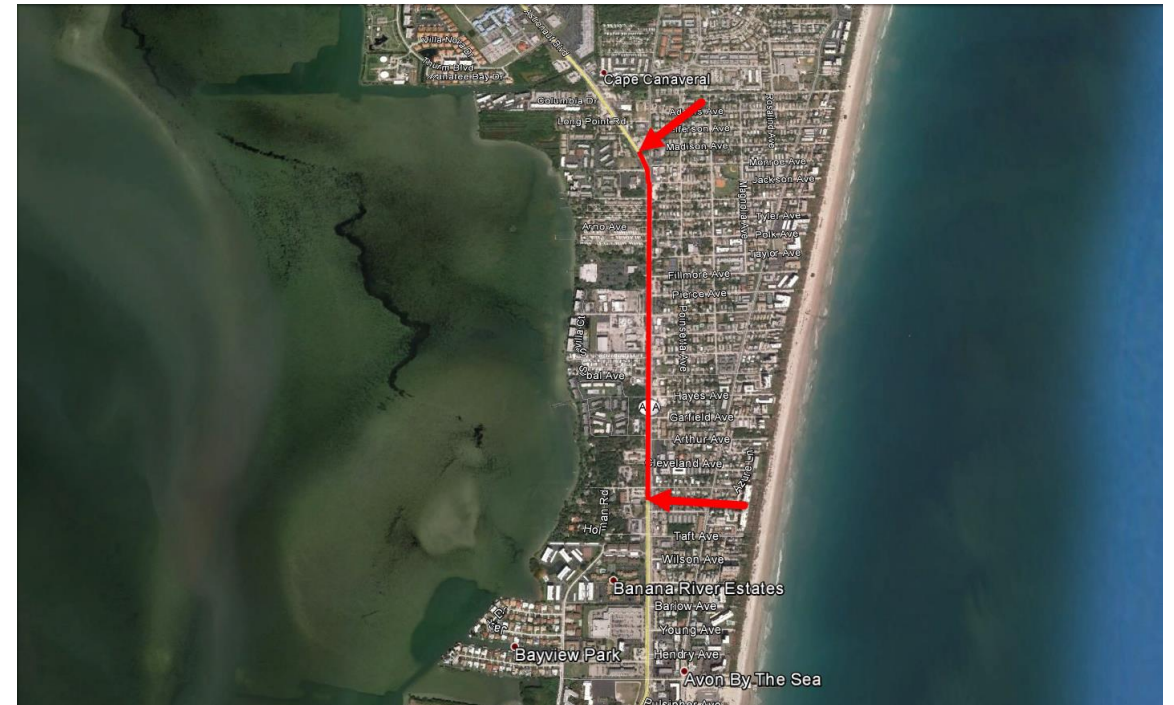

Design/SBE Bundled Projects – 435647-1 & 435651-1

Financial Project

- **SR 5/US 1 FROM SR 508 (NASA) TO CHERRY STREET**
 - Brevard County
 - Work Mix – TRAFFIC SIGNALS
 - Work Types – 3.1
 - Design Costs - \$320,000
 - Advertisement Date – March 28, 2016
 - Project Manager – Christine Bacomo
 - TRC Members – Beata Stys- Palasz,
Angela Cardona, Ty Garner

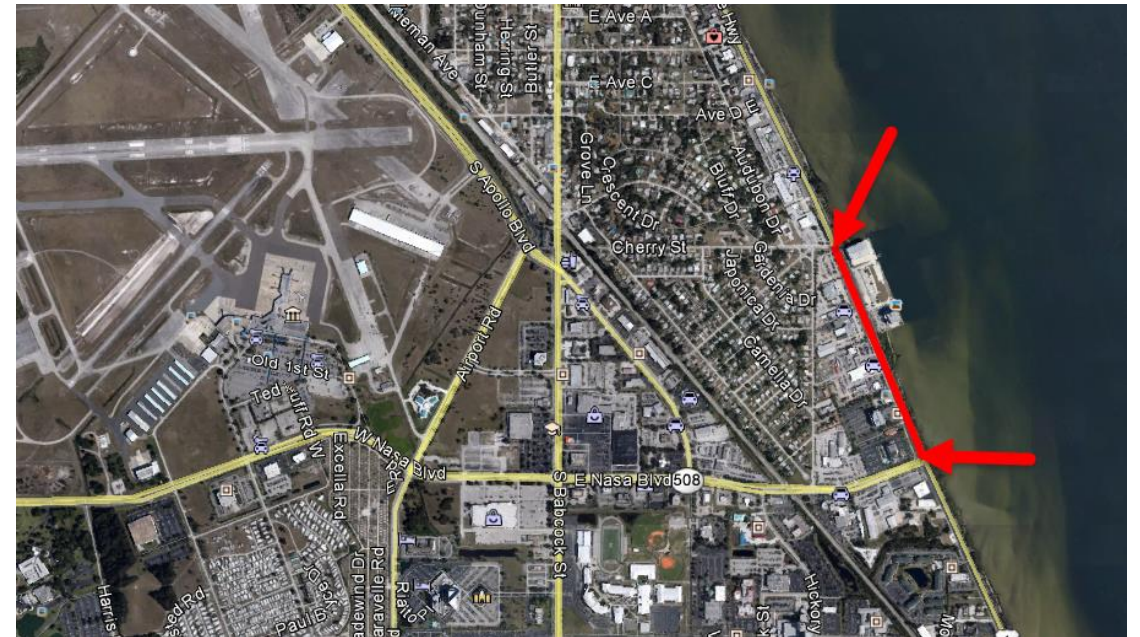


DESIGN

DESIGN BUILD


Financial Project 238319-2

■ SR 19 OVER LITTLE LAKE HARRIS BRIDGE # 110026

- Lake County
- Work Mix – Bridge Replacement
- Design Work Types – 3.2, 4.1.2
- Construction Work Type – 10.1
(Major Bridge)
- Design-Build Costs – \$44,691,282
- Advertisement Date – September 6, 2016
- Project Manager – Catalina Chacon
- TRC Members - TBD

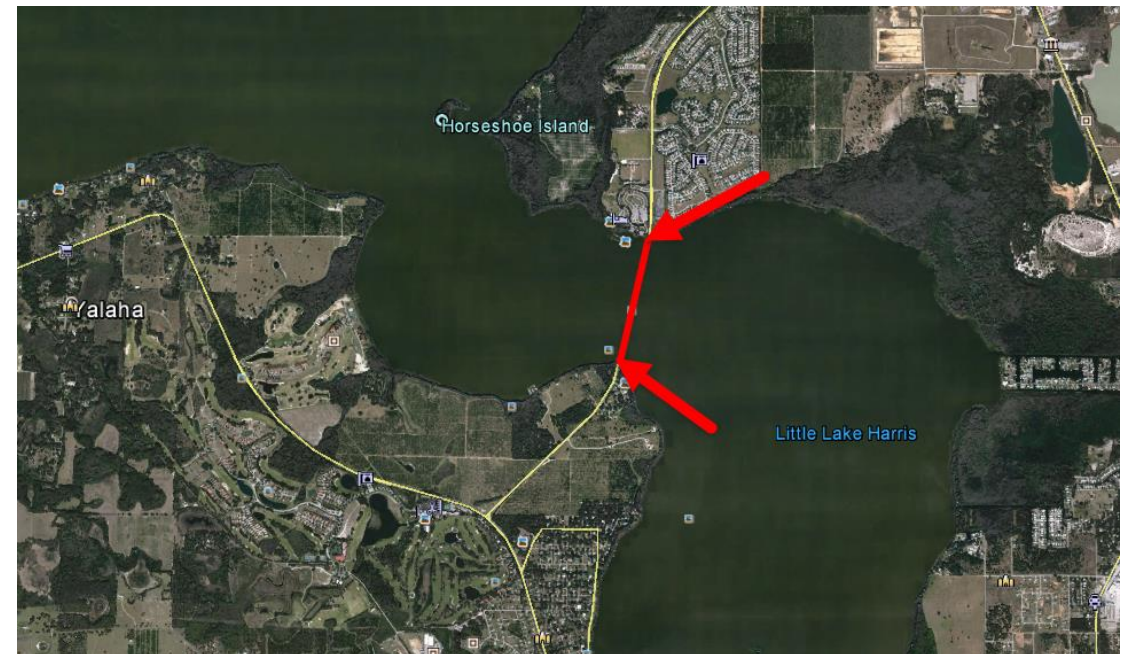

- **SR 429/SR 46 (WEKIVA PARKWAY) FROM WEST OF OLD MCDONALD ROAD TO EAST OF WEKIVA RIVER ROAD**
- Lake County
- Work Mix – New Road Construction
- Work Types – 3.3, 4.2.1, 4.2.3
- Design Costs – \$215,704,750
- Advertisement Date – May 2, 2016
- Project Manager – Kevin Moss
- TRC Members – John Tyler,
Amy Scales, Neil Kenis

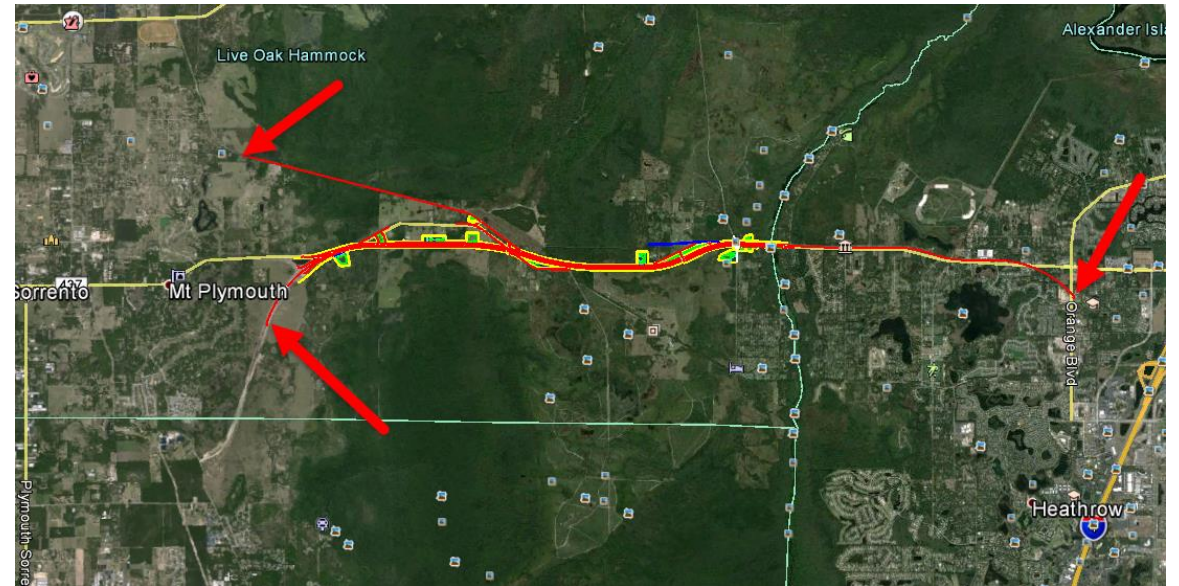



A Regional Transportation Solution

Industry Forum

January 26, 2016

1:30 – 5:00



DESIGN

MISCELLANEOUS DISTRICTWIDE CONTRACTS




Florida Department of Transportation

CAP
FDOT-D5
January 26, 2016

Financial Project 241081-1

■ DISTRICTWIDE DRAINAGE DESIGN CONSULTANT


- Location is throughout District 5
- Work Mix – Miscellaneous Drainage
- Work Types – 3.1, 3.2
- Contract estimated at \$300,000 currently programmed in first two years. Potentially worth 1.5M over 5-year term with renewals.
- Advertisement Date – March 14, 2016
- Project Manager – Efren Rivera
- TRC Members – Jeff Cicerello,
Patrick McConaghy, Karen Snyder

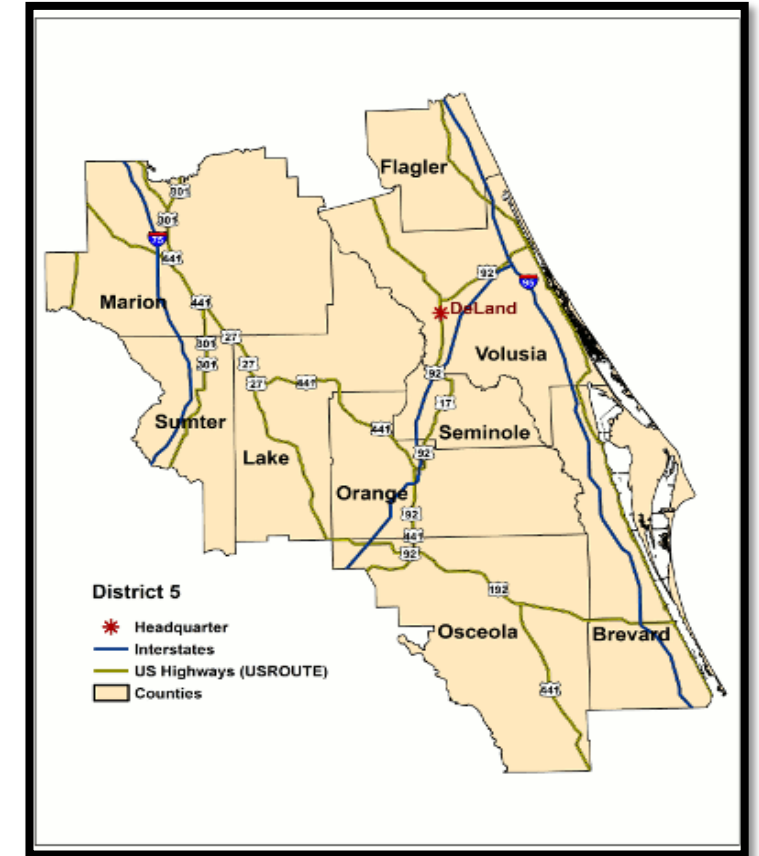

Financial Project 439167-1

■ ROADWAY LIGHTING DESIGN & STUDIES DW

- Location is throughout District 5
- Work Mix – Lighting Design & Studies
- Work Types – 7.2
- Design Costs – \$200,000
- Advertisement Date – TBD
- Project Manager – Megan Owens
- TRC Members – TBD

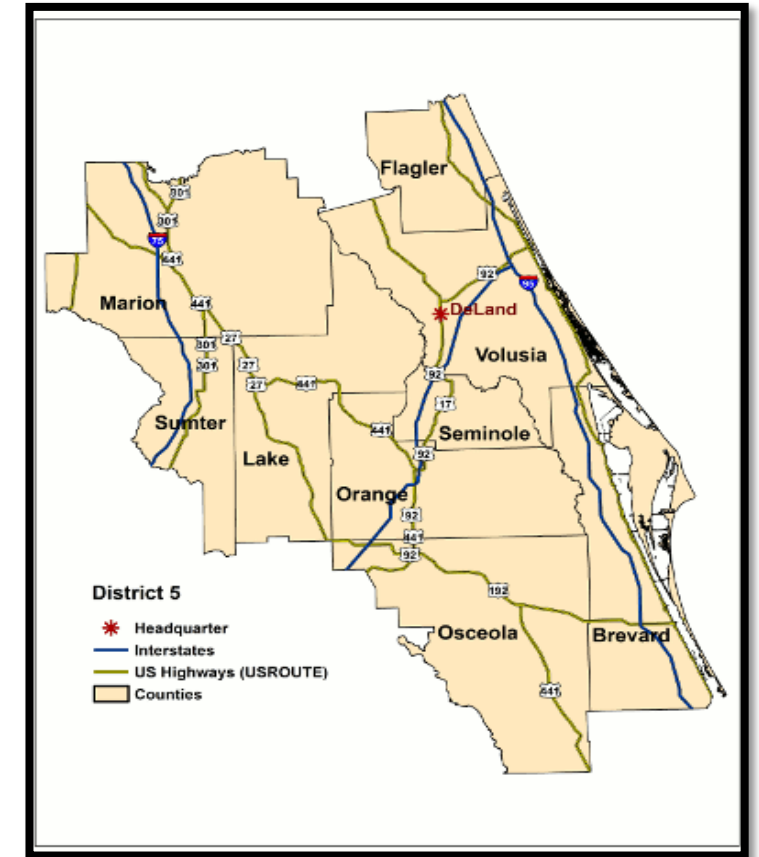

Planning & Environmental Management Office


PLEMO Contracts

**Brian Stanger, Planning & Environmental
Management Administrator**


Amy Sirmans, Project Development Manager

Bill Walsh, Environmental Manager


Planning & Environmental Management Office

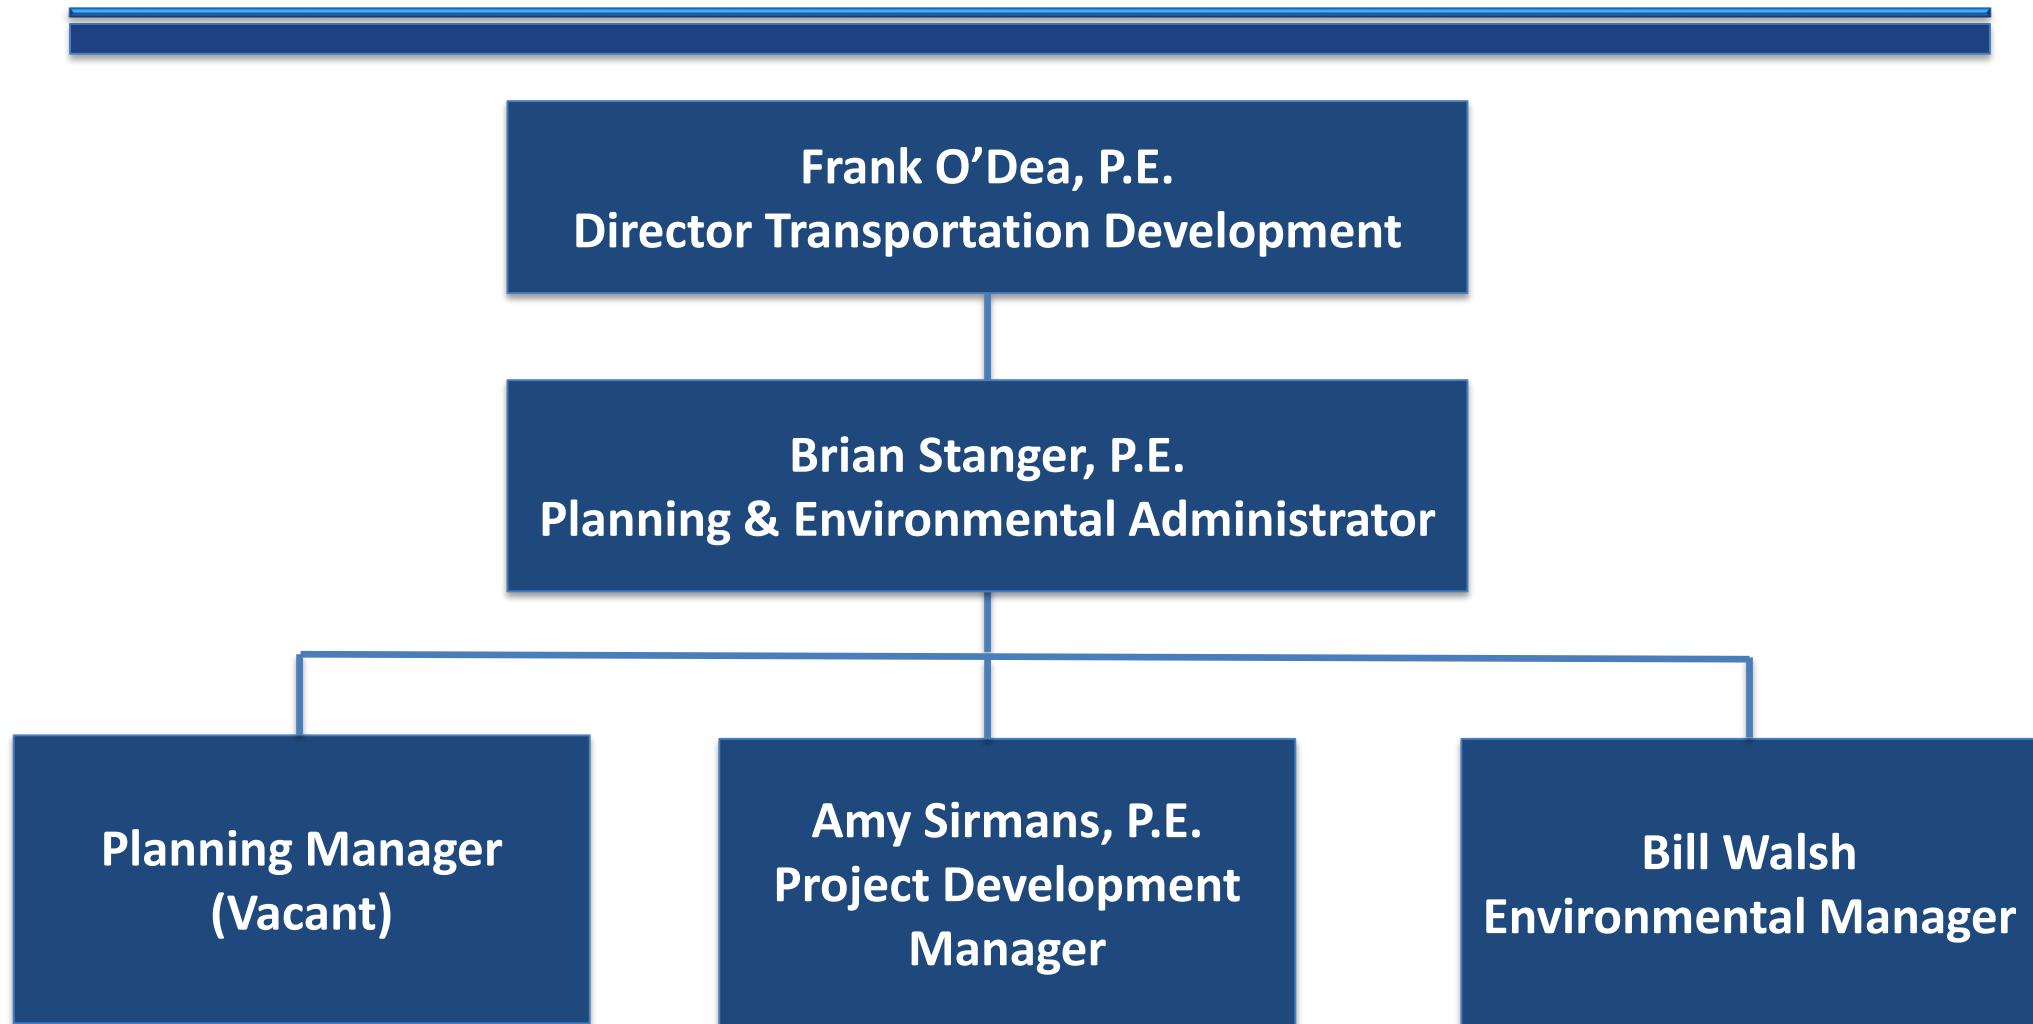


Environmental Management Unit

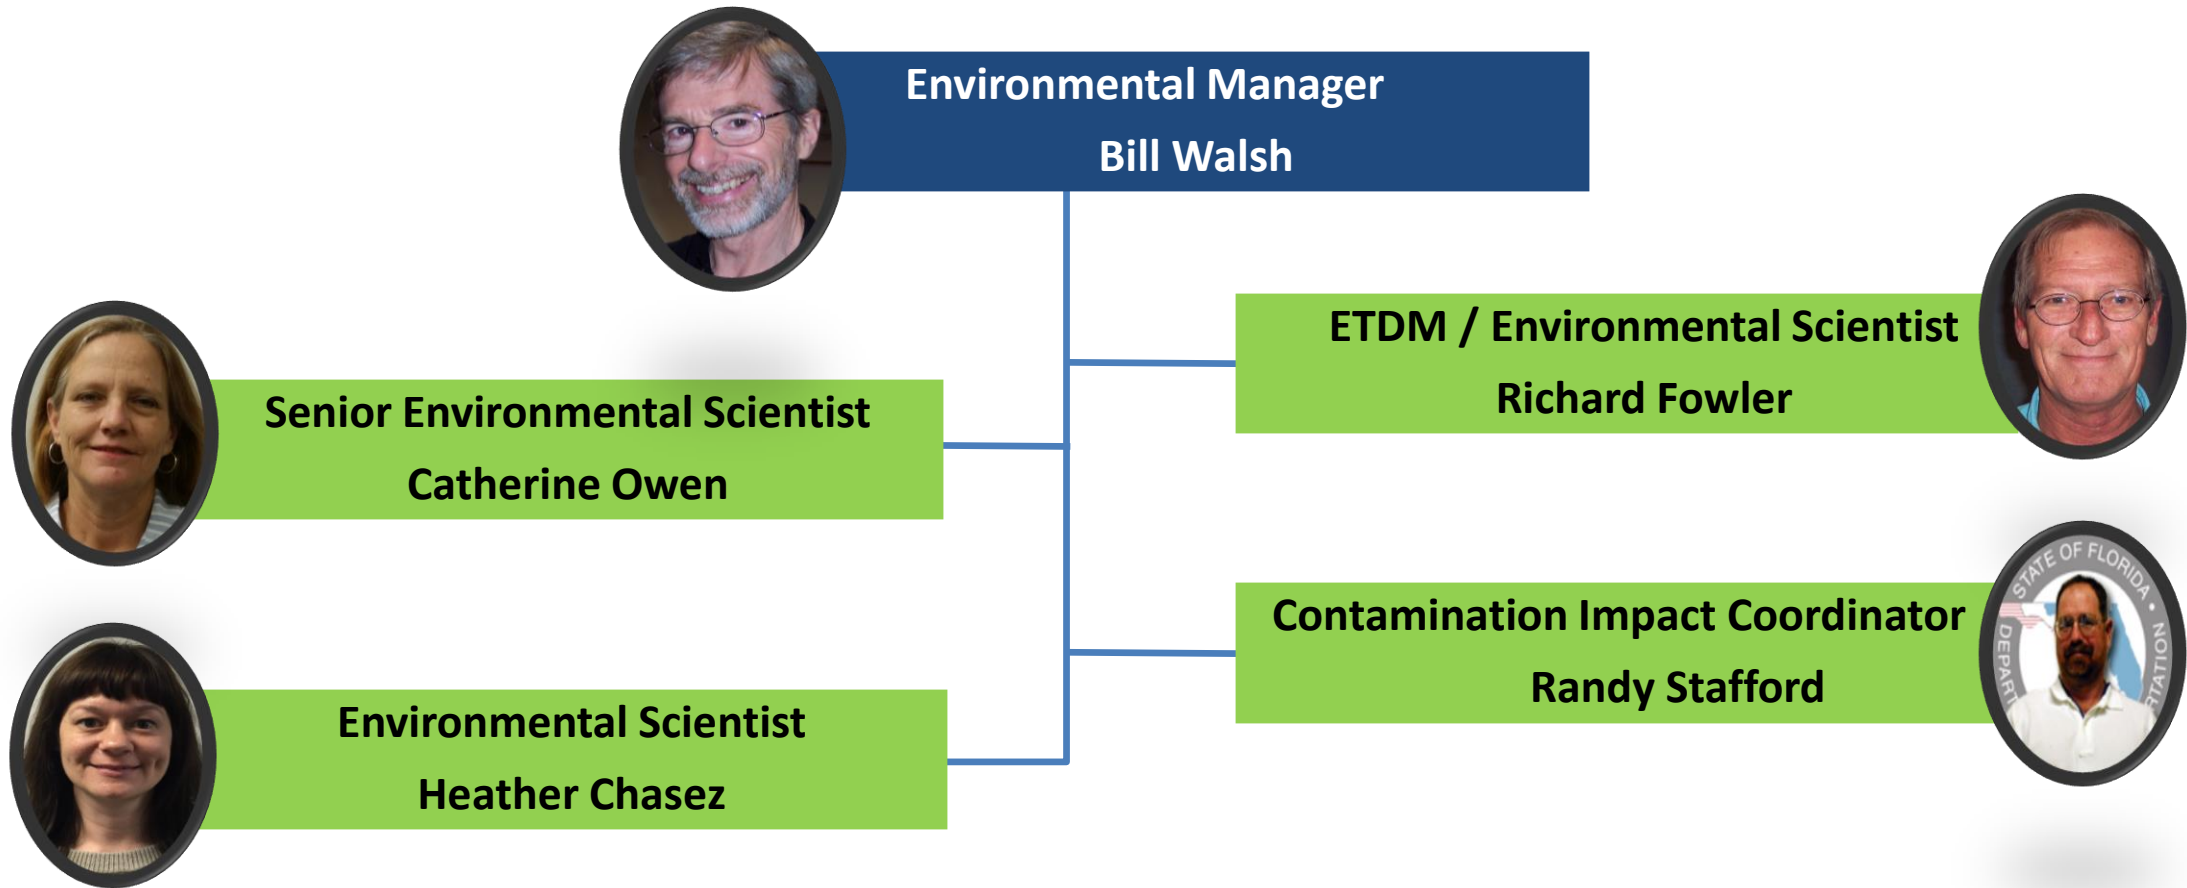

Project Development Unit

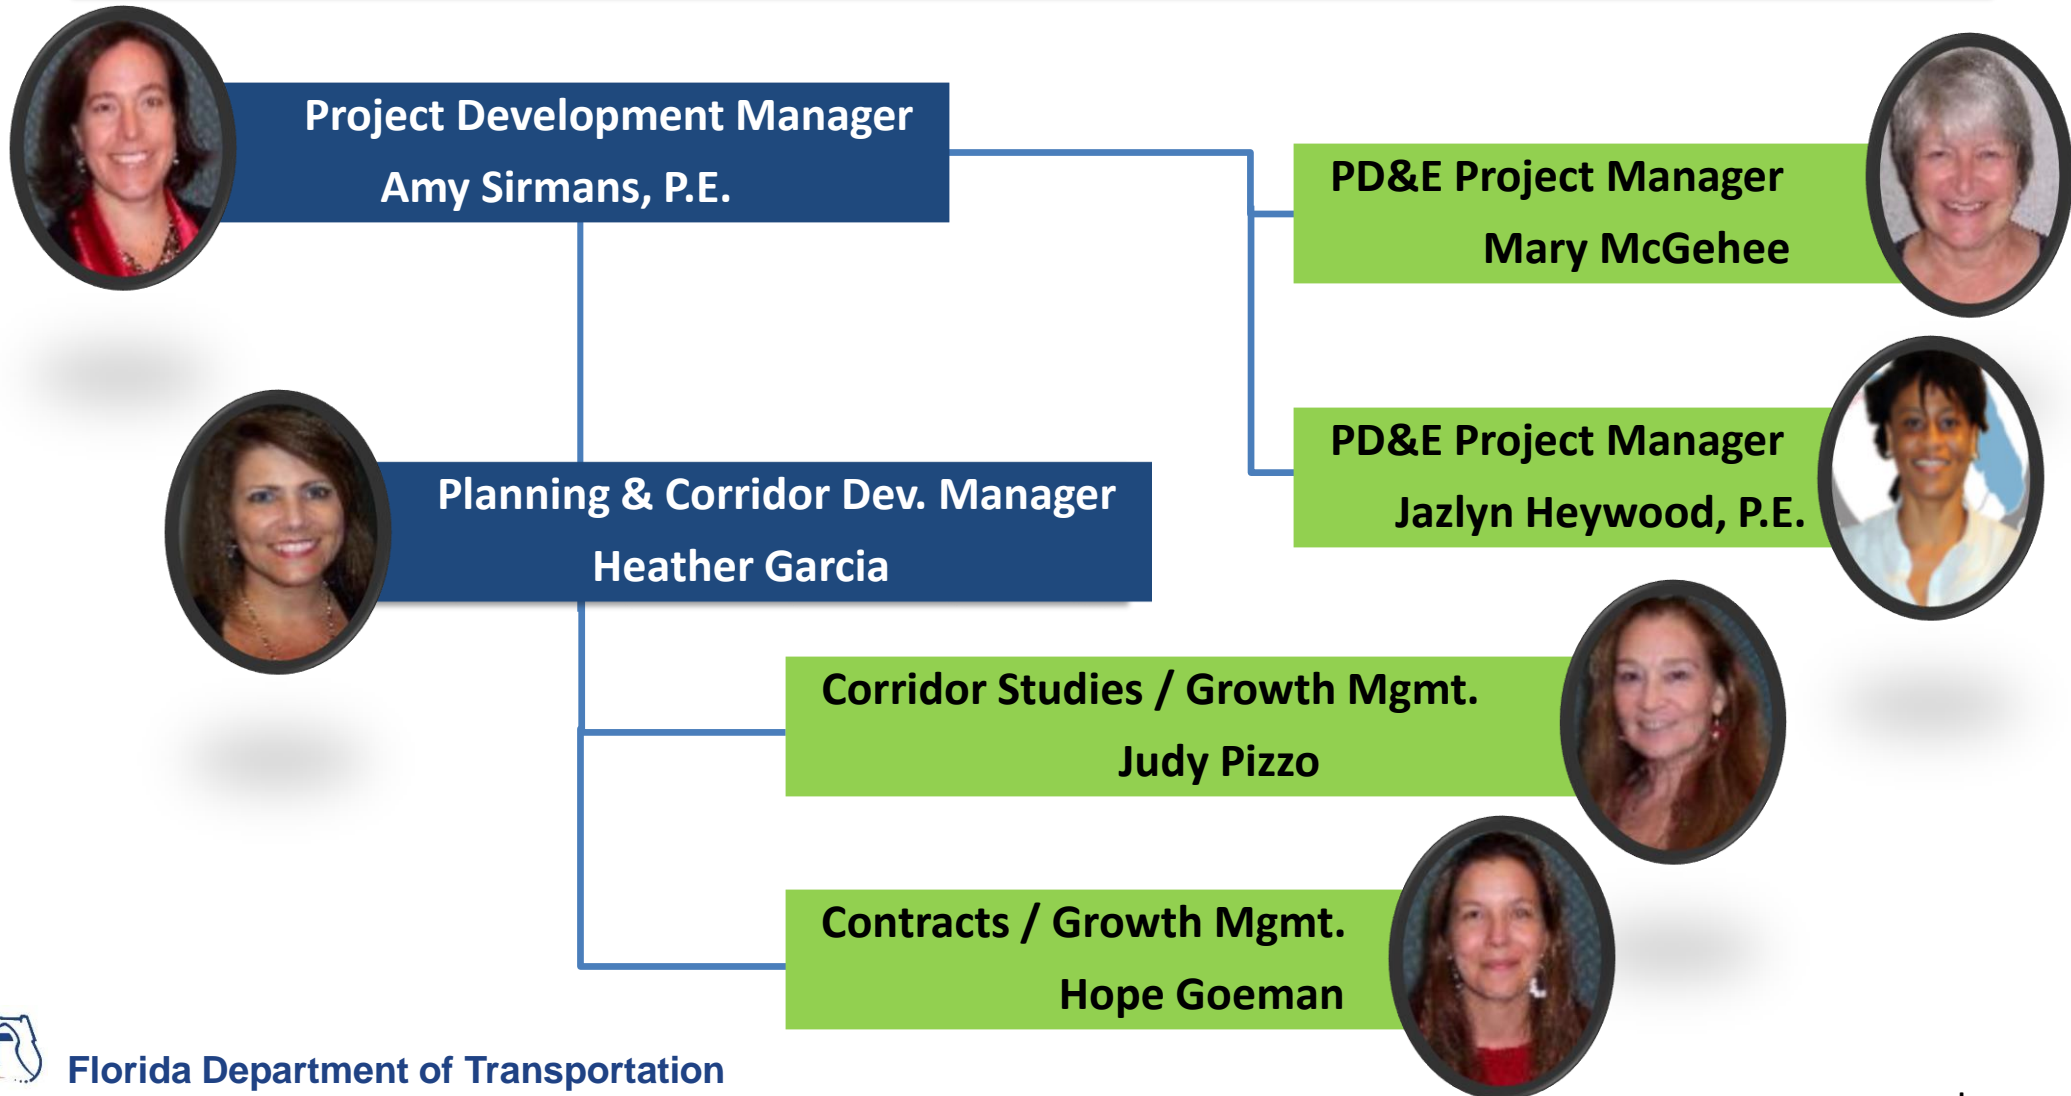

Planning Unit

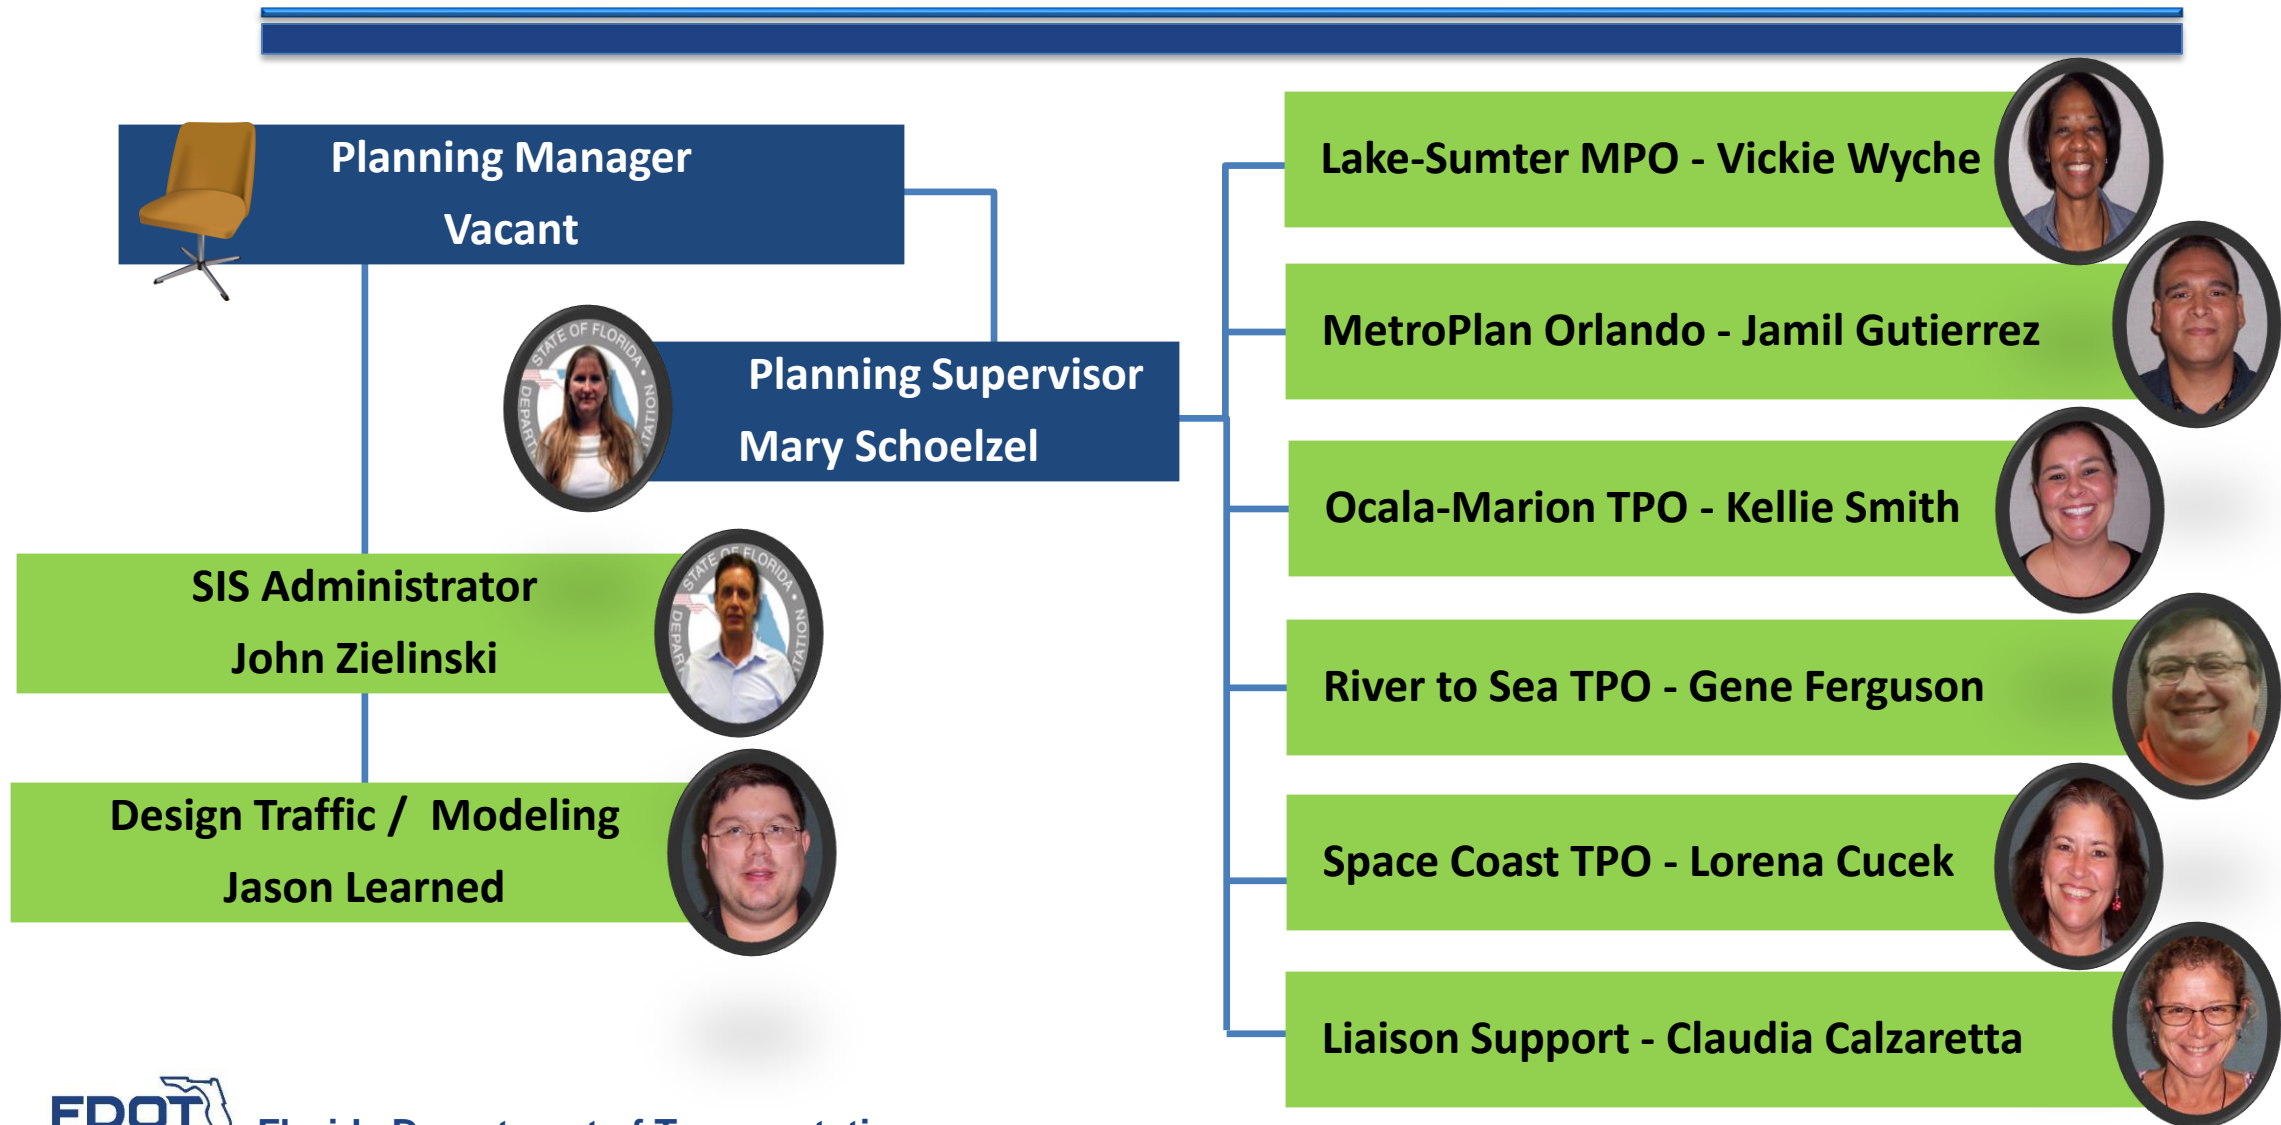

Florida Department of Transportation

Districtwide Environmental Services Contract


- 243396-1-22-03
 - Approximately \$300,000 per fiscal year allocated
 - 5 year contract
 - Advertising May 2016
 - PM: Catherine Owen
 - Recommended TRC: Bill Walsh, Amy Sirmans, Casey Lyon

Districtwide Environmental Services Contract


- Scope of Contract:
 - Environmental Analyses (e.g., listed species surveys, CRAS, noise analysis)
 - Environmental Documentation (Technical Reports, NEPA)
 - Scenic Highway Support Services [emphasis on D5's Fla. Scenic Highway Program]
 - Engineering Analyses and Reports / Public Involvement

I-75 Interchange at 49th Street PD&E Study

- 435209-1-22-01
- From end of NW 35th Street to NW 49th Street
- Marion County
- Approximately \$2,000,000 contract
- Advertising May 2016
- PM: Jazlyn Heywood, P.E.
- Recommended TRC: Amy Sirmans, Brian Stanger, Bill Walsh

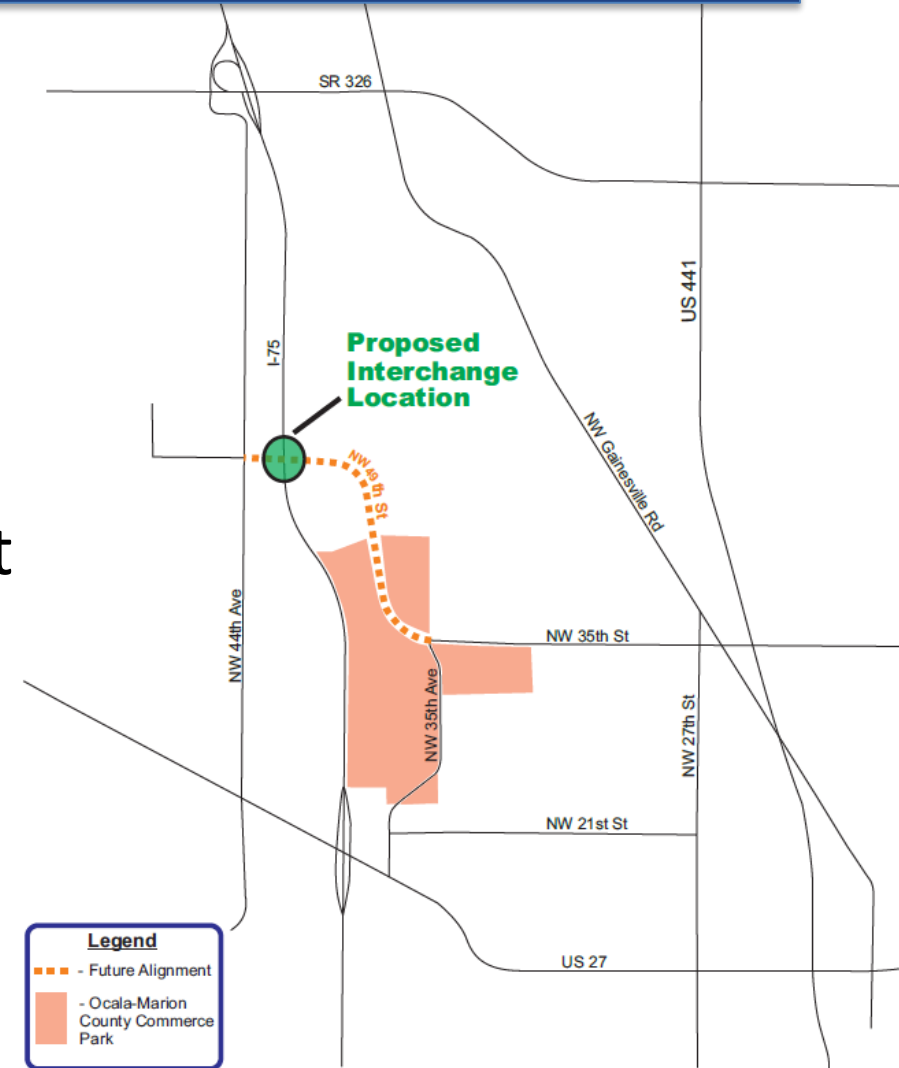

I-75 Interchange at 49th Street PD&E Study

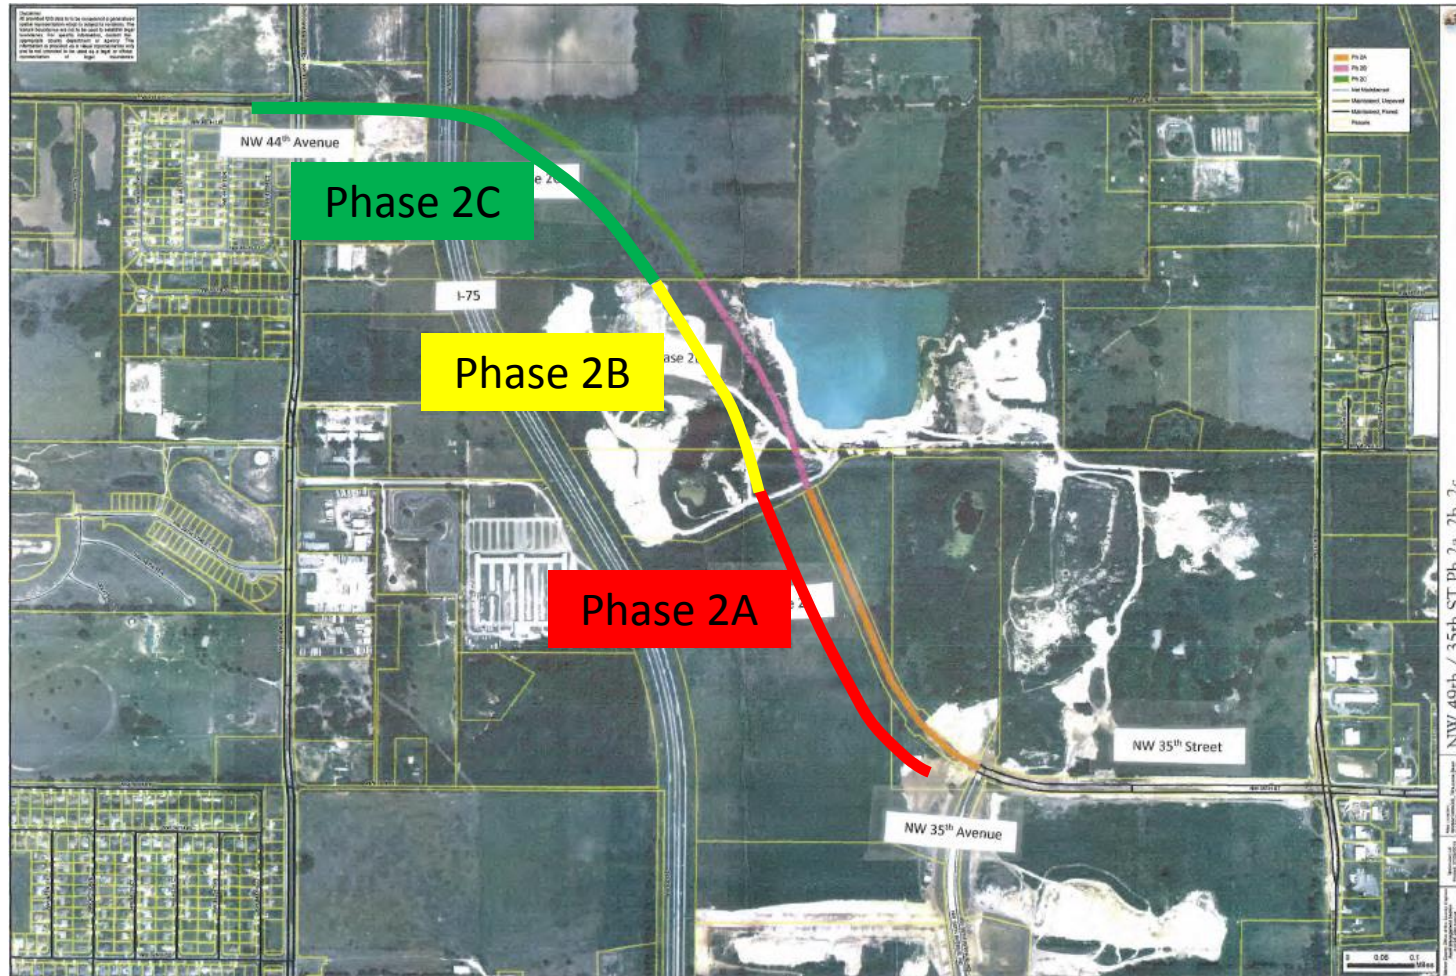

- Marion County will construct Phases 2A and 2B
- FDOT PD&E Study will cover Phase 2C



Florida Department of Transportation

CAP
FDOT-D5
January 26, 2016

I-75 Interchange at 49th Street PD&E Study

- IJR underway by Marion County
 - MLOU approved January 2015
 - 2nd Draft Preliminary IJR under revisions
 - IJR Programmatic Agreement
- ETDM Programming Screen
 - Plan to enter into EST in February

INTERCHANGE JUSTIFICATION REPORT

Interstate 75 and NW 49th/35th Street

Marion County, Florida



Prepared on behalf of:
Marion County



Florida Department of Transportation

CAP

FDOT-D5


January 26, 2016

South Sumter Connector Trail PD&E Study

- 435471-1-22-01
- From Withlacoochee State Trail to Van Fleet Trail
- Segment of Coast to Coast Trail
- Sumter County
- Advertising July/August 2016
- PM: Mary McGehee
- Recommended TRC: Amy Sirmans, Brian Stanger, Bill Walsh




South Sumter Connector Trail PD&E Study

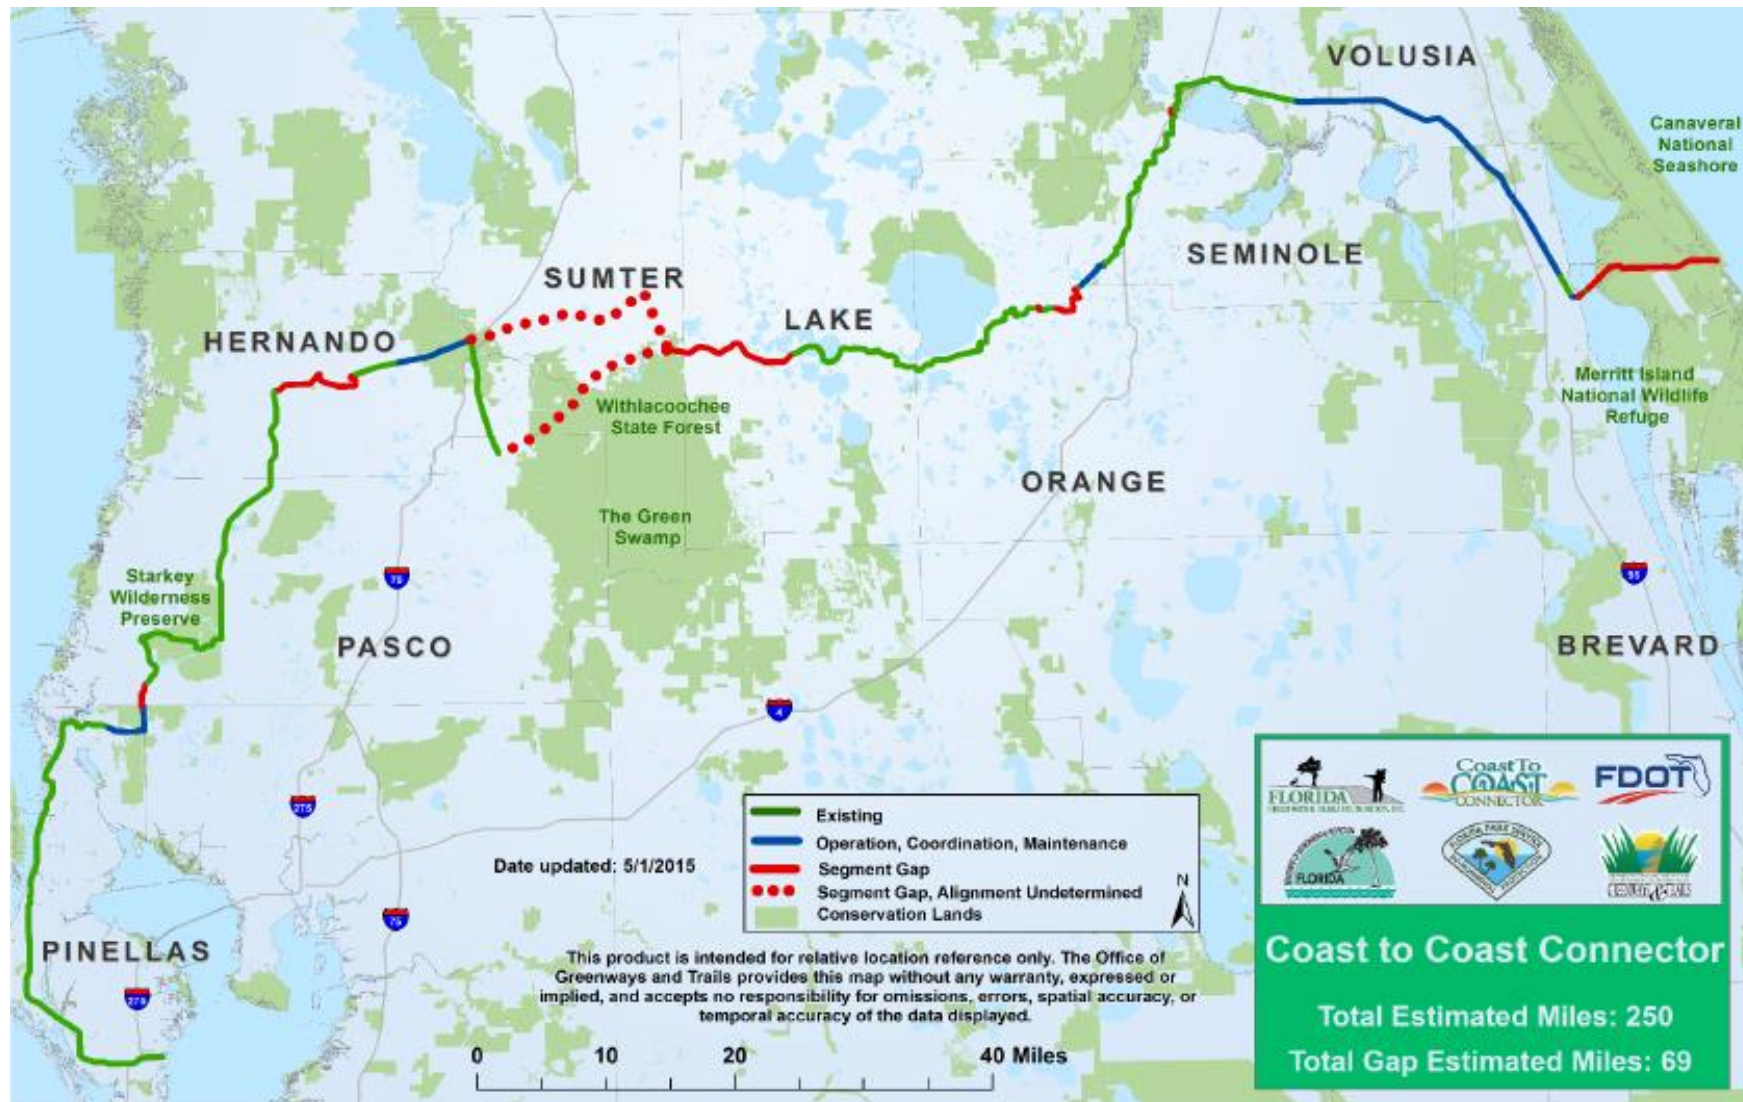

Florida Department of Transportation

CAP
FDOT-D5
January 26, 2016

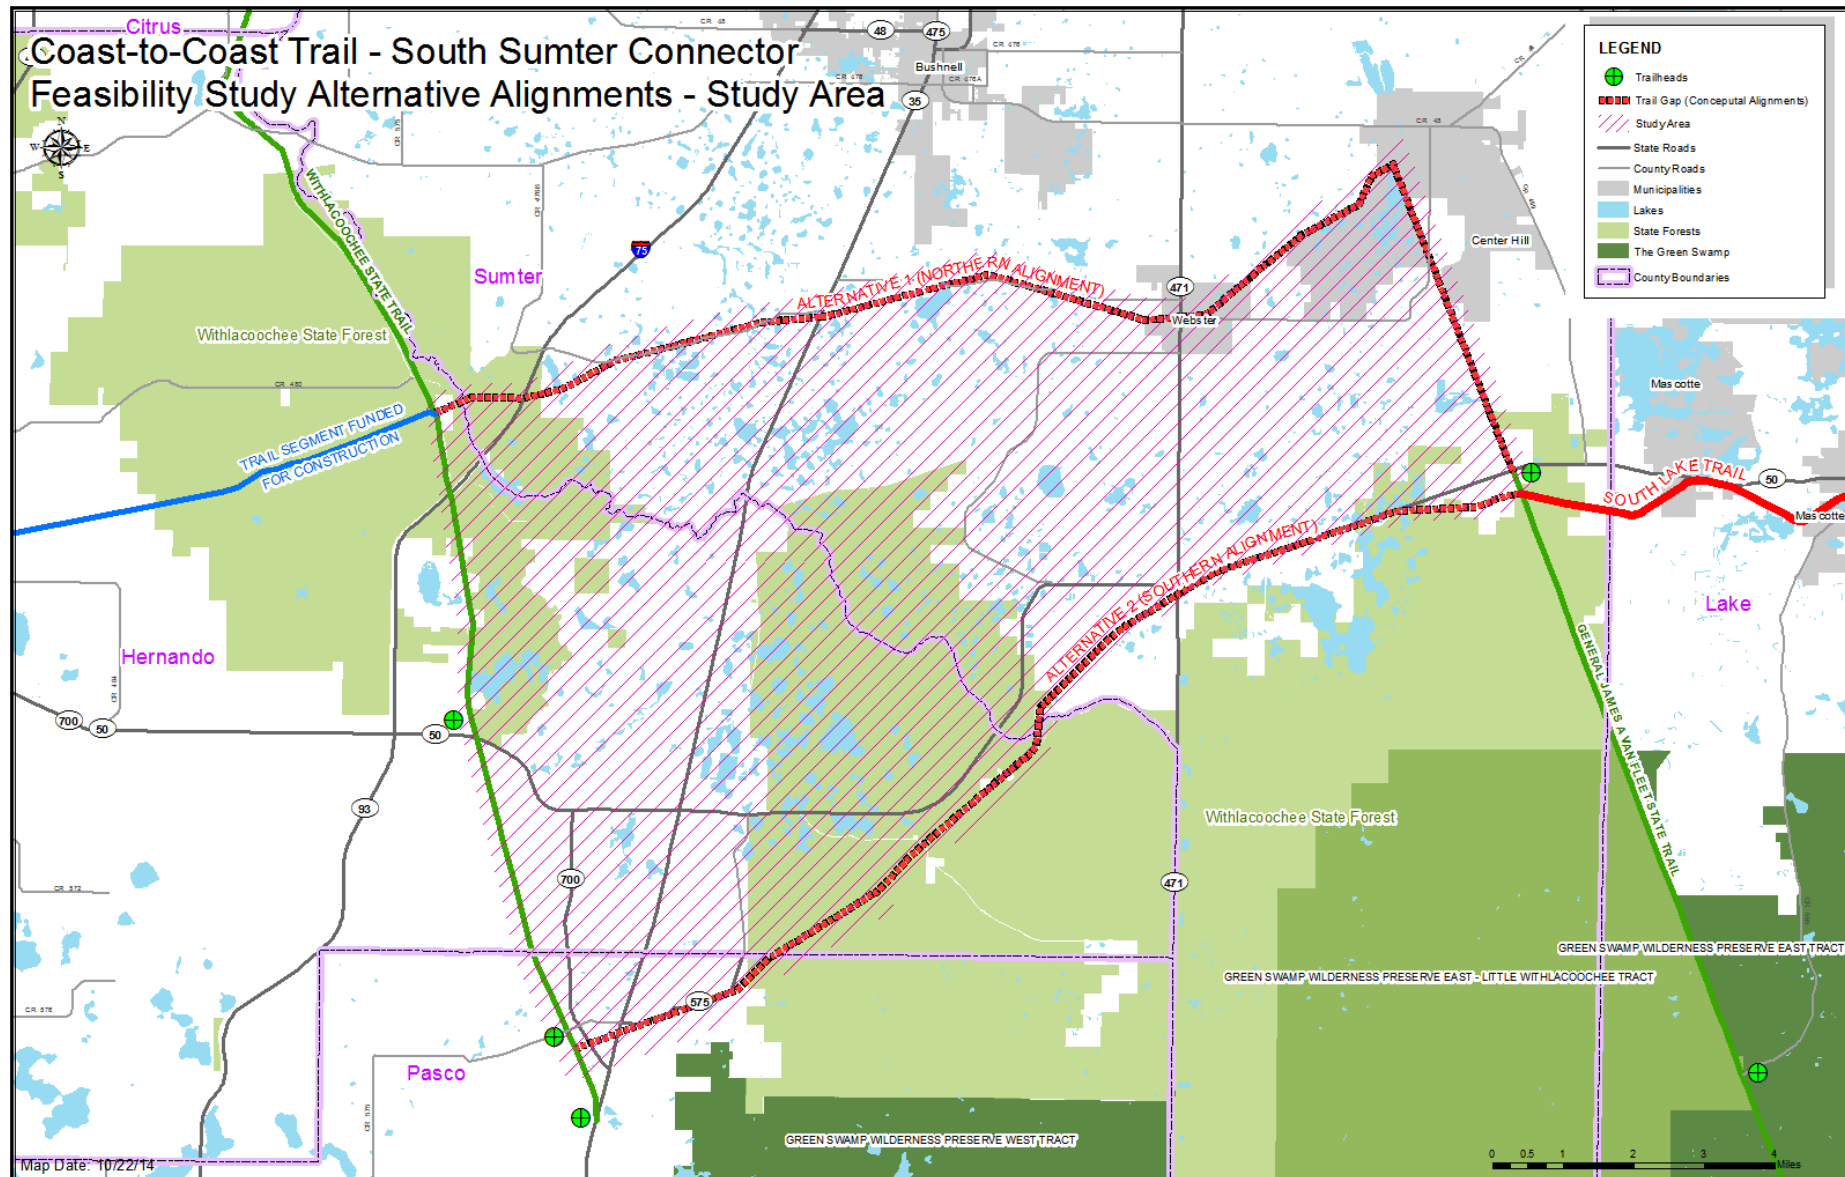


South Sumter Connector Trail PD&E Study

- South Sumter Connector Trail Planning Study
 - FM: 435471-1-12-01
 - PM: Heather Garcia
 - To be completed in June 2016
 - **www.cflroads.com** and search: South Sumter Connector Trail




C.R. 514 & Interchange PD&E Study

- 435476-1-22-01
- From 0.5 miles west of I-75 to US-301
- Sumter county
- Approximately \$2,000,000 contract
- Advertising December 2016/January 2017
- PM: Jazlyn Heywood, P.E.
- Recommended TRC: Amy Sirmans, Brian Stanger, Bill Walsh

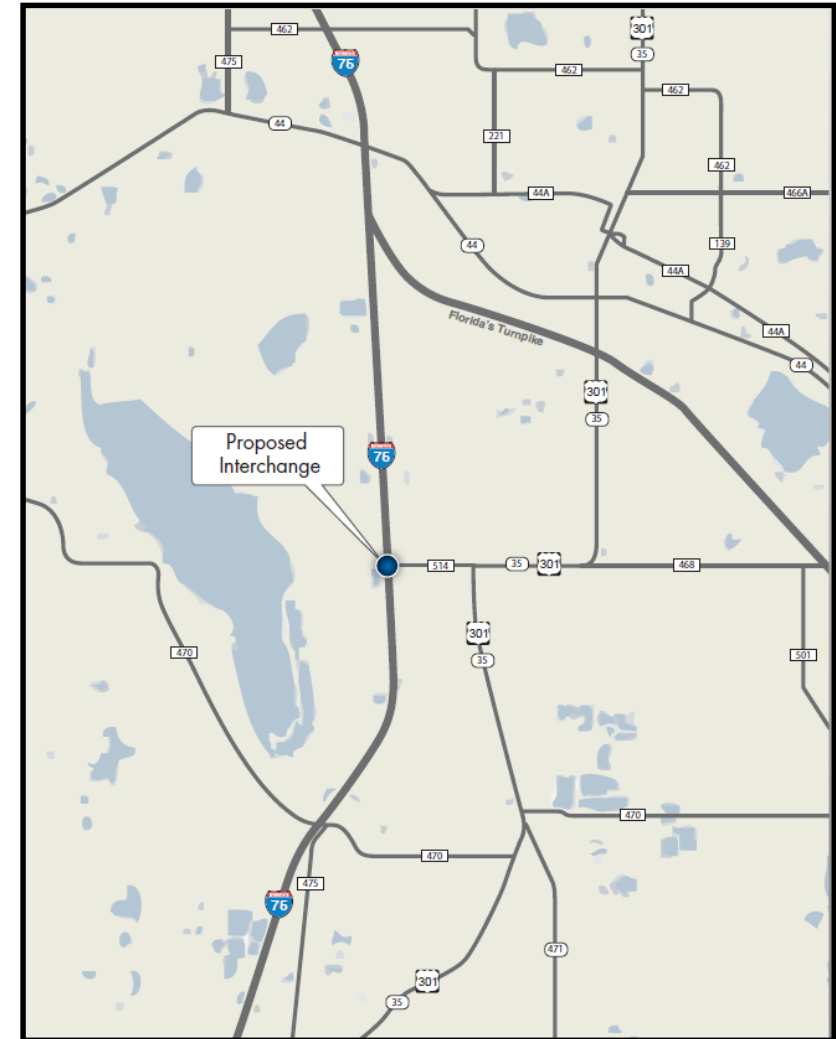

Other projects:

- C-470 PD&E (FDOT)
- US-301 PD&E (FDOT)
- I-75 D/B (FDOT)
- CR-501 Study (County)
- C-468 Widening (County)
- New C-468 / Turnpike Interchange (County)

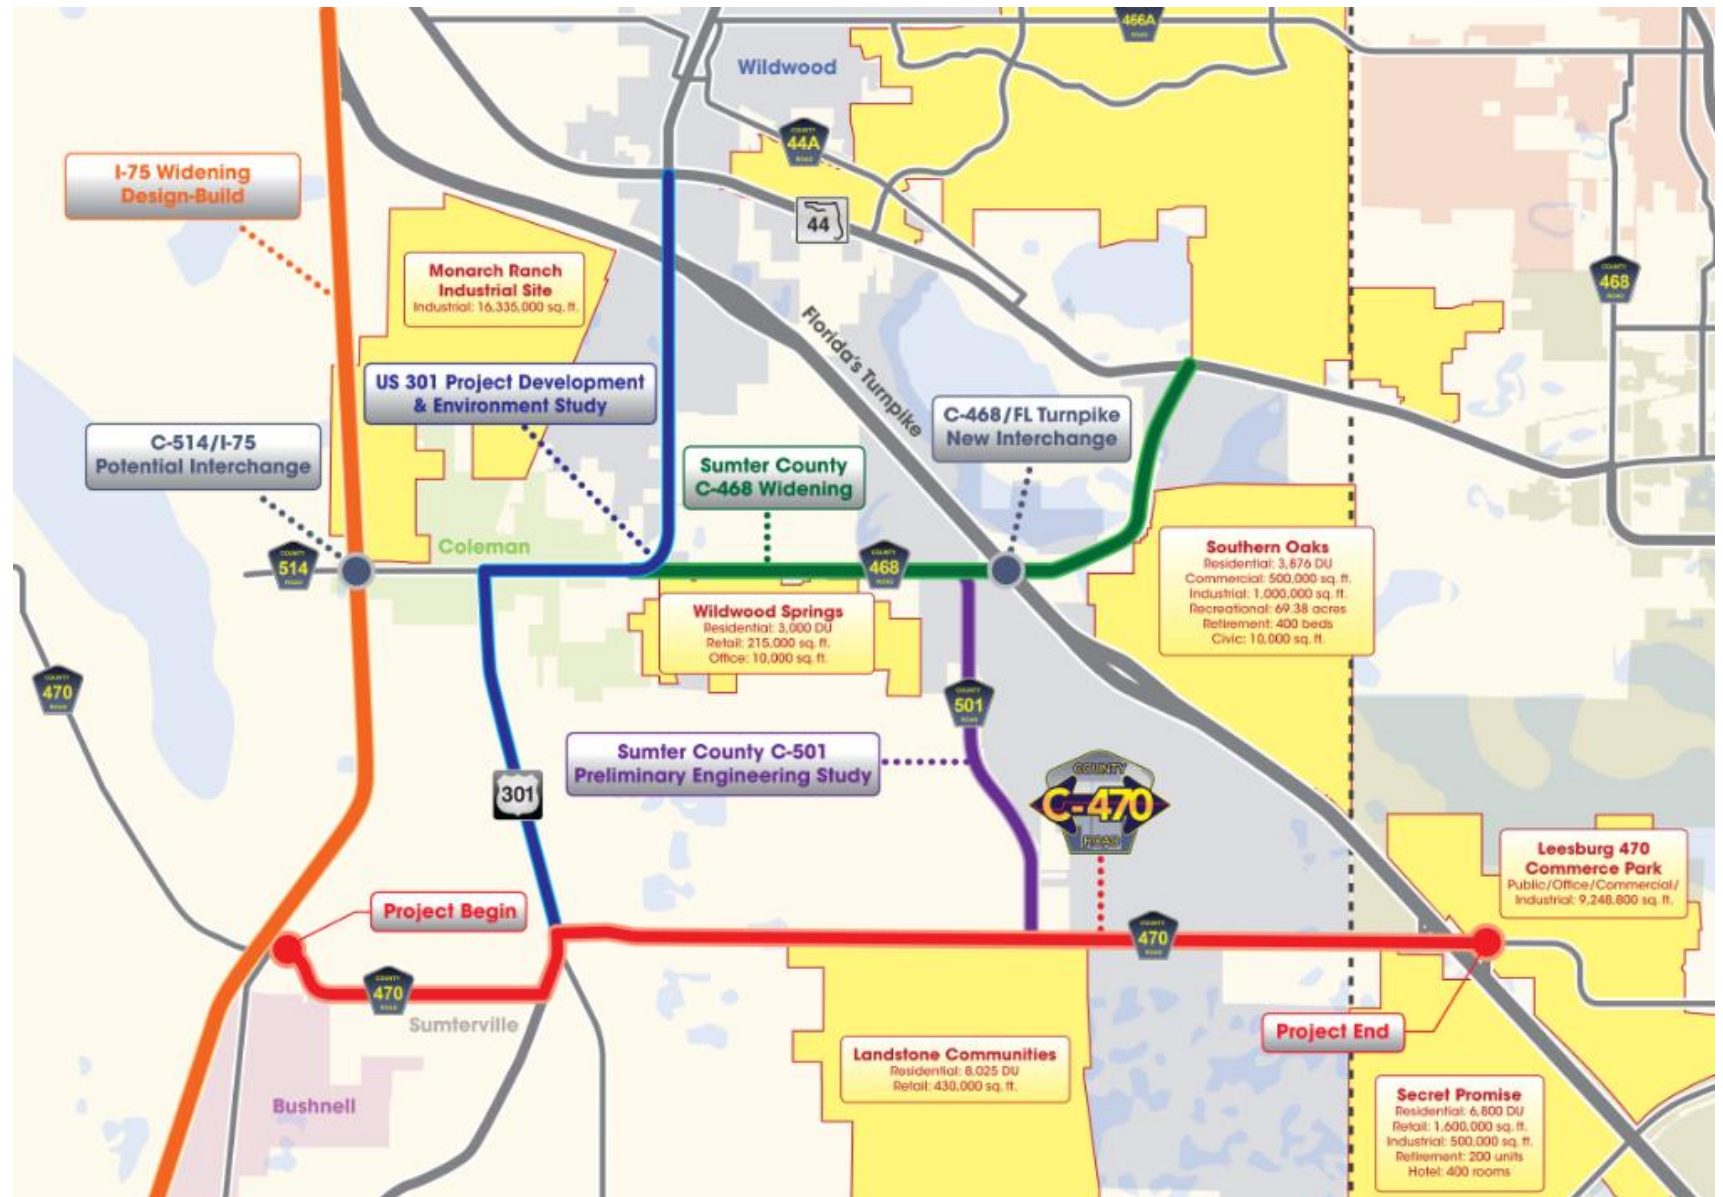

Planned Industrial Sites:

- Monarch Ranch Mega-Site
- Wade Industrial
- Pike 75 Logistics Center
- Mid-Florida Distribution Center



C.R. 514 & Interchange PD&E Study

- IJR underway
 - MLOU approved March 2014
 - Preliminary IJR under revisions
- ETDM Programming Screen
 - Began August 12, 2015
 - ETAT comments received
 - P&N needs revision

Draft

Interstate 75 and CR 514

Interchange Justification Report

Sumter County, FL

Prepared For:

Florida Department of Transportation, District Five

September 2015



Florida Department of Transportation

CAP
FDOT-D5

January 26, 2016

Design Traffic Contracts

- 405859-1-12-06 & -07
- One advertisement with two contracts awarded
- Maximum 5 year contract
- Planned Advertisement December 2016/January 2017
- PM: Jason Learned
- Recommended TRC: TBD



Design Traffic Contracts

- Scope of Contract:
 - Major tasks include:
 - ✓ Preparation of Project Traffic Reports for PD&E and Design
 - ✓ Completion of Equivalent Service Axle Load studies (ESALs)
 - ✓ Data collection associated with Project Traffic and ESAL studies, support to the Efficient Transportation Decision Making (ETDM) process, as well as transit-pedestrian safety projects



Design Traffic Contracts

- Scope of Contract:
 - Minor tasks include:
 - ✓ Access management
 - ✓ Crash and planning safety analysis
 - ✓ Feasibility studies
 - ✓ Policy development
 - ✓ Traffic database support





Right of Way

Continuing Services Contract

Right of Way Services

Jack Adkins, District R/W Manager

Mike McPhail, Deputy R/W Manager, Valuation Services

Jeff Marlowe, Deputy R/W Manager, Operations

Debbie Lynch, Deputy R/W Manager, Production

Right of Way Contract

- **Financial Project No. : 2410681-42-03**
- **Districtwide**
- **Includes but not limited to Acquisition, Appraisal, Relocation, Suit Preparation, Project Management, Property Management, Business Damage Review and Records Management**
- **5 year contract**
- **\$5,000,000 Cap**
- **Advertising Summer 2016**
- **PM: Jack Adkins**
- **Recommended TRC Members:**
Jeff Marlowe; Mike McPhail; Debbie Lynch





A Regional Transportation Solution

Industry Forum

January 26, 2016

1:30 – 5:00

