

**FLORIDA'S TURNPIKE ENTERPRISE  
CONSULTANT ACQUISITION PLAN (CAP)  
FY 2017  
VIRTUAL FORUM  
March 18, 2016**



- Opening Remarks – Mike Shannon, P.E.
- Continuing Services Contracts – Kathy Alexander
- Phase 22 (PD&E) – Rax Jung, P.E.
- Phase 32 (DESIGN) – Paul Satchfield
- Phase 62 Construction Consultant (CEI) – Karen Akers, P.E.
- PSU Consultant Acquisition Best Practices – Rich Nethercote
- Project Information Meetings, Technical Panel Sessions, and Marketing Opportunities – Paul Satchfield
- CAP, Advertisement and Work Program Map – Brianna Miller
- Question Review – Brianna Miller



# Continuing Services/Miscellaneous Design Services Contracts



Ad #	Description	Project Type	Contract Amount & Length	PM	Formal Advertisement
17814	LANDSCAPING DESIGN SERVICES	D/W Specialty	\$5M/5YR	Paul Satchfield	3/14/16 Under Acquisition
17815	ERCAR DEVELOPMENT (2 Awards)	CONT SRVCS BDI	\$1.5M/5YR	Paul Satchfield	4/11/16
17816	DESIGN BUILD RFP DEVELOPMENT (2 Awards)	CONT SRVCS	\$5M/5YR	Paul Satchfield	4/18/16
17817	INTELLIGENT TRANSPORTATION SYSTEM (ITS)	CONT SRVCS	\$5M/5YR	John Easterling	4/25/16
17818	MISCELLANEOUS DESIGN SERVICES (2 Awards)	MISC DESIGN BDI	\$1.5M/3YR	Paul Satchfield	5/2/16
17819	SURVEY AND GEOTECH (2 Awards)	D/W Specialty	\$5M/5YR	Mike Joiner Ken Morgan	4/8/16
17831	ARCHITECT	D/W Specialty	\$5M/5YR	Paul Satchfield	6/6/16 Tentative

ESTIMATED TOTAL CONTINUING/MISCELLANEOUS SERVICES CONTRACTS \$ 41 M

17832	ENGINEERING CONTRACT ADMINISTRATION AND MGMT	GEC	\$71.1M	Michael Shannon	5/23/16
-------	--	-----	---------	-----------------	---------



# Phase 22 (PD&E)




Ad No	FPID	BDI Y/N?	DESCRIPTION	TYPE	EST CONTRACT AMT	COUNTY	PM	FORMAL AD DATE
17810	437371-1	N	ALTERNATIVE CORRIDOR EVALUATION (ACE) CONSULTANT ACQUISITION	PD&E	\$2M	STATEWIDE	Becky Bolan	1/25/2016 Under Acquisition
17801	423374-1	N	PD&E MAINLINE WIDENING JUPITER TO FT PIERCE (MP 116 to 152)	PD&E	\$3.6M	MARTIN / ST. LUCIE	Brian Ribaric	5/2/2016
17803	437206-1	N	HEFT US1 EXIT RAMP MODIFICATION LOOP RAMP TO THE NW (MP 0)	PD&E	\$2M	MIAMI-DADE	Brian Ribaric	10/3/2016

ESTIMATED TOTAL PHASE 22 CONTRACTS \$7.6M



# PHASE 22

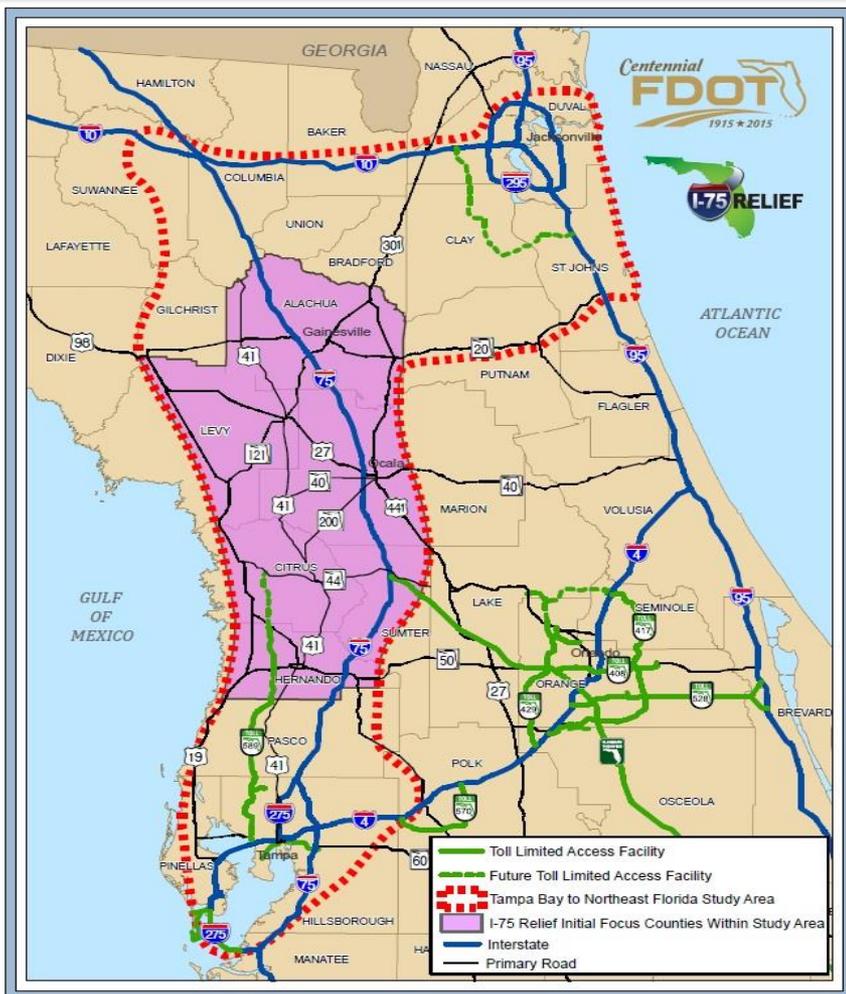

PM	Becky Bolan, P.E.
FPID(S)	437371-1 (Under Acquisition)
County/COUNTIES	Hernando, Citrus, Sumter, Marion, Levy, Alachua and possibly additional counties
Estimated Contract Amount	\$2M
Estimated Contract Start Date	September 2016
Estimated Length of Contract	TBD
BDI	No

Major/Minor Work Types Anticipated	2.0, 3.3 / 4.1.1, 4.1.2, 4.2.1, 4.2.2, 4.2.3, 6.3.1, 6.3.2, 7.1, 7.2, 7.3, 8.1, 8.2, 8.3, 8.4, 9.1, 9.2, 9.4.1, 14.0, 15.0
------------------------------------	--

*Project Description:*

**I-75 RELIEF PROJECT**



# PHASE 22




PM	<b>Brian Ribaric, P.E.</b>
FPID(S)	423374-1
County/Counties	Palm Beach, Martin and St. Lucie
Estimated Contract Amount	\$3.6M
Estimated Contract Start Date	February 2017
Estimated Length of Contract	30 Months
BDI	No

<b>Major/Minor Work Types Anticipated</b>	<b>2.2 / 3.3, 4.1.1, 4.1.2, 4.2.1, 4.2.2, 6.3.1, 6.3.2, 6.3.3, 7.1, 7.2, 7.3, 8.1, 8.2, 8.3, 8.4, 9.1, 9.2, 9.4.1, 14.0, 15.0</b>
---	---

***Project Description:***

***PD&E WIDEN MAINLINE FROM JUPITER TO FT PIERCE (MP 116 TO MP 152)***

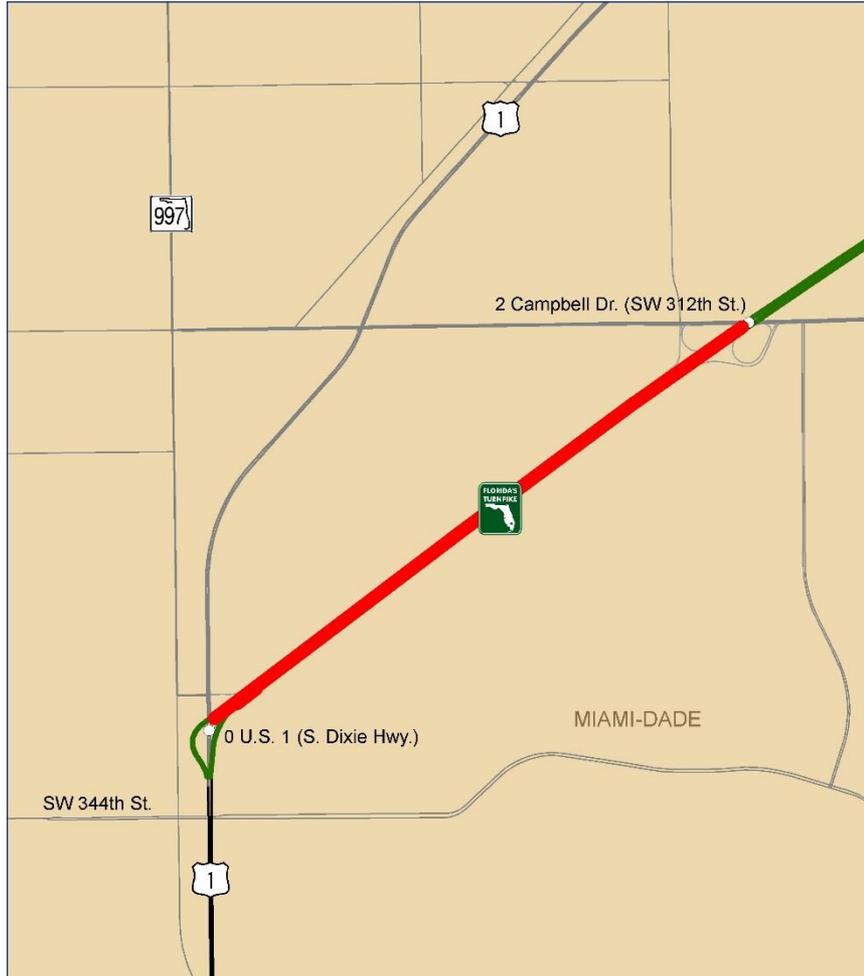

PM	<b>Brian Ribaric, P.E.</b>
FPID(S)	437206-1
County/Counties	Miami-Dade
Estimated Contract Amount	\$2M
Estimated Contract Start Date	May 2017
Estimated Length of Contract	24 Months
BDI	No

<b>Major/Minor Work Types Anticipated</b>	<b>2.2, 3.3 /</b> 4.1.1, 4.1.2, 4.2.1, 4.2.2, 6.3.1, 6.3.2, 6.3.3, 7.1, 7.2, 7.3, 8.1, 8.2, 8.3, 8.4, 9.1, 9.2, 9.4.1, 14.0, 15.0
---	---

***Project Description:***

***HEFT US 1 EXIT RAMP MODIFICATION LOOP RAMP TO THE NW (MP 0)***



# Phase 32 (DESIGN)



AD NO.	FPID	BDI Y/N?	DESCRIPTION	TYPE	EST CONTRACT AMT	COUNTY	PM	FORMAL AD DATE
17807	436517-1	Y	RESURFACE TPK MAINLINE IN ST. LUCIE COUNTY, MP 153.23-169.32	DESIGN	\$1.4M	ST LUCIE	Steve Soldati	2/22/2016 Under Acquisition LOI Due Date 3/7/16
17809	415748-1 436521-1	N	WIDEN TPK FROM SR710 (MP 106.1) TO MP 117 (4 TO 8 LNS) RESURFACE TPK MAINLINE IN PALM BEACH COUNTY FROM MP 106.1 TO 111.7	DESIGN	\$8.9M	PALM BEACH	Josh Pedersen	8/8/2016
17802	438547-1	N	ORLANDO SOUTH ULTIMATE INTERCHANGE IMPROVEMENTS	DESIGN	\$2.0M	ORANGE	Pam Nagot	7/25/2016
17808	436520-1	Y	RESURFACE POLK PKWY, MP 0.00 - 8.00	DESIGN	\$1.1M	POLK	Steve Soldati	4/4/2016
17811	437988-1	Y	RESURFACE MAINLINE LAKE COUNTY MP 287.761 TO 288.748 (NB AND SB) AND 288.748 TO 297.870 (NB ONLY)	DESIGN	\$0.7M	LAKE	DeAnne Hinson	5/2/2016
17812	437992-1	N	RESURFACE MAINLINE MARTIN COUNTY (MP 117.8 TO 138.10)	DESIGN	\$1.5M	MARTIN	Marcus Lisicki	8/15/2016
17830	435461-1	N	WIDEN SAWGRASS- N OF ATLANTIC TO SR 7 (MP8-18)(6TO10 LNS) (W EXP LNS)	DESIGN	\$11.0M	BROWARD	Tom Neyer	8/29/2016
*17804	437952-1	N	WIDEN SEMINOLE XWAY, SR434 TO N OF CR427 (MP44-49.4) (4TO8 LNS W EXP)	DESIGN	\$12.0M	SEMINOLE	Snehal Ambare	9/26/16 Tentative
*17806	435786-1	N	WIDEN TPK- MINNEOLA INTCHG TO LEESBURG NORTH INTCHG (MP 279 - 289.3)	DESIGN	\$9.1M	LAKE	DeAnne Hinson	8/22/2016

\* Consultant selection in FY17, contract execution expected in early FY18

ESTIMATED TOTAL PHASE 32 CONTRACTS \$47.7M



# PHASE 32



PM	Steve Soldati, P.E.
FPID(S)	436517-1 (Under Acquisition)
County/Counties	St. Lucie
Estimated Contract Amount	\$1.4M
Estimated Contract Execution	November 2016
Letting	December 2017
BDI	Yes

Major/Minor Work Types Anticipated	3.3 / 4.1.1, 4.1.2, 7.1, 8.2, 9.1, 9.2
------------------------------------	--

**Project Description:**  
*RESURFACE MAINLINE FROM MP 153.23 TO MP 169.32 (ST. LUCIE COUNTY)*



PM	Josh Pedersen, P.E.
FPID(S)	415748-1 & 436521-1
County/Counties	Palm Beach
Estimated Contract Amount	\$8.9M
Estimated Contract Execution	April 2017
Letting	2022+
BDI	No

Major/Minor Work Types Anticipated	3.3 / 2.0, 3.1, 3.2, 4.1.1, 6.2, 6.3.1, 7.1, 7.2, 9.2, 14
------------------------------------	---


**Project Description:**

*MAINLINE WIDENING FROM SR 710/MP 106.1 TO MP 117 (4 TO 8 LANES)*

*RESURFACE MAINLINE FROM MP 106.1 TO MP 111.7 (PALM BEACH COUNTY)*



# PHASE 32

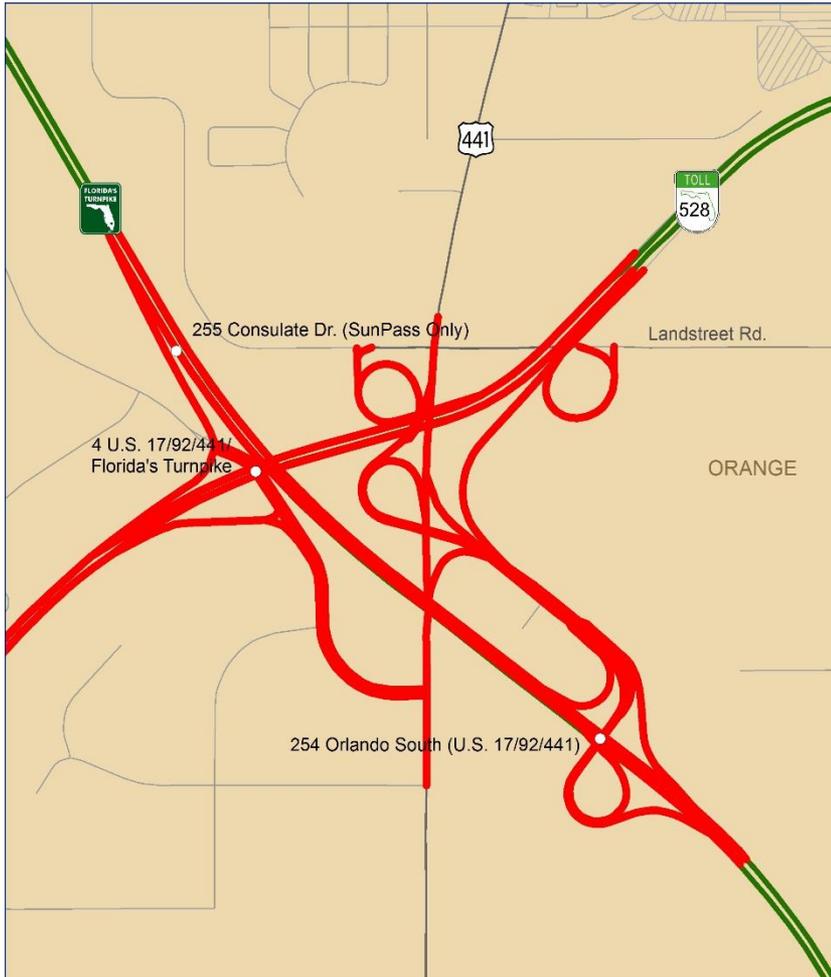


PM	Pam Nagot, P.E.
FPID(S)	438547-1
County/Counties	Orange
Estimated Contract Amount	\$2.0M
Estimated Contract Execution	July 2017
Letting	2022+
BDI	No

Major/Minor Work Types Anticipated	3.3 / 2.0, 4.1.1, 4.1.2, 6.3.1, 6.3.2, 6.3.3, 7.1, 7.2, 7.3, 8.1, 8.2, 8.4, 9.1, 9.2, 9.4, 14.0, 15.0
------------------------------------	---

**Project Description:**

**ORLANDO SOUTH ULTIMATE INTERCHANGE AT SR528/MP 4 AND SR 91/MP 254**

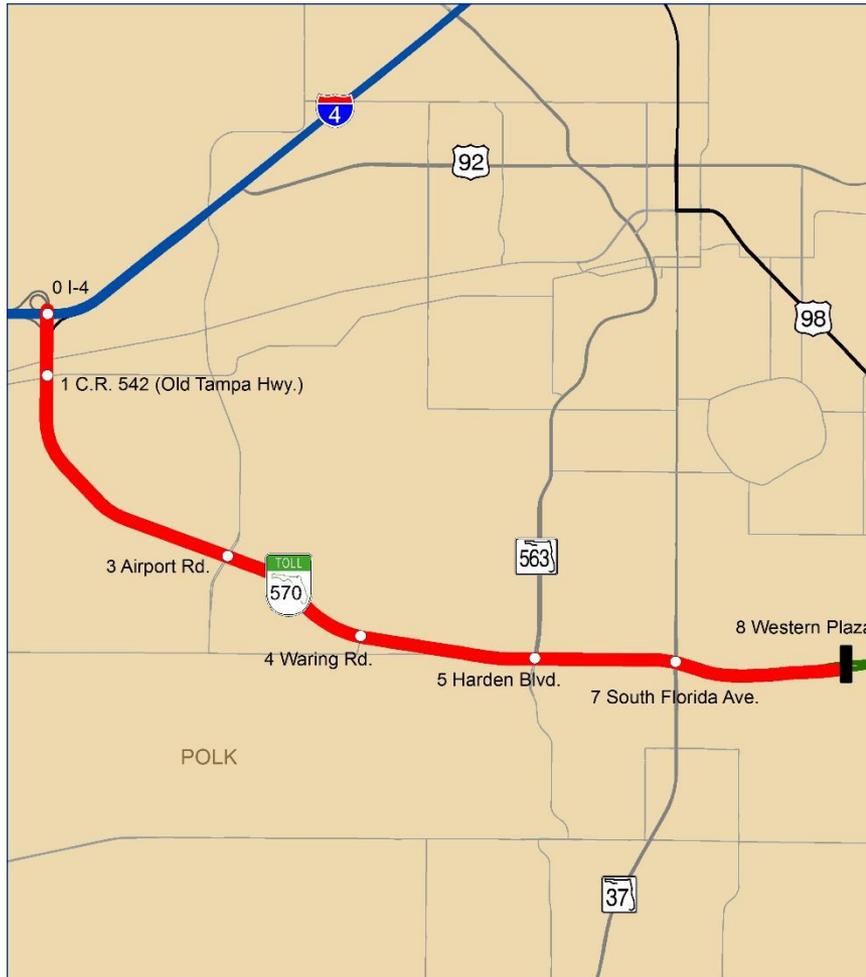


PM	Steve Soldati, P.E.
FPID(S)	436520-1
County/Counties	Polk
Estimated Contract Amount	\$1.1M
Estimated Contract Execution	January 2017
Letting	January 2018
BDI	Yes

Major/Minor Work Types Anticipated	3.3 / 4.1.1, 4.1.2, 7.1, 7.2, 7.3, 8.1, 8.2, 9.1, 9.2
------------------------------------	---

**Project Description:**

RESURFACE POLK PARKWAY, MP 0 TO MP 8 (POLK COUNTY)

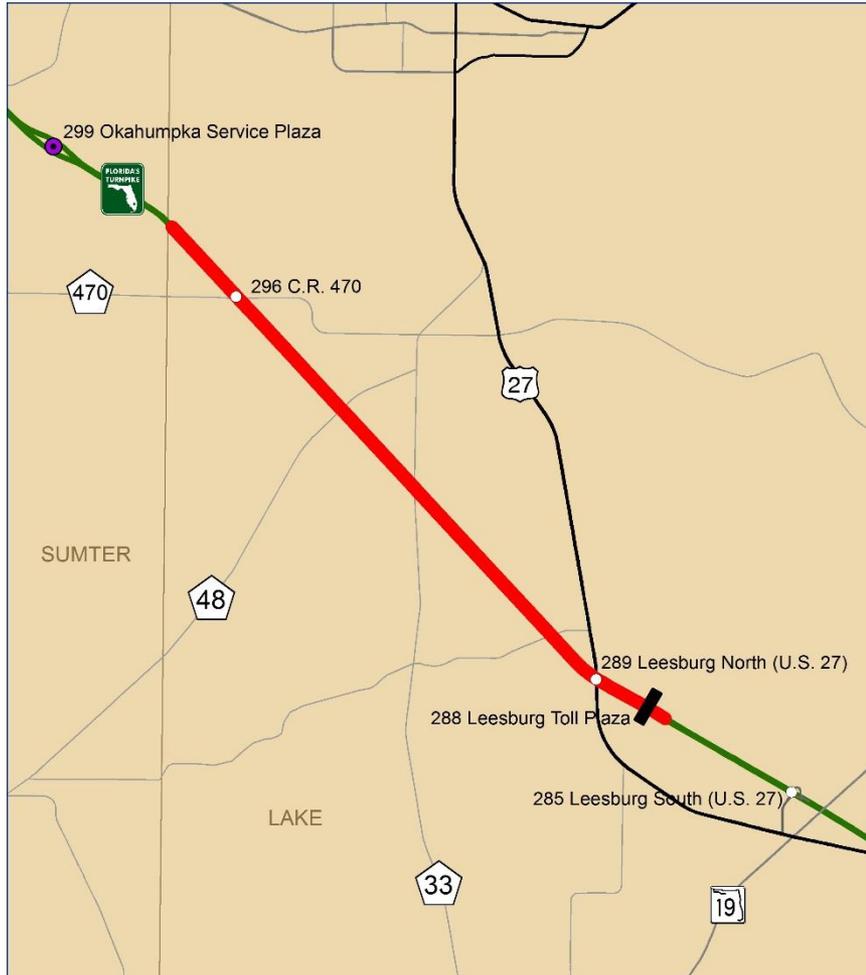

PM	DeAnne Hinson, P.E.
FPID(S)	437988-1
County/Counties	Lake
Estimated Contract Amount	\$0.7M
Estimated Contract Execution	December 2016
Letting	November 2017
BDI	No

Major/Minor Work Types Anticipated	3.3 / 3.1, 4.1.1, 7.1
------------------------------------	-----------------------

**Project Description:**

RESURFACE MAINLINE, MP 287.761 TO MP 288.748 NORTHBOUND AND SOUTHBOUND AND MP 288.748 TO MP 297.87 NORTHBOUND (LAKE COUNTY)



PM	Marcus Lisicki, P.E.
FPID(S)	437992-1
County/Counties	Martin
Estimated Contract Amount	\$1.5M
Estimated Contract Execution	April 2017
Letting	April 2018
BDI	No

Major/Minor Work Types Anticipated	3.3 / 3.1, 4.1.1, 4.2.2, 7.1
------------------------------------	------------------------------

**Project Description:**

*RESURFACE MAINLINE, MP 117.843 TO MP 138.037 (MARTIN COUNTY)*



# PHASE 32



PM	Tom Neyer, P.E.
FPID(S)	435461-1
County/Counties	Broward
Estimated Contract Amount	\$11.0M
Estimated Contract Execution	February 2017
Letting Date	March 2020
BDI	No

Major/Minor Work Types Anticipated	3.3 / 4.1, 4.2, 6.1, 6.2, 6.3, 7.1, 7.2, 7.3, 8.1, 8.2, 8.3, 8.4, 9.1, 9.2, 9.4, 9.5, 14.0, 15.0
------------------------------------	--

**Project Description:**

*WIDEN SAWGRASS EXPRESSWAY NORTH OF ATLANTIC TO SR 7 (MP 8 TO MP 18) (6 TO 10 LANES WITH EXPRESS LANES)*



# PHASE 32




PM	Snehal Ambare, P.E.
FPID(S)	437952-1
County/Counties	Seminole
Estimated Contract Amount	\$12.0M
Estimated Contract Execution	July 2017
Letting	July 2022
BDI	No

Major/Minor Work Types Anticipated	3.3 / 2.0, 3.1, 3.2, 4.1.1, 4.1.2, 6.1, 6.2, 6.3.1, 6.3.2, 6.3.3, 7.1, 7.2, 7.3, 8.1, 8.2, 8.3, 8.4, 9.1, 9.2, 9.4.1, 14.0, 15.0
------------------------------------	--

**Project Description:**

*WIDEN SEMINOLE EXPRESSWAY SR 434 TO NORTH OF CR 427 (MP 44 TO MP 49.4) (4 TO 8 LANES WITH EXPRESS LANES)*

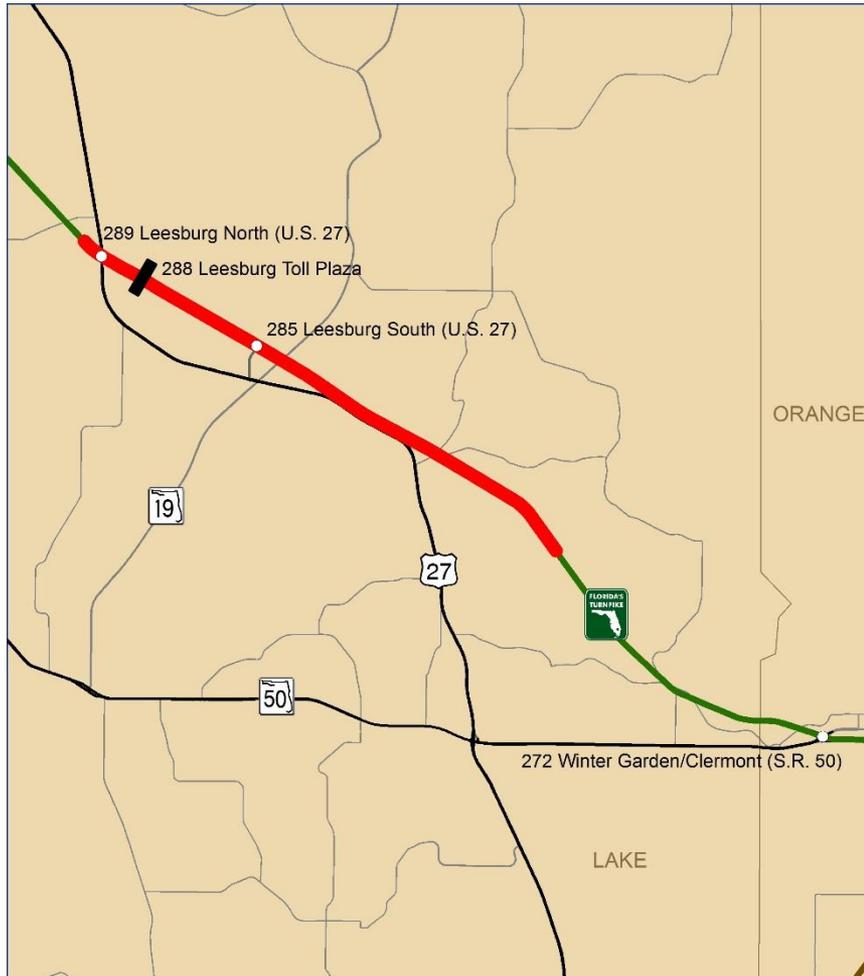

PM	DeAnne Hinson, P.E.
FPID(S)	435786-1
County/Counties	Lake
Estimated Contract Amount	\$9.1M
Estimated Contract Execution	July 2017
Letting	2022+
BDI	No

Major/Minor Work Types Anticipated	3.3 / 3.1, 3.2, 4.1.1, 4.1.2, 6.2, 6.3.1, 7.1, 7.2, 7.3, 8.1, 8.2, 8.4, 9.1, 9.2, 9.3, 9.4.1, 14.0, 15.0
------------------------------------	--

**Project Description:**

**WIDEN MAINLINE MINNEOLA INTERCHANGE TO LEESBURG NORTH (MP 279 TO MP 289.3)**

FPID	BDI Y/N?	DESCRIPTION	EST CONTRACT AMOUNT	COUNTY	PM	FORMAL AD DATE
417545-1	N	WIDEN SEMINOLE XWAY FROM ALOMA AVE TO SR 434 (MP 38 - 44) (4TO8 LANES)	\$128M	SEMINOLE	Snehal Ambare	11/9/2016 Under Acquisition
435543-1	N	WIDEN HEFT FROM SR836 TO NW 106TH ST (MP26-33) (6/8 LNS TO 10 INC EXP)	\$177M	MIAMI DADE	Scott Kamien	10/27/2016 Tentative

ESTIMATED TOTAL DESIGN BUILD CONTRACTS \$305M



PM	Snehal Ambare, P.E.
FPID(S)	417545-1 (Under Acquisition)
County/Counties	Seminole/Orange
Estimated Contract Amount	\$128M
Estimated Contract Execution	August 2016
Letting	August 2016
BDI	No
<b>Major/Minor Work Types Anticipated</b>	<b>3.3 / 3.2, 4.1.1, 5.4, 6.3.1, 6.3.2, 6.3.3, 7.1, 7.2, 7.3, 8.1, 8.2, 9.1, 9.2, 9.4.1, 9.4.2, 14.0, 15.0</b>

**Project Description:**

**WIDEN SEMINOLE EXPRESSWAY ALOMA AVENUE TO SR 434 (MP 38 TO MP 44) (4 TO 8 LANES WITH EXPRESS LANES)**



PM	Scott Kamien, P.E.
FPID(S)	435543-1
County/COUNTIES	Miami-Dade
Estimated Contract Amount	\$177M
Estimated Contract Execution	August 2017
Letting	May 2017
BDI	No
<b>Major/Minor Work Types Anticipated</b>	<b>3.3 / 3.2, 4.1, 4.2, 4.3, 5.4, 6.1, 6.2, 6.3, 7.1, 7.2, 7.3, 8.1, 8.2, 8.3, 9.1, 9.2, 9.3, 9.4, 9.5, 14 and 15.</b>

**Project Description:**

*WIDEN HEFT FROM SR 836 TO NW 106TH STREET (MP 26 TO MP 33) (6/8 TO 10 LANES WITH EXPRESS LANES)*




# Construction Engineering and Inspection (CEI) – Phase 62



AD NO	FPID	BDI (Y / N)	DESCRIPTION	COUNTY	EST CONTRACT AMT	PM	FORMAL AD DATE
17821	437156-2	Y	ORLANDO SOUTH INTERCHANGE INTERIM IMPROVEMENTS (MP 4)	ORANGE	\$952K	Todd Kelly	4/19/2016
17823	437300-1	N	FLORIDA POLYTECH -CENTER OF EXCELLENCE- TEST FACILITY	POLK	\$2.6M	Todd Kelly	10/17/2016
17824	435165-1 435165-3 435167-1 435167-3 435166-1 435166-3 435168-1 435168-3	N	RESURFACE OF TPK MAINLINE FROM MP181.1 TO MP185.0 (OKEECHOBEE COUNTY) RESURFACE OF TPK MAINLINE FROM MP188.5 TO MP190.5 (INDIAN RIVER CNTY)	OKEECHOBEE INDIAN RIVER	\$1.6M	Todd Kelly	10/17/2016
17825	435608-1	Y	POLK PARKWAY TRUSS CANTILEVER & POST SIGN PANEL REPLACEMENTS (MP 8-21)	POLK HILLSBOROUGH PASCO HERNANDO	\$597K	Todd Kelly	11/28/2016
17826	435169-1 435169-3	N	RESURFACE OF TPK MAINLINE FROM MP 207.00 TO 220.076 (OSCEOLA COUNTY)	OSCEOLA	\$849K	Jon Ford	1/2/2017
17820	411406-1 411406-4	N	WIDEN TPK FROM OSCEOLA CNTY LINE TO BEACHLINE, W/EXP LANES (4TO8 LNS)	ORANGE OSCEOLA	\$13.28M	Jon Ford	5/9/2016
17822	435406-1	Y	PAINT BRIDGES AT TPK SPUR (870701,870702)	MIAMI-DADE	\$824K	Roxanne Riggs	7/11/2016
17827	429339-1	N	AET PHASE 5A, TPK MAINLINE, I-595 TO S OF LANTANA TOLLPLAZA,MP54-88	BROWARD PALM BEACH	\$1.7M	Ken Hudson	1/30/2017
17828	435171-1 435171-3 435172-1 435172-3	N	RESURFACE TPK MAINLINE (MP92.53-102.47 NB&SB) & (MP90.06-90.30 NB ONLY) RESURFACE OF TPK MAINLINE FROM MP 103.70 TO 106.11 (PALM BEACH COUNTY)	PALM BEACH	\$1.69M	Jaime Gomez	2/6/2017
17829	435543-1	N	WIDEN HEFT FROM SR836 TO NW 106TH ST (MP26-33) (6/8 LNS TO 10 INC EXP)	MIAMI-DADE	\$17.7M	Pacifico Castillo	2/13/2017

ESTIMATED TOTAL CEI CONTRACTS AMOUNT \$41.7M

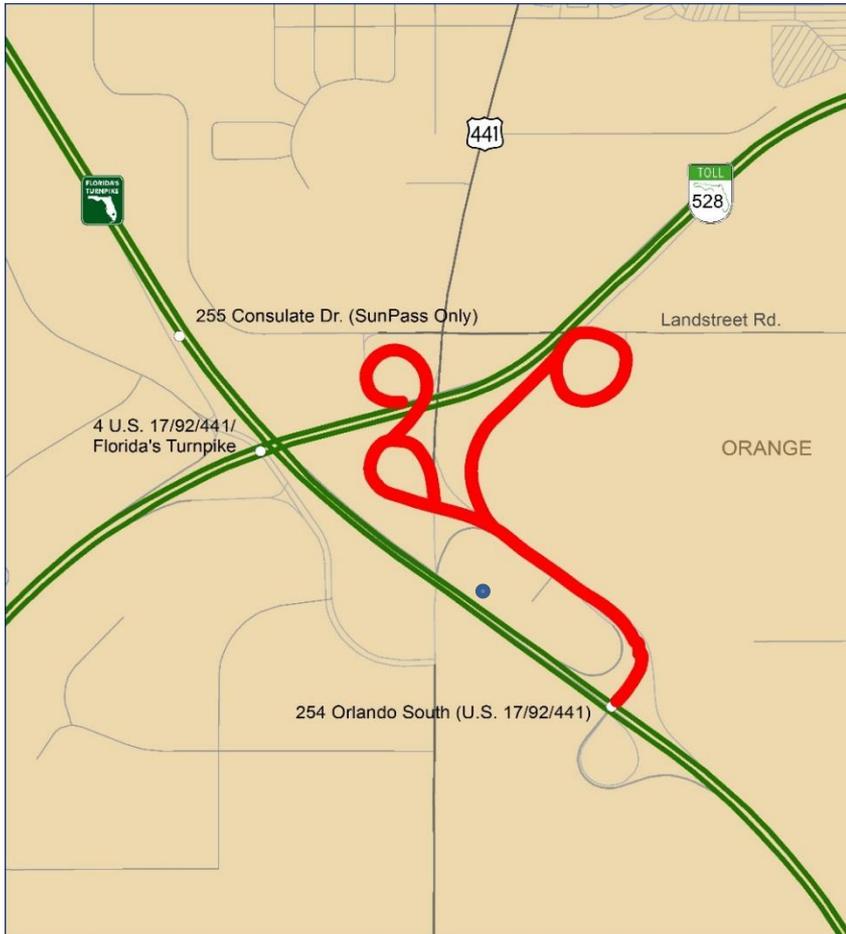


PM	Todd Kelly, P.E.
FPID(S)	437156-2
County/Counties	Orange
Estimated CEI Contract Amount	\$952K
Estimated CEI Contract Start Date	October 2016
Estimated Length of CEI Contract	18 Months
BDI	Yes

Major/Minor Work Types Anticipated	10.1 / 8.2
------------------------------------	------------

**Project Description:**

*ORLANDO SOUTH INTERIM INTERCHANGE, RESURFACE RAMPS AND ADD LANE WITH NEW BRIDGE (MP 254)*

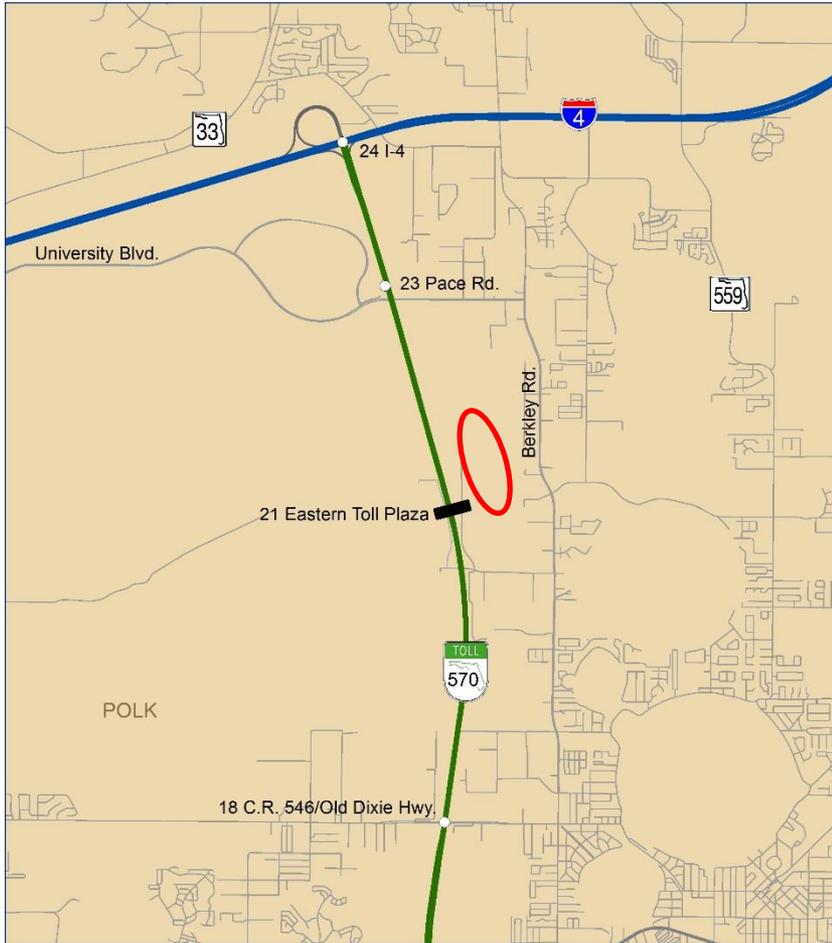


PM	<b>Todd Kelly, P.E.</b>
FPID(S)	437300-1
County/Counties	Polk
Estimated CEI Contract Amount	\$2.6M
Estimated CEI Contract Start Date	March 2017
Estimated Length of CEI Contract	18 Months
BDI	No

<b>Major/Minor Work Types Anticipated</b>	<b>10.1 / 8.2</b>
---	-------------------

*Project Description:*

**FLORIDA POLYTECH -CENTER OF EXCELLENCE- TEST FACILITY**

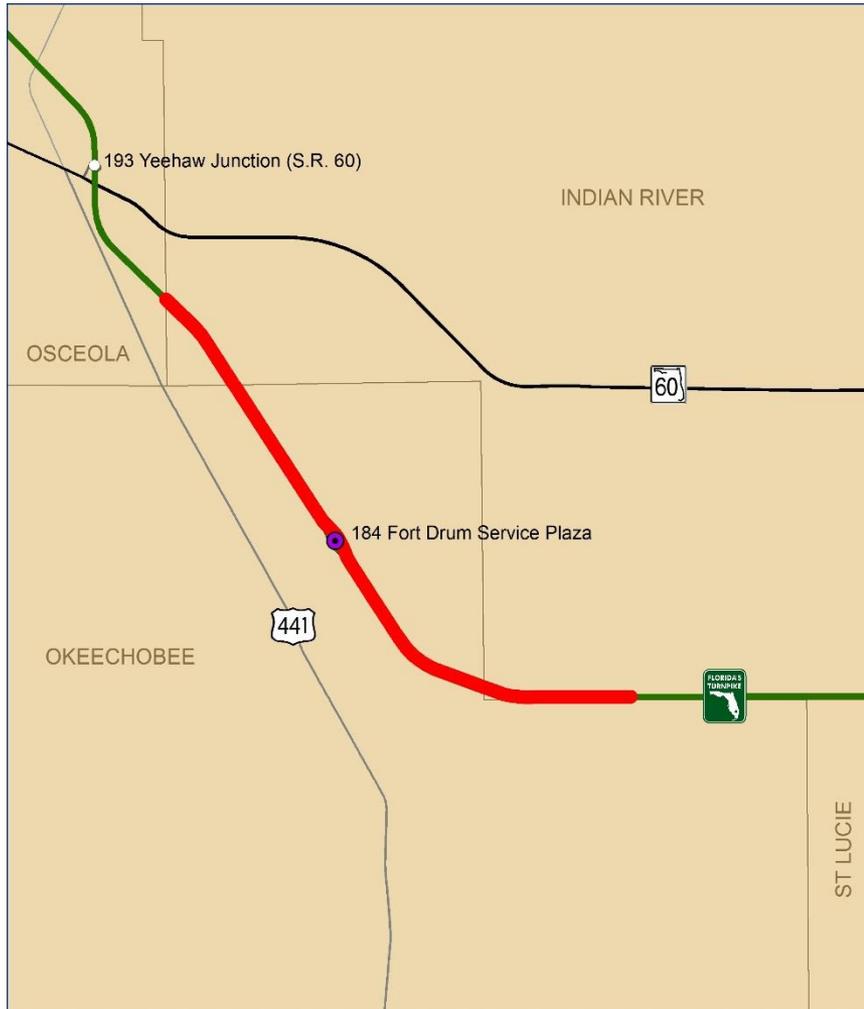

PM	<b>Todd Kelly, P.E.</b>
FPID(S)	435165-1/3, 435166-1/3 435167-1/3, 435168-1/3
County/Counties	Okeechobee and Indian River
Estimated CEI Contract Amount	\$1.6M
Estimated CEI Contract Start Date	April 2017
Estimated Length of CEI Contract	11 Months
BDI	No
<b>Major/Minor Work Types Anticipated</b>	<b>10.1 / 8.2</b>

**Project Description:**  
*RESURFACE MAINLINE FROM MP 181.1 TO MP 185.0 (OKEECHOBEE COUNTY) / ROADSIDE IMPROVEMENT FOR MAINLINE FROM MP 181.1 TO MP 185.0*  
*RESURFACE OF MAINLINE FROM MP 185.0 TO MP 188.5 (OKEECHOBEE COUNTY) / ROADSIDE IMPROVEMENT FOR MAINLINE FROM MP 185.0 TO MP 188.5*  
*RESURFACE OF MAINLINE FROM MP 178.3 TO MP 181.1 (INDIAN RIVER COUNTY) / ROADSIDE IMPROVEMENT FOR MAINLINE FROM MP 178.3 TO MP 181.1*  
*RESURFACE OF MAINLINE FROM MP 188.5 TO MP 190.5 (INDIAN RIVER COUNTY) / ROADSIDE IMPROVEMENT FOR MAINLINE FROM MP 188.5 TO MP 190.5*




PM	<b>Todd Kelly, P.E.</b>
FPID(S)	435608-1 & 438420-1
County/Counties	Polk, Hillsborough, Pasco, Hernando
Estimated CEI Contract Amount	\$597K
Estimated CEI Contract Start Date	June 2017
Estimated Length of CEI Contract	10 Months
BDI	Yes

<b>Major/Minor Work Types Anticipated</b>	<b>10.1</b>
---	-------------

***Project Description:***

*POLK PARKWAY TRUSS CANTILEVER AND POST SIGN PANEL REPLACEMENTS (MP 8 TO MP 21)*

*SUNCOAST PARKWAY SIGN REPLACEMENT (MP 14 TO MP 55)*

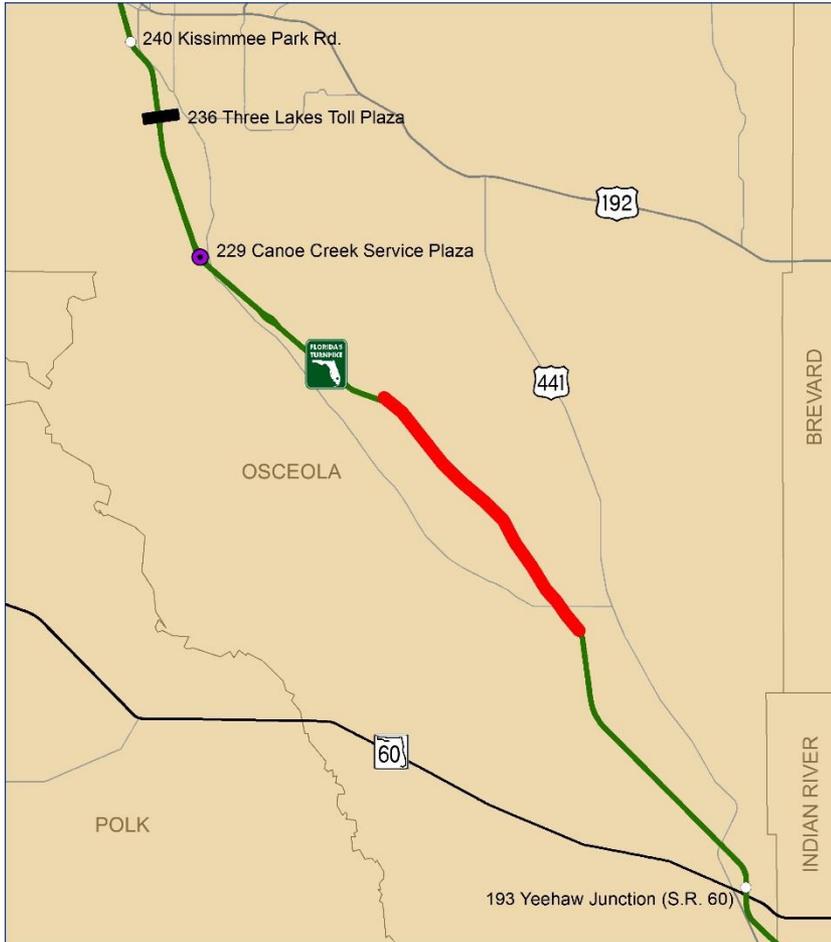


PM	Jon Ford
FPID(S)	435169-1/3
County/Counties	Osceola
Estimated CEI Contract Amount	\$849K
Estimated CEI Contract Start Date	July 2017
Estimated Length of CEI Contract	11 Months
BDI	No

Major/Minor Work Types Anticipated	10.1 / 8.2
------------------------------------	------------

**Project Description:**

*RESURFACE MAINLINE FROM MP 207.00 TO MP 220.076 (OSCEOLA COUNTY)*

*ROADSIDE IMPROVEMENTS FOR MAINLINE FROM MP 207.00 TO MP 220.076*

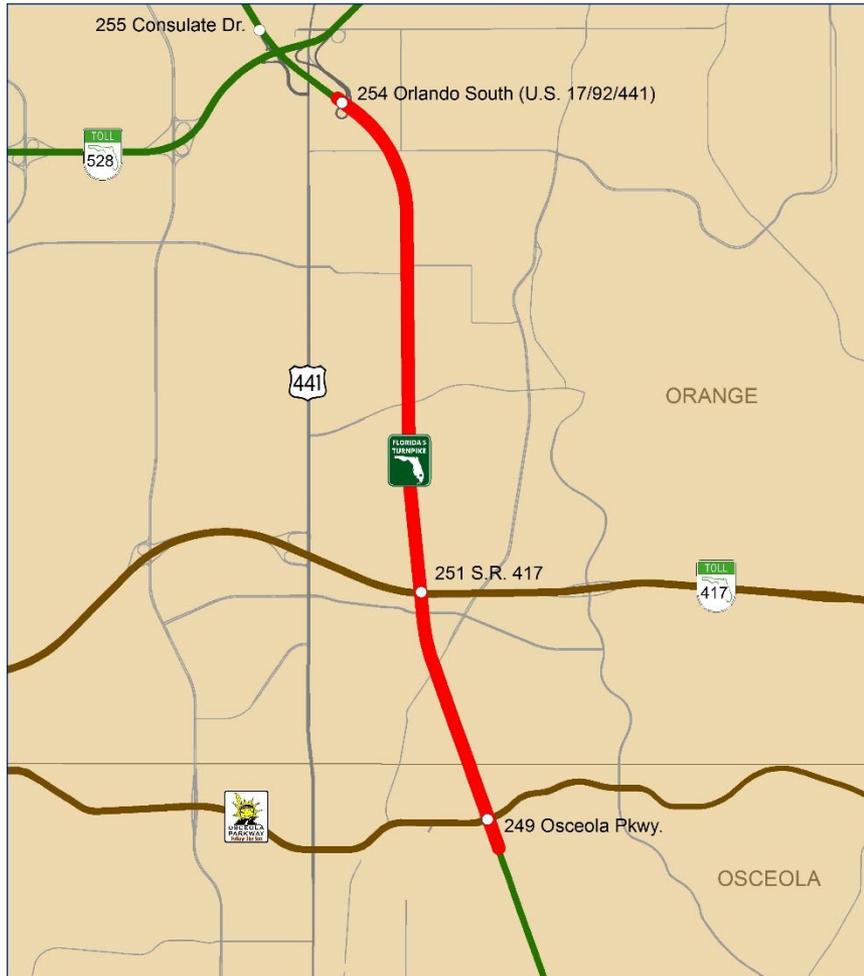


PM	Jon Ford
FPID(S)	411406-1/4
County/Counties	Orange and Osceola
Estimated CEI Contract Amount	\$13.28M
Estimated CEI Contract Start Date	October 2016
Estimated Length of CEI Contract	51 Months
BDI	No

Major/Minor Work Types Anticipated	10.1 / 8.2
------------------------------------	------------

**Project Description:**

*WIDEN MAINLINE FROM OSCEOLA COUNTY LINE TO BEACHLINE EXPRESSWAY (4 TO 8 LANES WITH EXPRESS LANES)*

*WIDEN MAINLINE FROM SOUTH OF OSCEOLA PARKWAY TO OSCEOLA COUNTY LINE (4 TO 8 LANES WITH EXPRESS LANES)  
MP 248.5 TO MP 249.3*

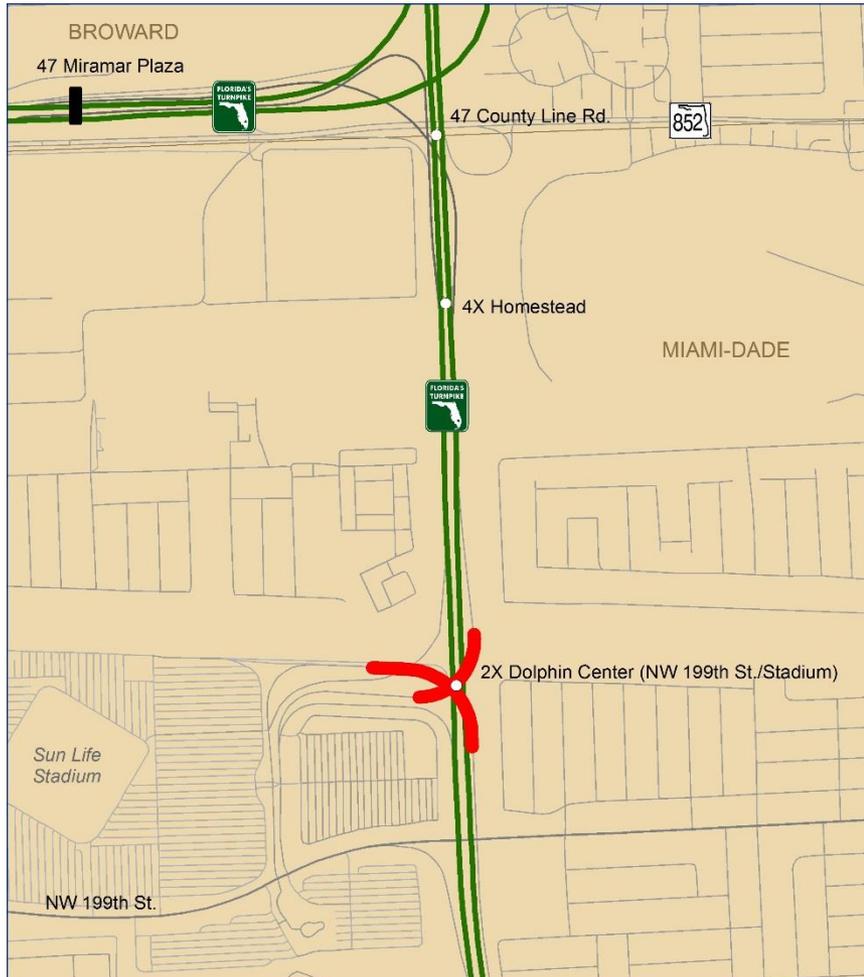

PM	Roxanne Riggs, P.E.
FPID(S)	435406-1
County/Counties	Miami-Dade
Estimated CEI Contract Amount	\$824K
Estimated CEI Contract Start Date	December 2016
Estimated Length of CEI Contract	20 Months
BDI	Yes

Major/Minor Work Types Anticipated	10.1
------------------------------------	------

*Project Description:*

**PAINT BRIDGES AT MAINLINE SPUR (870701, 870702)**



PM	Ken Hudson
FPID(S)	429339-1
County/Counties	Broward and Palm Beach
Estimated CEI Contract Amount	\$1.7M
Estimated CEI Contract Start Date	July 2017
Estimated Length of CEI Contract	16 Months
BDI	No

Major/Minor Work Types Anticipated	10.1 / 8.2
------------------------------------	------------

**Project Description:**

*ALL ELECTRONIC TOLLING (AET) PHASE 5A, MAINLINE, I-595 TO SOUTH OF LANTANA TOLLPLAZA, MP 54 TO MP 88*



PM	Jaime Gomez, P.E.
FPID(S)	435171-1/3 & 435172-1/3
County/Counties	Palm Beach
Estimated CEI Contract Amount	\$1.69M
Estimated CEI Contract Start Date	July 2017
Estimated Length of CEI Contract	12 Months
BDI	No

Major/Minor Work Types Anticipated	10.1 / 8.2
------------------------------------	------------

**Project Description:**

*RESURFACE MAINLINE MP 92.53 TO 102.47 (NB & SB) AND MP 90.06 TO MP 90.30 (NB ONLY) (PALM BEACH COUNTY) / ROADSIDE IMPROVEMENT FOR MAINLINE FROM MP 92.53 TO MP 102.47*

*RESURFACE MAINLINE MP 103.70 TO MP 106.11 (PALM BEACH COUNTY) / ROADSIDE IMPROVEMENT FOR MAINLINE FROM MP 103.70 TO MP 106.11*



PM	Pacifico Castillo, P.E.
FPID(S)	435543-1
County/Counties	Miami-Dade
Estimated CEI Contract Amount	\$17.7M
Estimated CEI Contract Start Date	July 2017
Estimated Length of CEI Contract	51 Months
BDI	No

Major/Minor Work Types Anticipated	10.1 / 8.2
------------------------------------	------------

**Project Description:**

WIDEN HEFT FROM SR 836 TO NW 106TH STREET, MP 26 TO MP 33 (6/8 LANES TO 10 LANES WITH EXPRESS LANES)



## Professional Services Unit – Best Practices/Tips



1. Prime Consultant and all sub consultants must provide resumes and payroll registers for all personnel listed on the AFP; in addition to any required forms.
2. Prime Consultant should make sure that all personnel listed on the AFP are listed in the proper job classification in accordance with the Negotiations Handbook.
3. Team personnel that are either a P.E. or E.I.T must provide their license number or certificate number and the date credentials were issued.
4. Fee sheets should support the items listed on the loaded tab of the AFP.
5. Self-certification form for all non-technical firms or non-professional services firms must be provided.
6. Prime Consultant shall request 2 quotes and utilize the lowest rates for non-technical or non-professional firms proposing, i.e., pipe video, equipment rates, court reporters, corrosion inspection and testing, aerial photography, and maintenance of traffic, etc.
7. Prime Consultant should QA/QC all sub consultants AFP's and audit their package to ensure all required information is submitted prior to submitting to Professional Services Unit



# Miscellaneous Project/Contract Information



## Design Project/Contract Information

Technical Panel Sessions - These are typically scheduled on project specific contract acquisitions and are announced on the Planned Advertisement. They are individual 30 minute sessions between interested Consultant(s) and the Technical Review Committee members, Project Manager, and requested Florida Turnpike Enterprise technical staff. These sessions are not intended for marketing and are not considered during selection. The expectation is that project related technical questions will be asked of the staff requested.

General Information Meetings – These are typically scheduled for District Wide/Non Project specific contracts and are also announced on the Planned Advertisement. They are an open forum type meeting for interested Consultants where a brief presentation is provided by FTE staff, followed by Q &A's with the Technical Review Committee members, Project Manager and Procurement staff.

## Production/Design/EMO Consultant Marketing Meetings

These are held monthly at TPK Headquarters, typically on the second Monday. They are for Consultant Firms to present to Florida Turnpike Enterprise staff. Contact Linda Beverly to schedule - 407-264-3647 or email [linda.beverly@dot.state.fl.us](mailto:linda.beverly@dot.state.fl.us)

**CEI – Marketing Meetings** – A day will be set aside with 30 minutes per firm for the marketing meetings. The construction project manager and the Technical Review Committee members will be in attendance. The day will be noticed in the planned advertisement with instructions on scheduling these optional marketing meetings.



## Miscellaneous Project/Contract Information (Continued)



### Public Information Requests for ALL Procurements

#### PRIOR to Formal Advertisement

Stephanie Maldonado (407) 264-3171

[Stephanie.Maldonado@dot.state.fl.us](mailto:Stephanie.Maldonado@dot.state.fl.us)

#### POST Formal Advertisement

Professional Services Unit

Direct Contact information can be found on the  
advertisement



## WEB LINKS



FDOT: Procurement - Marketing – CAP

<http://www.dot.state.fl.us/procurement/CAP.shtm>

FDOT: Procurement – Advertisements

<http://www.dot.state.fl.us/procurement/Advertisements.shtm>

GIS - Geographic Information Systems - Work Program Maps

<http://fdot.maps.arcgis.com/apps/OnePane/basicviewer/index.html?appid=71d5dbe101874d8ebef391a1cf94d962>

FTE's Design Website

<http://design.floridasturnpike.com/index.html>

FTE's Marketing Website

<http://www.dot.state.fl.us/procurement/marketingTP/>



## QUESTIONS AND ANSWERS

### Turnpike Program Management Staff

- Mike Shannon, P.E. – Director of Transportation Development
- Paul Satchfield – District Program Management Administrator
- Kathy Alexander – District Program Administration Manager  
[katherine.alexander@dot.state.fl.us](mailto:katherine.alexander@dot.state.fl.us)
- Karen Akers, P.E. – CEI Manager
- Brianna Miller – Production Manager  
[brianna.miller@dot.state.fl.us](mailto:brianna.miller@dot.state.fl.us)

### Professional Services Unit

- Rich Nethercote – Professional Services/Design Build Contract Manager

1. New firms seeking to work for the Turnpike Enterprise organization have difficulty being selected. Can the Turnpike Enterprise offer these firms an orientation so that they can understand what is necessary to get through the threshold?

*As mentioned in the previous slides, in the last 12 months we have brought on 5 new consultants out of the 24 consultant selections.*

*As Paul discussed take advantage of the consultant presentation meetings on the 2<sup>nd</sup> Monday of each month.*

*Other suggestions would be to work hard, provide quality work, debrief win or lose, implement the suggestions and then don't give up.*

2. Will a copy of the audio be available

*Yes, the PPT and recording of the presentation are available at this location:*

*<http://www.dot.state.fl.us/procurement/marketingTP/>*

3. Will the two continuing services contracts for geotech and surveying include both, or will one be surveying and another geotech?

*Yes, these will be two separate Continuing Services Contracts including both Geotech and Survey. Each will be for 5 years / \$5 Million. One advertisement, two awards.*
